



ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
1			GRM	63,2 days	Fri 04-09-26	Fri 04-12-26		54%
2			PAP 1	1 day	Fri 04-09-26	Fri 04-09-26		100%
3			Pase Producción	1 day	Fri 04-09-26	Fri 04-09-26		100%
4			Fase de Garantía	5 days	Fri 04-09-26	Thu 10-09-26		94%
5			Atenciones de Incidencias PAP	5 days	Fri 04-09-26	Thu 10-09-26		94%
6			Desarrollo	4 days	Mon 07-09-26	Thu 10-09-26	3	100%
7			Pruebas Internas	4 days	Mon 07-09-26	Thu 10-09-26	3	100%
8			Entrega y despliegue en QA	4 days	Mon 07-09-26	Thu 10-09-26	3	90%
9			Ejecucion de pruebas	4 days	Mon 07-09-26	Thu 10-09-26	3	90%
10			Reuniones de Revisión UAT	4 days	Mon 07-09-26	Thu 10-09-26	3	90%
11			HU Postergadas Fase Garantía	58,2 days	Fri 11-09-26	Fri 04-12-26		50%
12			1 Caso Gobierno OK con OBS	8 days	Fri 11-09-26	Wed 23-09-26		100%
13			OK con OBS: G_12_ RI_49.2	8 days	Fri 11-09-26	Wed 23-09-26		100%
14			Medición de Esfuerzo	0 days	Fri 11-09-26	Fri 11-09-26	10	100%
15			Análisis, Revision y Aprobacion	0 days	Fri 11-09-26	Fri 11-09-26	10	100%
16			Desarrollo	1 day	Fri 11-09-26	Mon 14-09-26	10	100%
17			Pruebas Internas	1 day	Mon 14-09-26	Tue 15-09-26	15	100%
18			Entrega y despliegue en QA	1 day	Wed 16-09-26	Thu 17-09-26	17	100%
19			Induccion de HU	1 day	Wed 16-09-26	Thu 17-09-26	17	100%
20			Ejecucion de pruebas ciclo 1	1 day	Wed 16-09-26	Thu 17-09-26	17	100%
21			Reuniones de Revisión UAT	1 day	Wed 16-09-26	Thu 17-09-26	17	100%
22			Correcciones y despliegue	1 day	Mon 21-09-26	Tue 22-09-26	21	100%
23			Ejecucion de pruebas ciclo 2	1 day	Wed 23-09-26	Wed 23-09-26	22	100%

Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
24			2 Casos Documentación OK con OBS	7 days	Fri 11-09-26	Tue 22-09-26		100%
25			OK con OBS: 1.1, 4.1	7 days	Fri 11-09-26	Tue 22-09-26		100%
26			Medición de Esfuerzo	0 days	Fri 11-09-26	Fri 11-09-26	10	100%
27			Análisis, Revision y Aprobacion	1 day	Fri 11-09-26	Fri 11-09-26	10	100%
28			Desarrollo	2 days	Mon 14-09-26	Tue 15-09-26	27	100%
29			Pruebas Internas	1 day	Wed 16-09-26	Wed 16-09-26	28	100%
30			Entrega y despliegue en QA	1 day	Thu 17-09-26	Thu 17-09-26	29	100%
31			Induccion de HU	1 day	Thu 17-09-26	Thu 17-09-26	29	100%
32			Ejecucion de pruebas ciclo 1	1 day	Thu 17-09-26	Thu 17-09-26	29	100%
33			Reuniones de Revisión UAT	1 day	Thu 17-09-26	Thu 17-09-26	29	100%
34			Correcciones y despliegue	1 day	Mon 21-09-26	Mon 21-09-26	30	100%
35			Ejecucion de pruebas ciclo 2	1 day	Tue 22-09-26	Tue 22-09-26	34	100%
36			3 Casos Incidencias OK con OBS	9,5 days	Fri 11-09-26	Fri 25-09-26		100%
37			OK con OBS: 5.3, 7.1, 9.3	9,5 days	Fri 11-09-26	Fri 25-09-26		100%
38			Medición de Esfuerzo	1 day	Fri 11-09-26	Fri 11-09-26		100%
39			Análisis, Revision y Aprobacion	1 day	Fri 11-09-26	Fri 11-09-26		100%
40			Desarrollo	2 days	Mon 14-09-26	Tue 15-09-26	39	100%
41			Pruebas Internas	1 day	Tue 15-09-26	Tue 15-09-26	40	100%
42			Entrega y despliegue en QA	1 day	Wed 16-09-26	Wed 16-09-26	41	100%
43			Induccion de HU	1 day	Wed 16-09-26	Wed 16-09-26	41	100%
44			Ejecucion de pruebas ciclo 1	1 day	Thu 17-09-26	Thu 17-09-26	43	100%
45			Reuniones de Revisión UAT	1 day	Mon 21-09-26	Mon 21-09-26	44	100%
46			Correcciones y despliegue	2,5 days	Tue 22-09-26	Thu 24-09-26	45	100%

Project: msproj11
Date: Wed 30-09-26



Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
47			Ejecucion de pruebas ciclo 2	1 day	Thu 24-09-26	Fri 25-09-26	46	100%
48			3 Casos Filiales OK con OBS	9 days	Fri 11-09-26	Thu 24-09-26		100%
49			OK con OBS: 2.1, 10.2, 11.2	9 days	Fri 11-09-26	Thu 24-09-26		100%
50			Medición de Esfuerzo	1 day	Fri 11-09-26	Fri 11-09-26		100%
51			Análisis, Revision y Aprobacion	1 day	Mon 14-09-26	Mon 14-09-26	50	100%
52			Desarrollo	2 days	Mon 14-09-26	Tue 15-09-26	50	100%
53			Pruebas Internas	1 day	Wed 16-09-26	Wed 16-09-26	52	100%
54			Entrega y despliegue en QA	1 day	Thu 17-09-26	Thu 17-09-26	53	100%
55			Induccion de HU	1 day	Thu 17-09-26	Thu 17-09-26	53	100%
56			Ejecucion de pruebas ciclo 1	1 day	Mon 21-09-26	Mon 21-09-26	55	100%
57			Reuniones de Revisión UAT	1 day	Tue 22-09-26	Tue 22-09-26	56	100%
58			Correcciones y despliegue	1 day	Wed 23-09-26	Wed 23-09-26	57	100%
59			Ejecucion de pruebas ciclo 2	1 day	Thu 24-09-26	Thu 24-09-26	58	100%
60			4 Casos Información inventario - OK con OBS	6 days	Tue 22-09-26	Tue 29-09-26		100%
61			OK con OBS: 10.2,13.2 (8.3N/A, 11.1N/A)	6 days	Tue 22-09-26	Tue 29-09-26		100%
62			Medición de Esfuerzo	1 day	Tue 22-09-26	Tue 22-09-26	58	100%
63			Análisis, Revision y Aprobacion	1 day	Tue 22-09-26	Tue 22-09-26	58	100%
64			Desarrollo	2 days	Wed 23-09-26	Thu 24-09-26	63	100%
65			Pruebas Internas	1 day	Wed 23-09-26	Wed 23-09-26	63	100%
66			Entrega y despliegue en QA	1 day	Fri 25-09-26	Fri 25-09-26	64	100%
67			Induccion de HU	1 day	Fri 25-09-26	Fri 25-09-26	64	100%

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
68			Ejecucion de pruebas ciclo 1	1 day	Fri 25-09-26	Fri 25-09-26	64	100%
69			Reuniones de Revisión UAT	1 day	Fri 25-09-26	Fri 25-09-26	64	100%
70			Correcciones y despliegue	1 day	Mon 28-09-26	Mon 28-09-26	69	100%
71			Ejecucion de pruebas ciclo 2	1 day	Tue 29-09-26	Tue 29-09-26	70	100%
72			14 Casos Validación- OK con OBS	10 days	Mon 21-09-26	Fri 02-10-26		100%
73			OK con OBS: 30.1, 36.1	10 days	Mon 21-09-26	Fri 02-10-26		100%
74			Medición de Esfuerzo	1 day	Mon 21-09-26	Mon 21-09-26		100%
75			Análisis, Revision y Aprobacion	1 day	Mon 21-09-26	Mon 21-09-26		100%
76			Desarrollo	2 days	Tue 22-09-26	Wed 23-09-26	75	100%
77			Pruebas Internas	1 day	Thu 24-09-26	Thu 24-09-26	76	100%
78			Entrega y despliegue en QA	1 day	Fri 25-09-26	Fri 25-09-26	77	100%
79			Induccion de HU	1 day	Fri 25-09-26	Fri 25-09-26	77	100%
80			Ejecucion de pruebas ciclo 1	1 day	Mon 28-09-26	Mon 28-09-26	79	100%
81			Reuniones de Revisión UAT	1 day	Tue 29-09-26	Tue 29-09-26	80	100%
82			Correcciones y despliegue	2 days	Wed 30-09-26	Thu 01-10-26	81	100%
83			Ejecucion de pruebas ciclo 2	1 day	Fri 02-10-26	Fri 02-10-26	82	100%
84			27 Casos Registro Información	34 days	Fri 02-10-26	Thu 19-11-26	82	0%
85			HUs Garantía: 1, 3, 4, 49.1, 63-67	34 days	Fri 02-10-26	Thu 19-11-26	82	0%
86			Medición de Esfuerzo	1 day	Fri 02-10-26	Fri 02-10-26	82	0%
87			Análisis, Revision y Aprobacion	1 day	Fri 02-10-26	Fri 02-10-26	82	0%
88			Desarrollo	25 days	Fri 02-10-26	Fri 06-11-26	82	0%
89			Pruebas Internas	1 day	Mon 09-11-26	Mon 09-11-26	88	0%
90			Entrega y despliegue en QA	1 day	Tue 10-11-26	Tue 10-11-26	89	0%

Project: msproj11
Date: Wed 30-09-26



Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
91			Induccion de HU	1 day	Wed 11-11-26	Wed 11-11-26	90	0%
92			Ejecucion de pruebas ciclo 1	3 days	Thu 12-11-26	Mon 16-11-26	91	0%
93			Reuniones de Revisión UAT	1 day	Tue 17-11-26	Tue 17-11-26	92	0%
94			Correcciones y despliegue	1 day	Wed 18-11-26	Wed 18-11-26	93	0%
95			Ejecucion de pruebas ciclo 2	1 day	Thu 19-11-26	Thu 19-11-26	94	0%
96			27 Casos Seguimiento y Control	33 days	Thu 17-09-26	Wed 04-11-26	42	56%
97			OK con OBS: 8.4, 12.2, 29.1, 47.1	10 days	Thu 17-09-26	Thu 01-10-26	42	100%
98			Medición de Esfuerzo	1 day	Thu 17-09-26	Thu 17-09-26	42	100%
99			Análisis, Revision y Aprobacion	1 day	Thu 17-09-26	Thu 17-09-26	42	100%
100			Desarrollo	4 days	Thu 17-09-26	Wed 23-09-26	42	100%
101			Pruebas Internas	1 day	Thu 24-09-26	Thu 24-09-26	100	100%
102			Entrega y despliegue en QA	1 day	Fri 25-09-26	Fri 25-09-26	101	100%
103			Induccion de HU	1 day	Fri 25-09-26	Fri 25-09-26	101	100%
104			Ejecucion de pruebas ciclo 1	1 day	Mon 28-09-26	Mon 28-09-26	103	100%
105			Reuniones de Revisión UAT	1 day	Tue 29-09-26	Tue 29-09-26	104	100%
106			Correcciones y despliegue	1 day	Wed 30-09-26	Wed 30-09-26	105	100%
107			Ejecucion de pruebas ciclo 2	1 day	Thu 01-10-26	Thu 01-10-26	106	100%
108			NOK: 3.1, 3.7, 15.4, 30.1, 30.2, 31.2	9 days	Fri 25-09-26	Wed 07-10-26	100	100%
109			Medición de Esfuerzo	1 day	Fri 25-09-26	Fri 25-09-26	101	100%
110			Análisis, Revision y Aprobacion	1 day	Fri 25-09-26	Fri 25-09-26	101	100%
111			Desarrollo	4 days	Fri 25-09-26	Wed 30-09-26	101	100%
112			Pruebas Internas	1 day	Thu 01-10-26	Thu 01-10-26	111	100%
113			Entrega y despliegue en QA	1 day	Thu 01-10-26	Thu 01-10-26	111	100%

Project: msproj11
Date: Wed 30-09-26



Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
114			Induccion de HU	1 day	Thu 01-10-26	Thu 01-10-26	111	100%
115			Ejecucion de pruebas ciclo 1	1 day	Fri 02-10-26	Fri 02-10-26	114	100%
116			Reuniones de Revisión UAT	1 day	Mon 05-10-26	Mon 05-10-26	115	100%
117			Correcciones y despliegue	1 day	Tue 06-10-26	Tue 06-10-26	116	100%
118			Ejecucion de pruebas ciclo 2	1 day	Wed 07-10-26	Wed 07-10-26	117	100%
119			HU Garantía: 2.5, 6.1, 8.6, 14.3, 19.1, 19.2, 23.1, 24.4, 24.5, 26.1, 34.1, 38.4, 41.2, 42.2	24 days	Thu 01-10-26	Wed 04-11-26	111	13%
120			Medición de Esfuerzo	1 day	Thu 01-10-26	Thu 01-10-26	111	100%
121			Análisis, Revision y Aprobacion	1 day	Thu 01-10-26	Thu 01-10-26	111	100%
122			Desarrollo	15 days	Thu 01-10-26	Thu 22-10-26	111	10%
123			Pruebas Internas	1 day	Fri 23-10-26	Fri 23-10-26	122	0%
124			Entrega y despliegue en QA	1 day	Mon 26-10-26	Mon 26-10-26	123	0%
125			Induccion de HU	1 day	Mon 26-10-26	Mon 26-10-26	123	0%
126			Ejecucion de pruebas ciclo 1	2 days	Tue 27-10-26	Wed 28-10-26	125	0%
127			Reuniones de Revisión UAT	1 day	Thu 29-10-26	Thu 29-10-26	126	0%
128			Correcciones y despliegue	2 days	Fri 30-10-26	Mon 02-11-26	127	0%
129			Ejecucion de pruebas ciclo 2	2 days	Tue 03-11-26	Wed 04-11-26	128	0%
130			47 Casos Mejoras trasnversales	48,2 days	Wed 23-09-26	Tue 01-12-26		24%
131			NOK: 14.2, 14.3, 15.1, 15.2	7,2 days	Wed 23-09-26	Fri 02-10-26		100%
132			Medición de Esfuerzo	1 day	Wed 23-09-26	Wed 23-09-26	77	100%
133			Análisis, Revision y Aprobacion	1 day	Wed 23-09-26	Wed 23-09-26	77	100%
134			Desarrollo	1 day	Wed 23-09-26	Fri 25-09-26	77	100%

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predicted	% Complete
135			Pruebas Internas	1 day	Thu 24-09-26	Fri 25-09-26	134	100%
136			Entrega y despliegue en QA	1 day	Fri 25-09-26	Mon 28-09-26	135	100%
137			Induccion de HU	1 day	Fri 25-09-26	Mon 28-09-26	135	100%
138			Ejecucion de pruebas ciclo 1	1 day	Mon 28-09-26	Tue 29-09-26	137	100%
139			Reuniones de Revisión UAT	1 day	Tue 29-09-26	Wed 30-09-26	138	100%
140			Correcciones y despliegue	1 day	Wed 30-09-26	Thu 01-10-26	139	100%
141			Ejecucion de pruebas ciclo 2	1 day	Thu 01-10-26	Fri 02-10-26	140	100%
142			HU Garantía: 11, 19, 21, 25, 26, 27, 29, 32, 33, 38, 39	43 days	Wed 30-09-26	Tue 01-12-26	139	7%
143			Medición de Esfuerzo	1 day	Wed 30-09-26	Thu 01-10-26	139	100%
144			Análisis, Revision y Aprobacion	1 day	Wed 30-09-26	Thu 01-10-26	139	100%
145			Desarrollo	28 days	Wed 30-09-26	Tue 10-11-26	139	5%
146			Pruebas Internas	5 days	Tue 10-11-26	Tue 17-11-26	145	0%
147			Entrega y despliegue en QA	1 day	Tue 17-11-26	Wed 18-11-26	146	0%
148			Induccion de HU	1 day	Tue 17-11-26	Wed 18-11-26	146	0%
149			Ejecucion de pruebas ciclo 1	5 days	Wed 18-11-26	Wed 25-11-26	148	0%
150			Reuniones de Revisión UAT	1 day	Wed 25-11-26	Thu 26-11-26	149	0%
151			Correcciones y despliegue	2 days	Thu 26-11-26	Mon 30-11-26	150	0%
152			Ejecucion de pruebas ciclo 2	1 day	Mon 30-11-26	Tue 01-12-26	151	0%
153			PAP 2	0 days	Tue 01-12-26	Tue 01-12-26		0%
154			Coordinacion PAP	0 days	Tue 01-12-26	Tue 01-12-26	152	0%
155			Ejecución PAP	0 days	Tue 01-12-26	Tue 01-12-26	154	0%
156			Documentación Actualización	7 days	Wed 25-11-26	Fri 04-12-26	149	0%


Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Pred	% Complete
157			Documento Técnica Actualización	3 days	Wed 25-11-26	Mon 30-11-26	149	0%
158			Manual de Usuario Actualización	3 days	Mon 30-11-26	Thu 03-12-26	157	0%
159			Aprobaciones Documentos	1 day	Thu 03-12-26	Fri 04-12-26	158	0%

Project: msproj11
Date: Wed 30-09-26

Task



Split



Milestone



Summary



Project Summary



Inactive Task



Inactive Milestone



Inactive Summary



Manual Task



Duration-only



Manual Summary Rollup



Manual Summary




Start-only



Finish-only



External Tasks



External Milestone



Deadline




Progress






Manual Progress



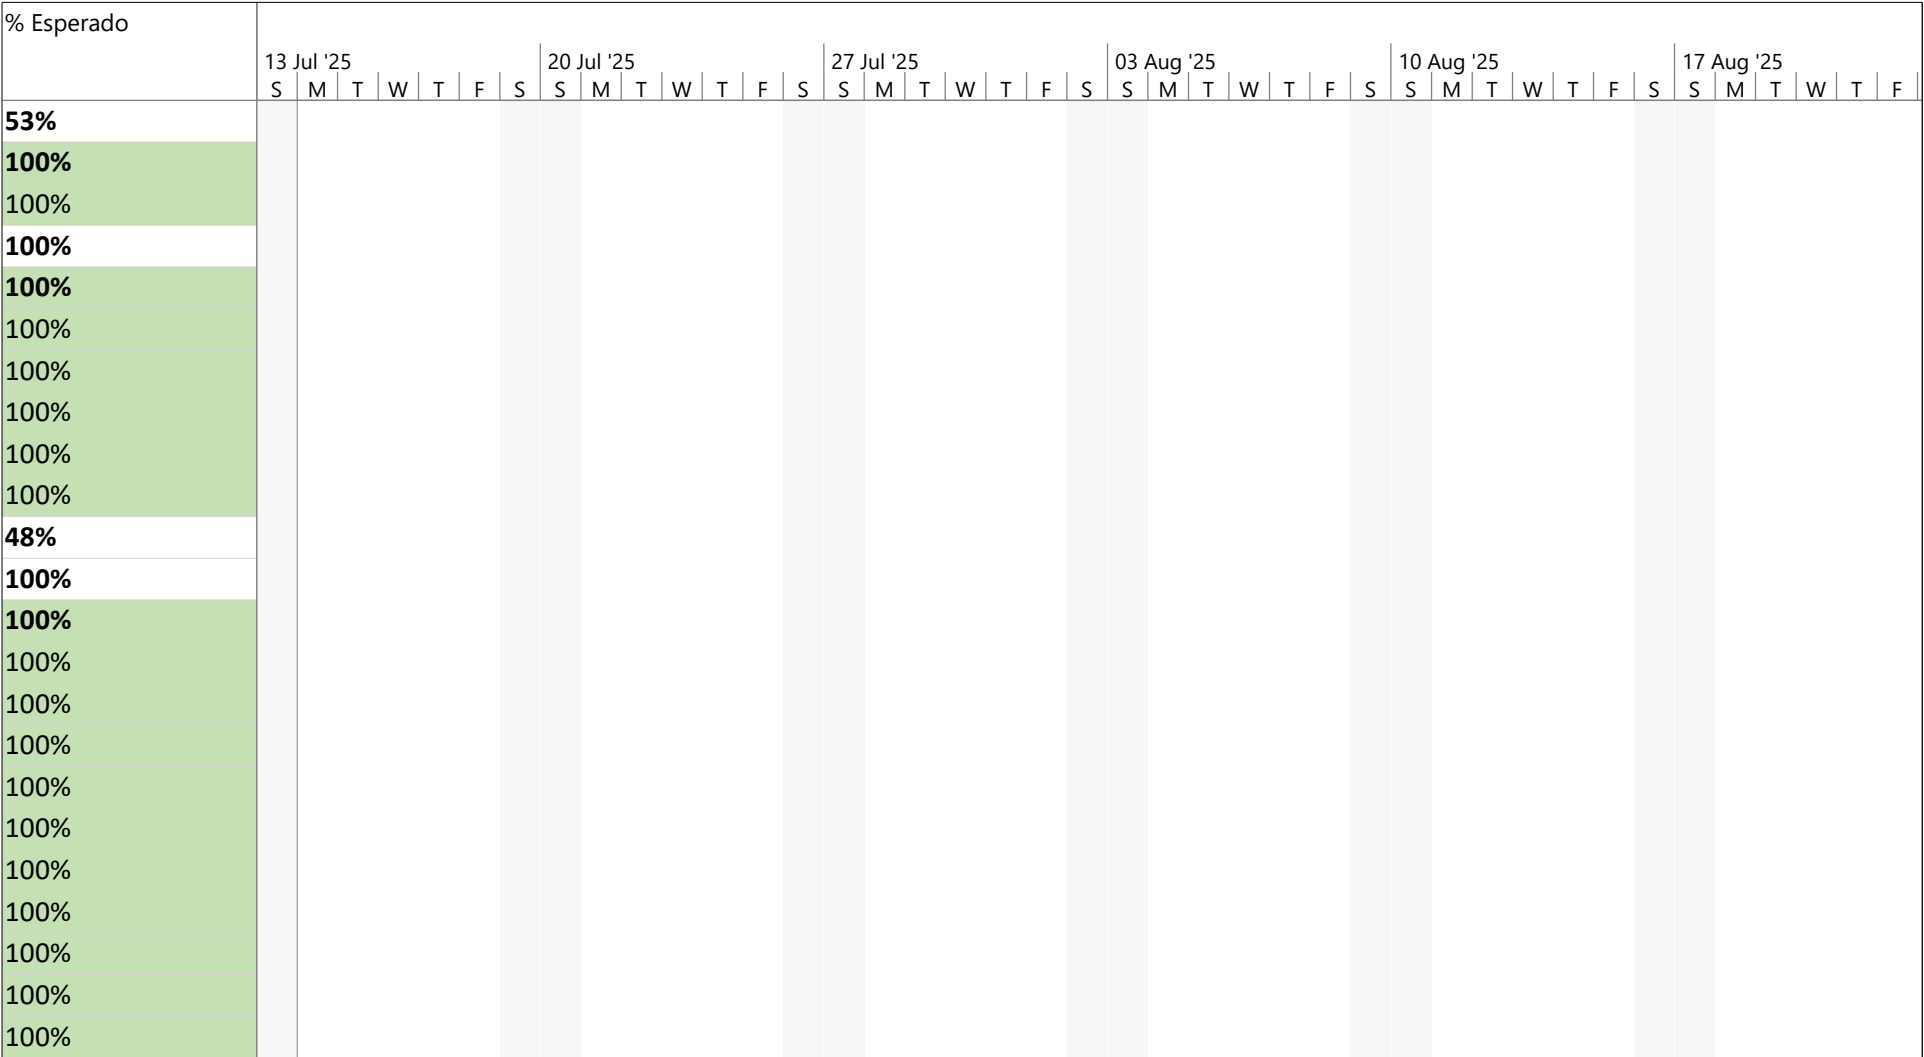



Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

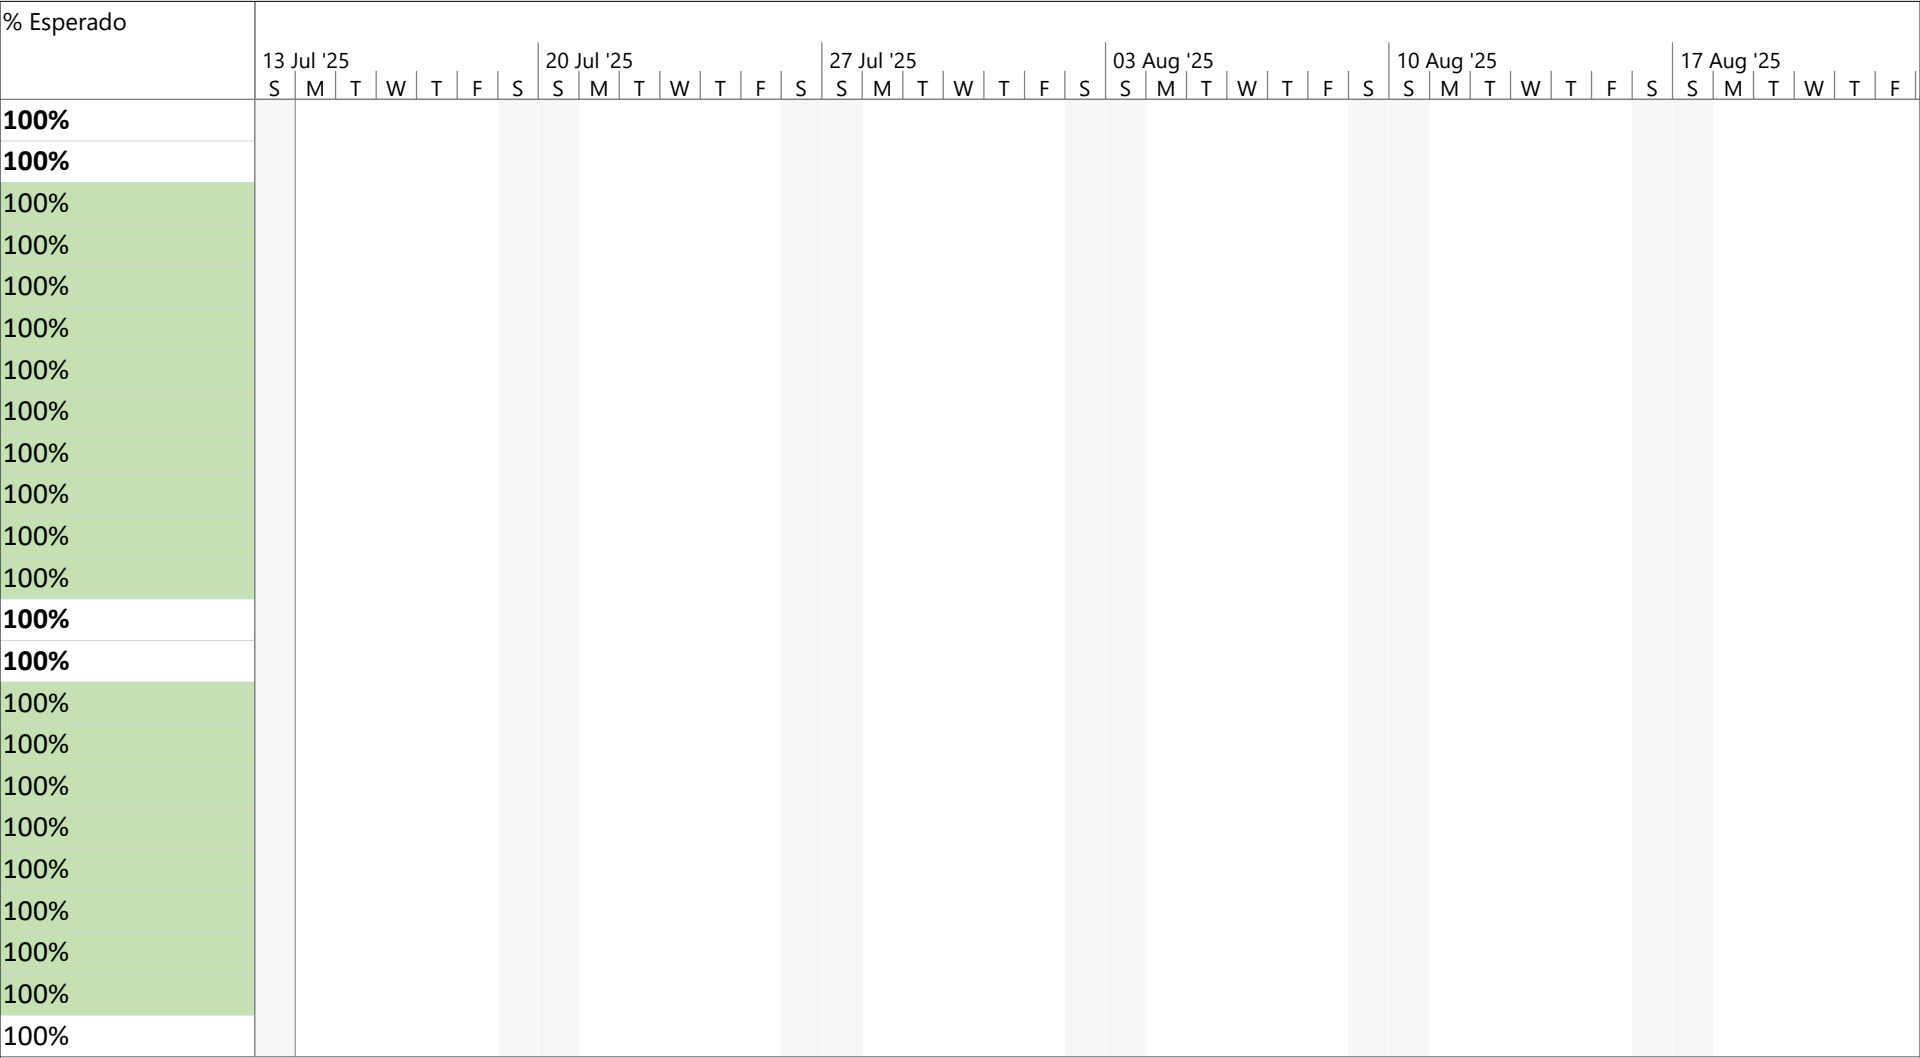


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


[illegible]

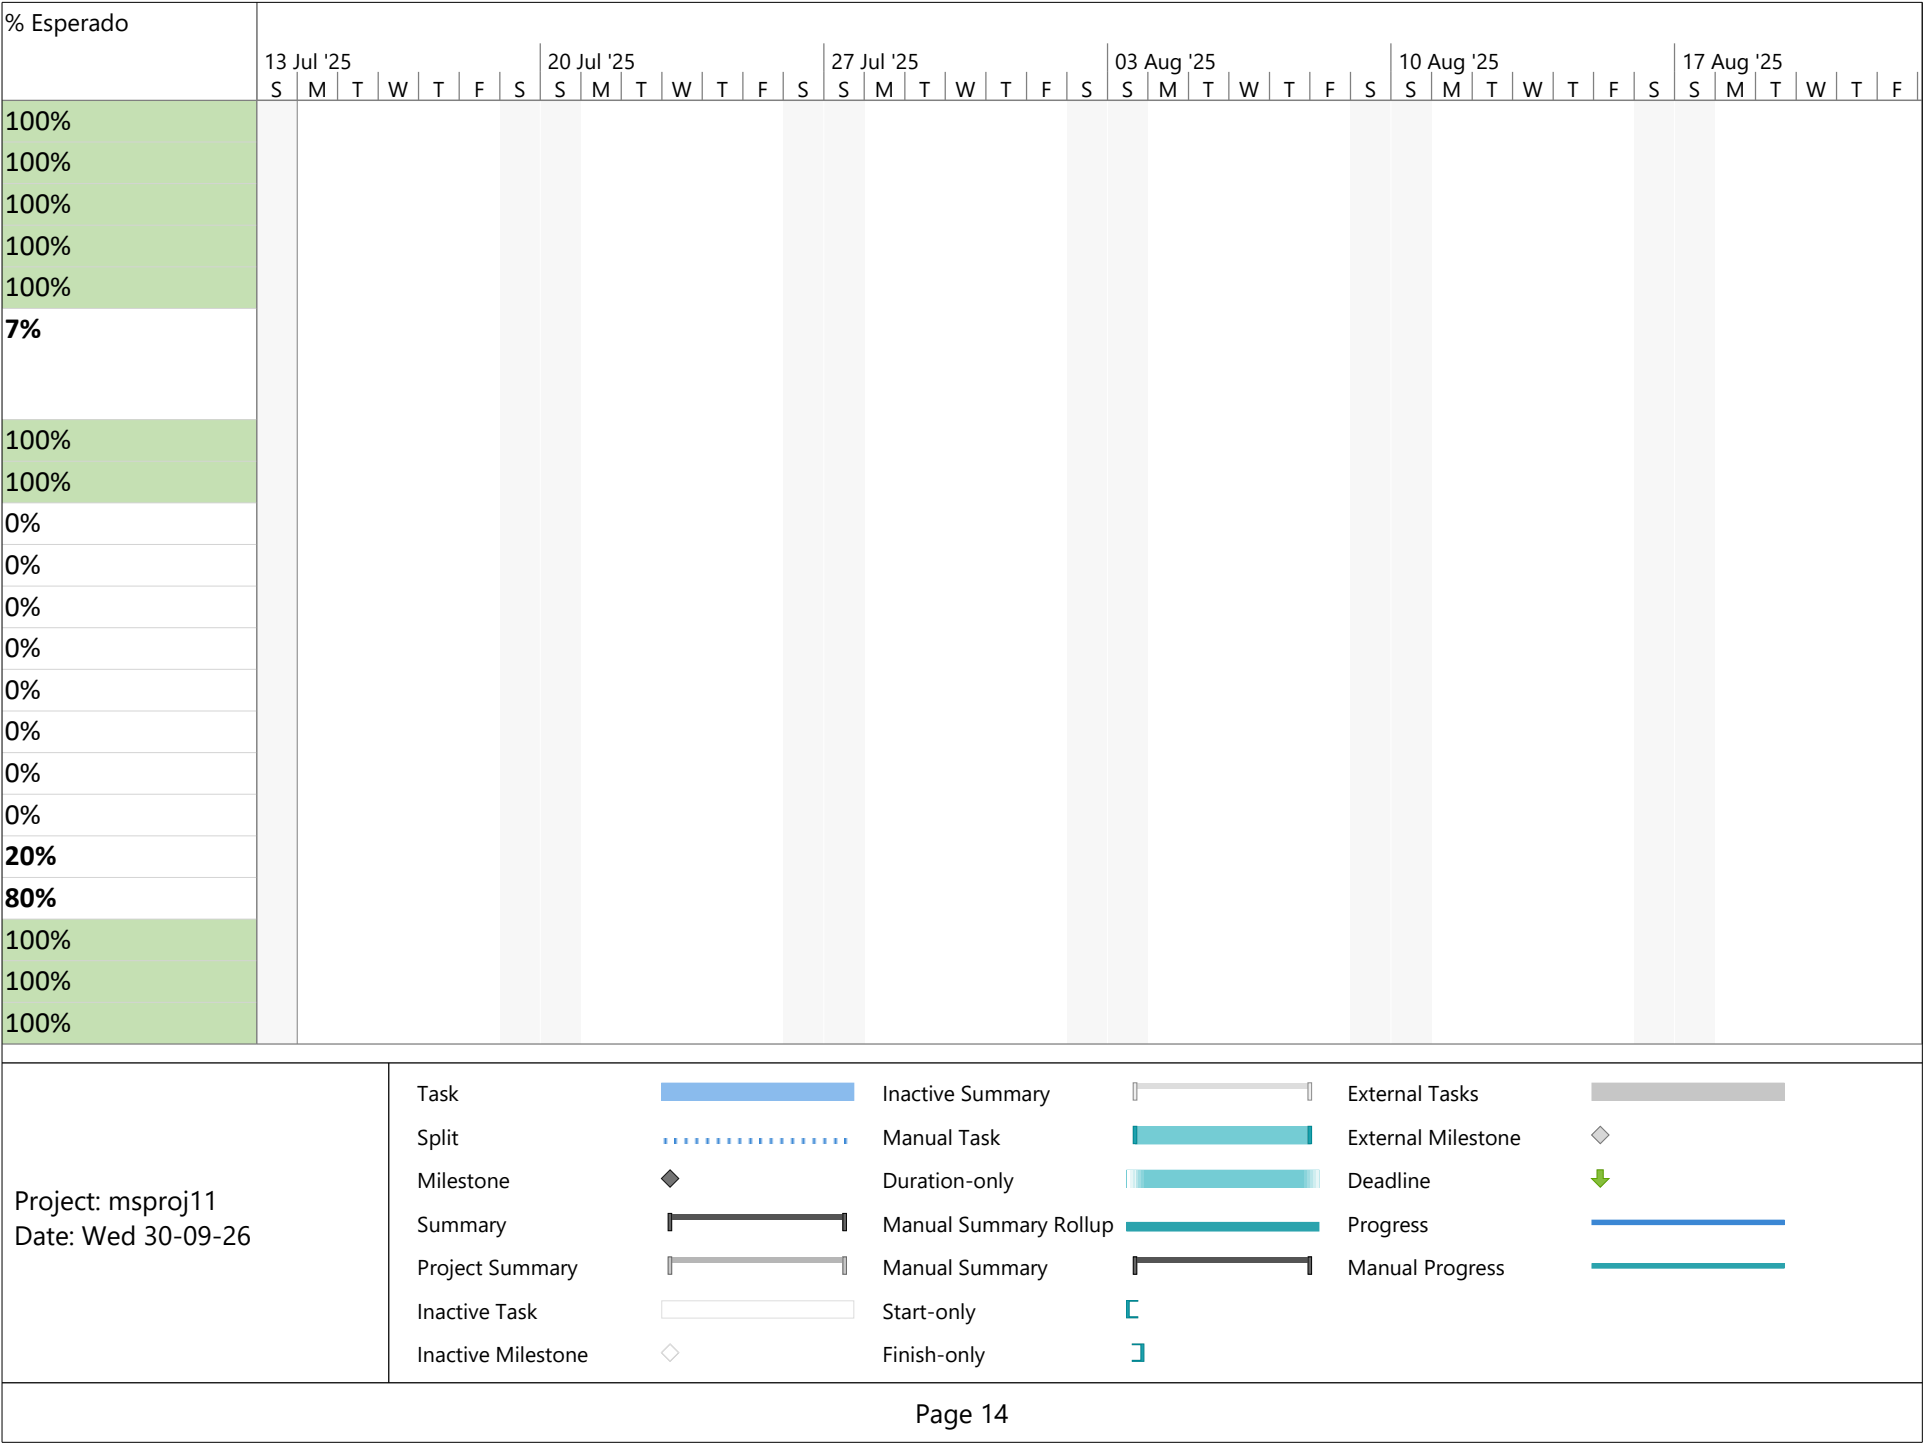

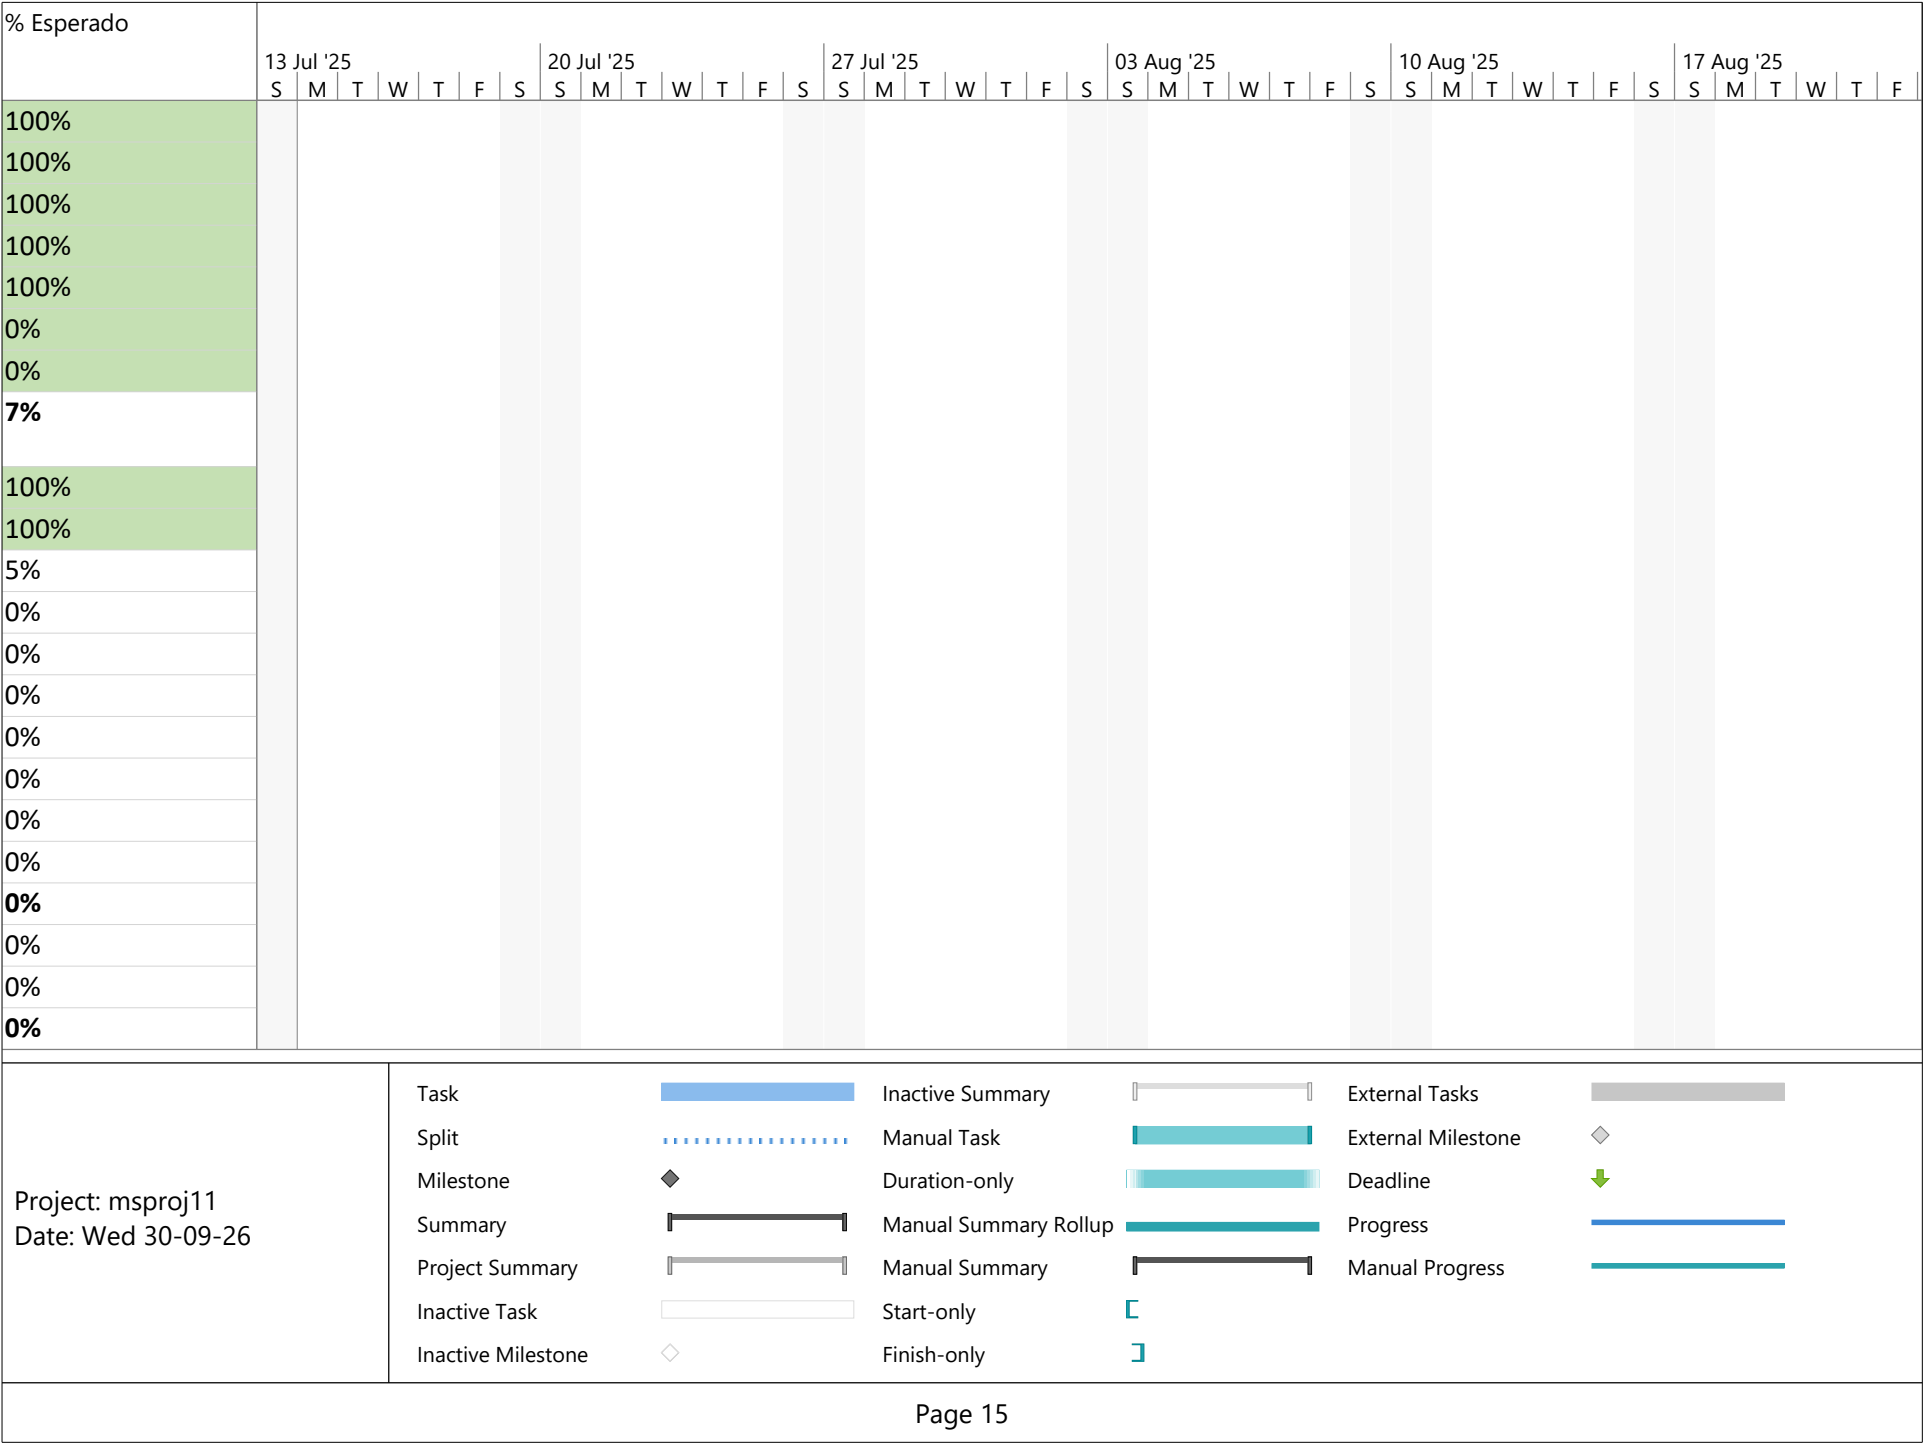






Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

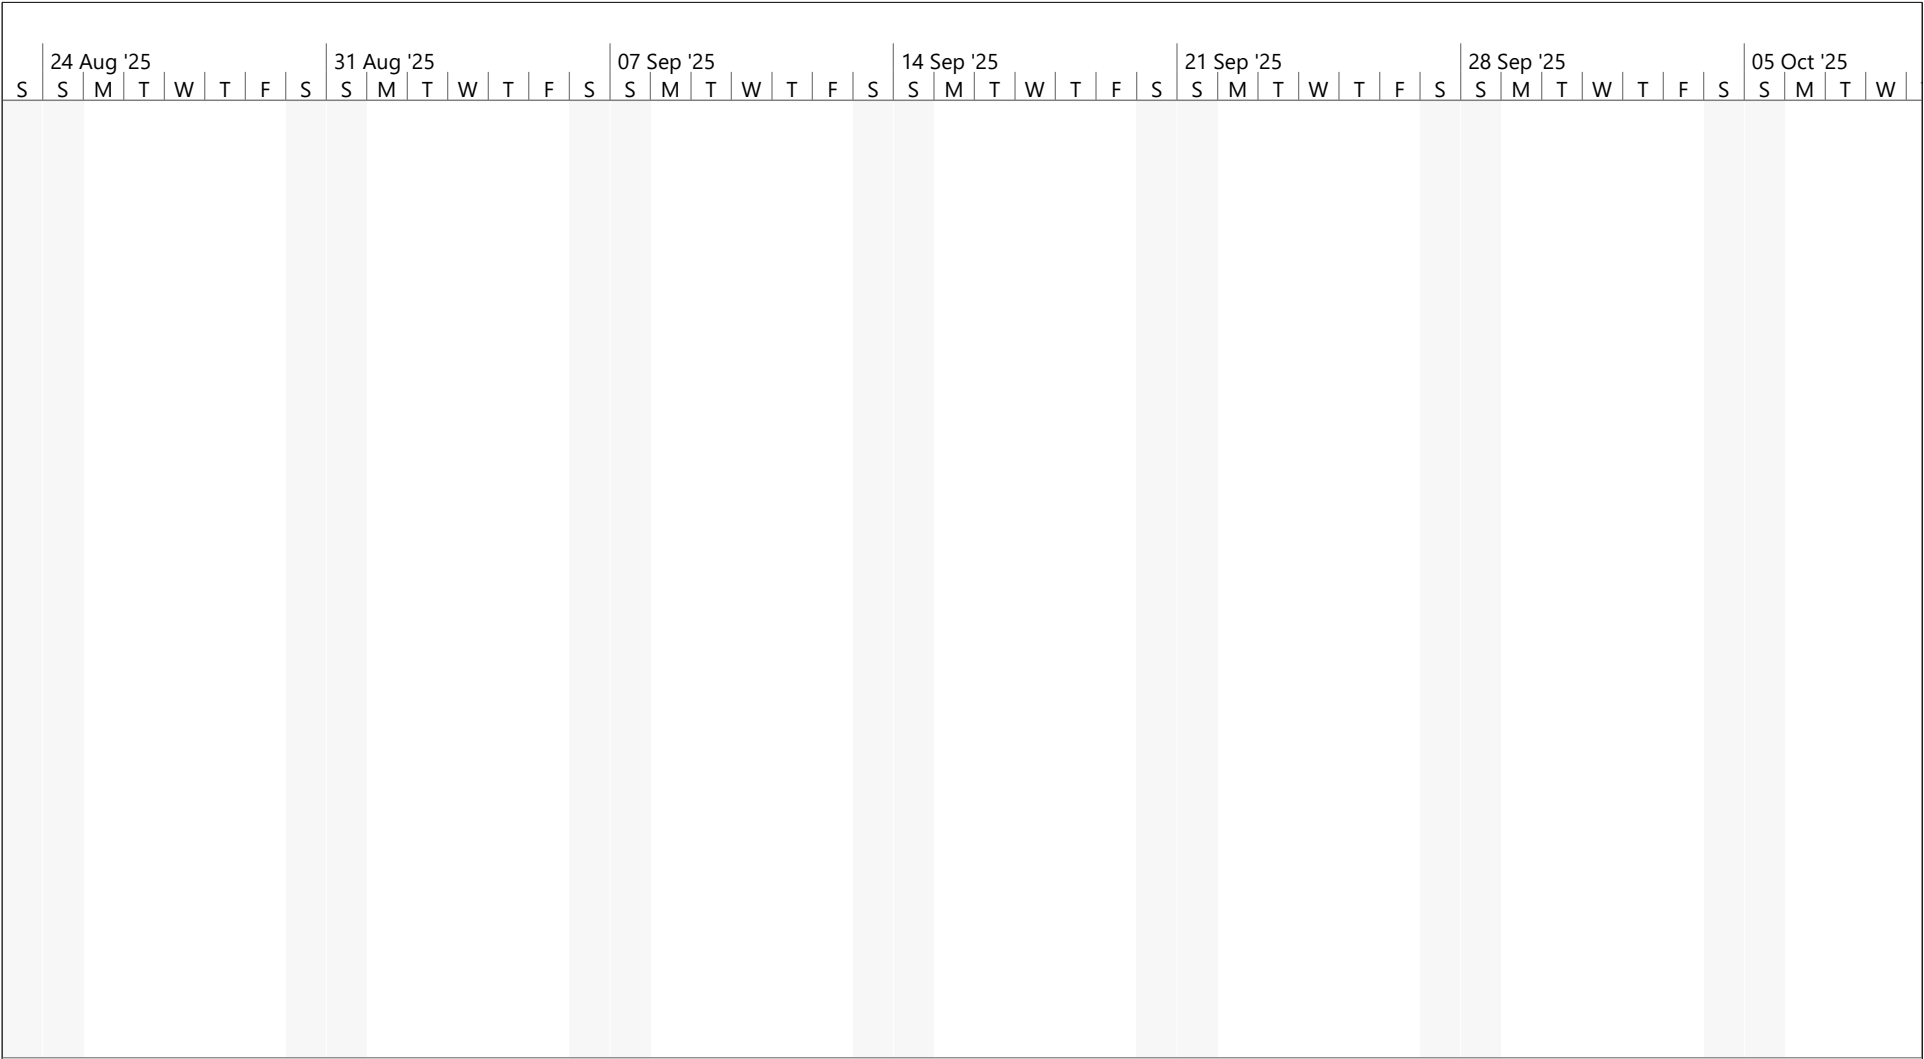


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

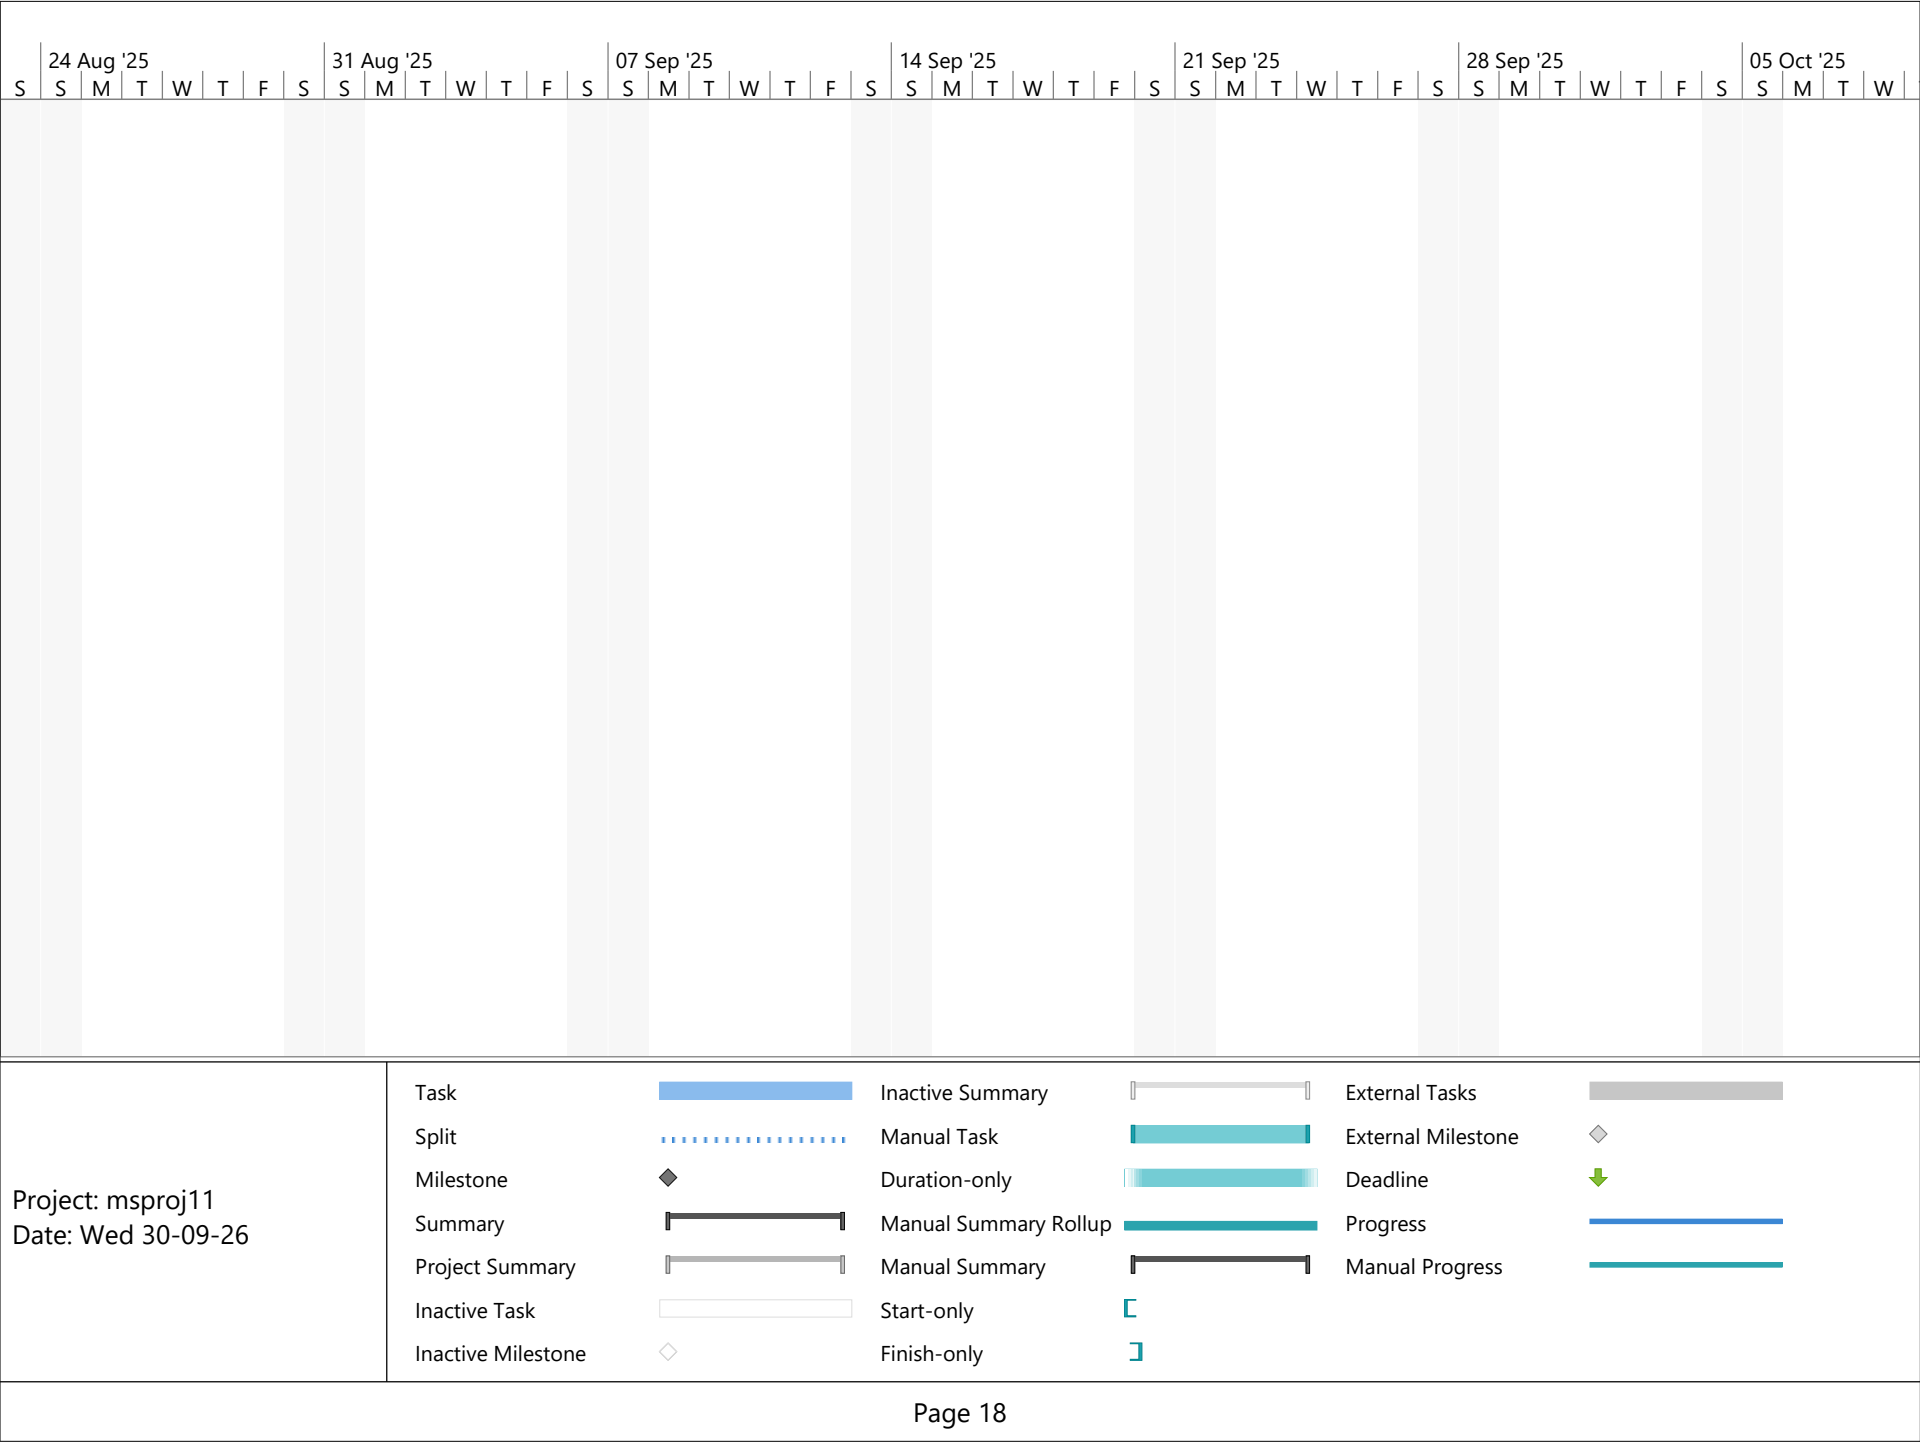

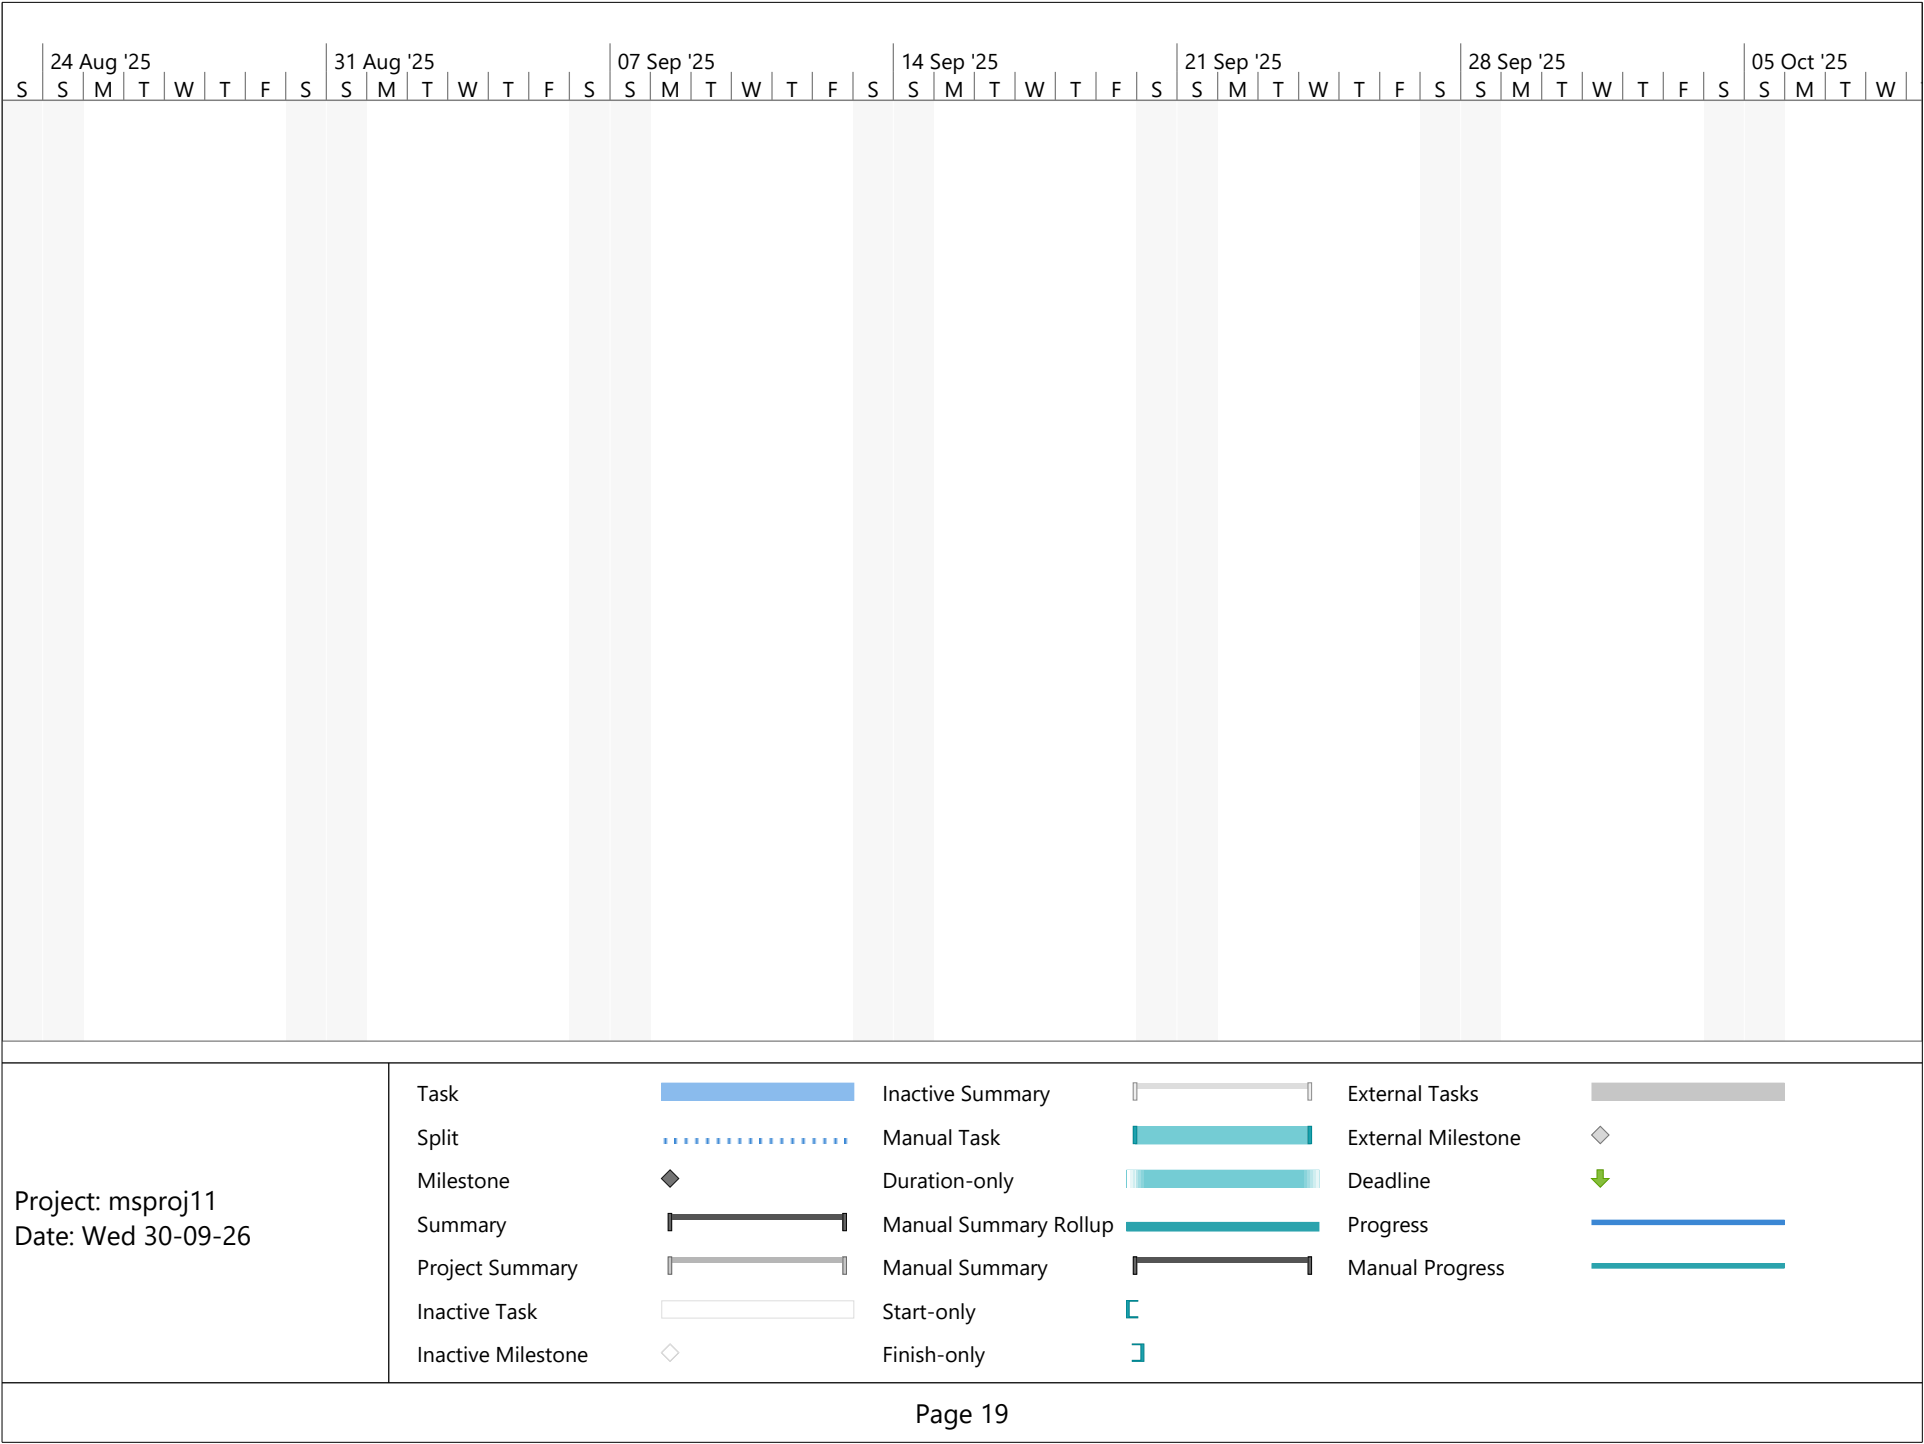

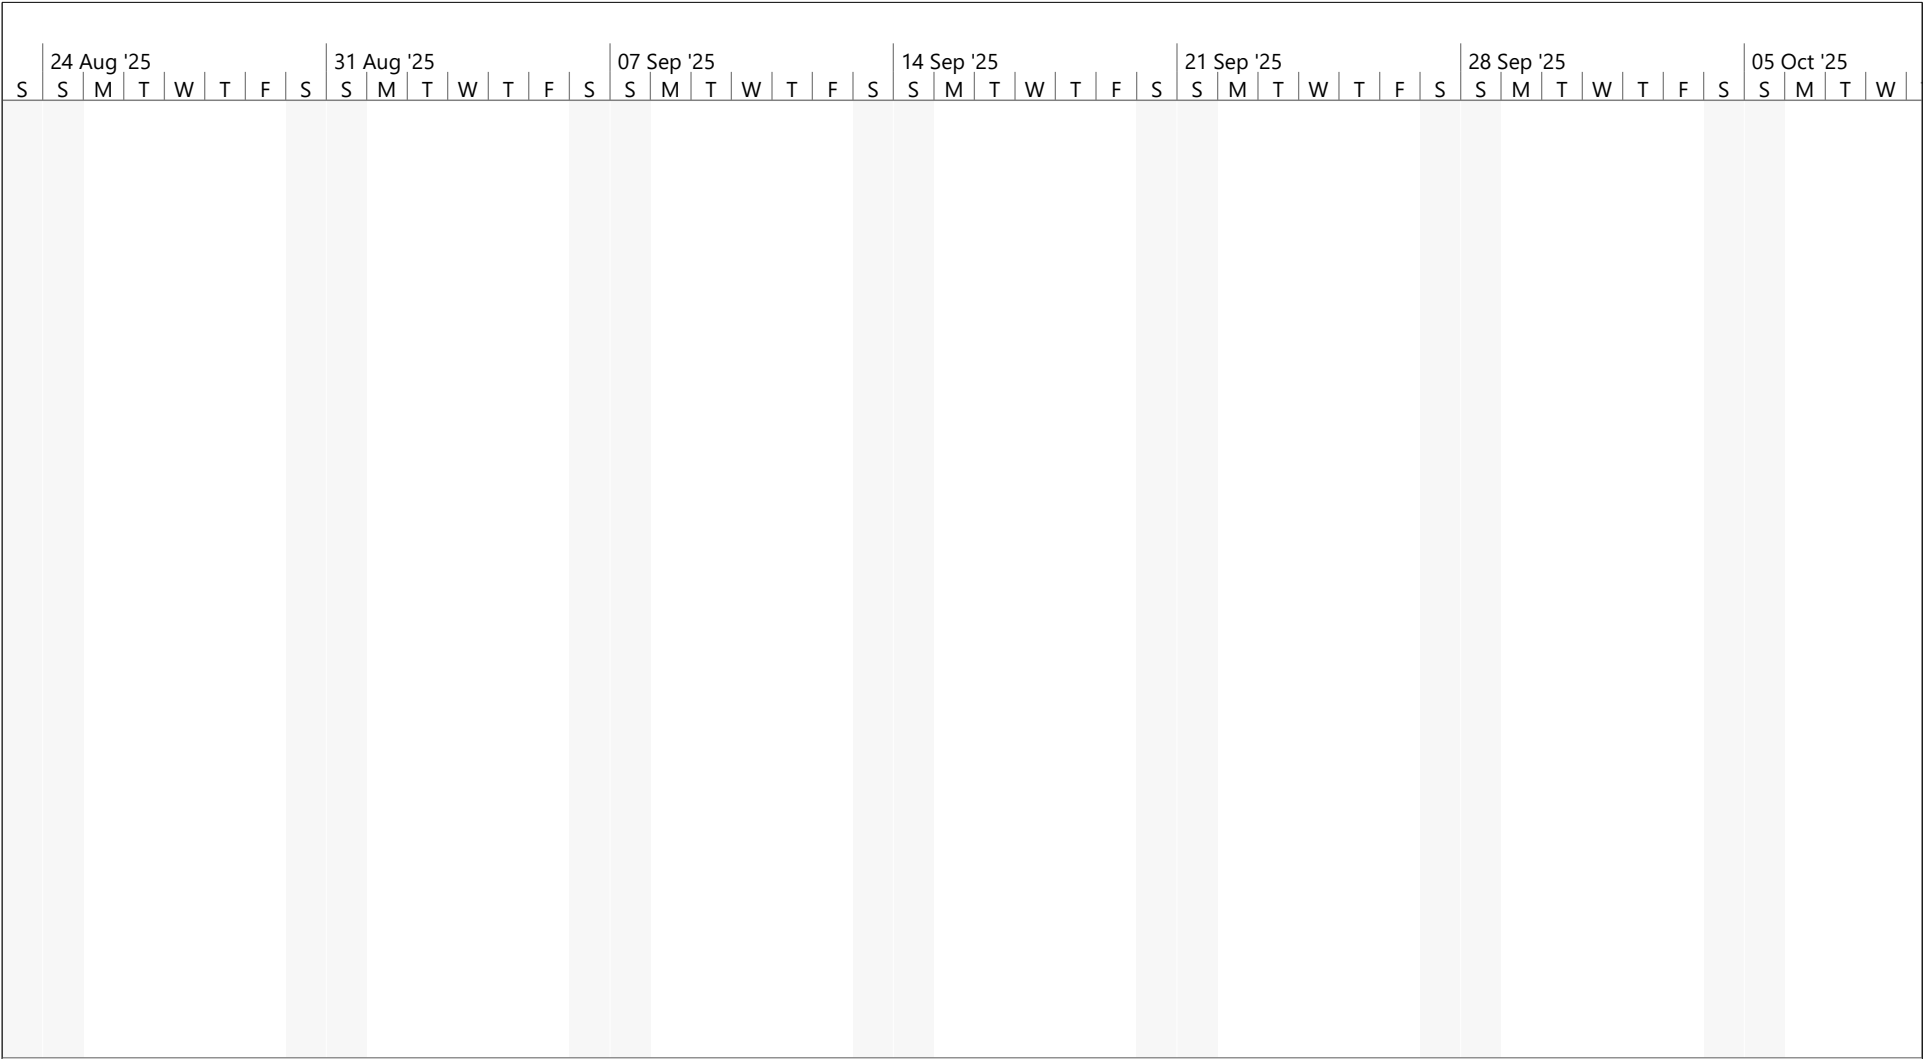

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

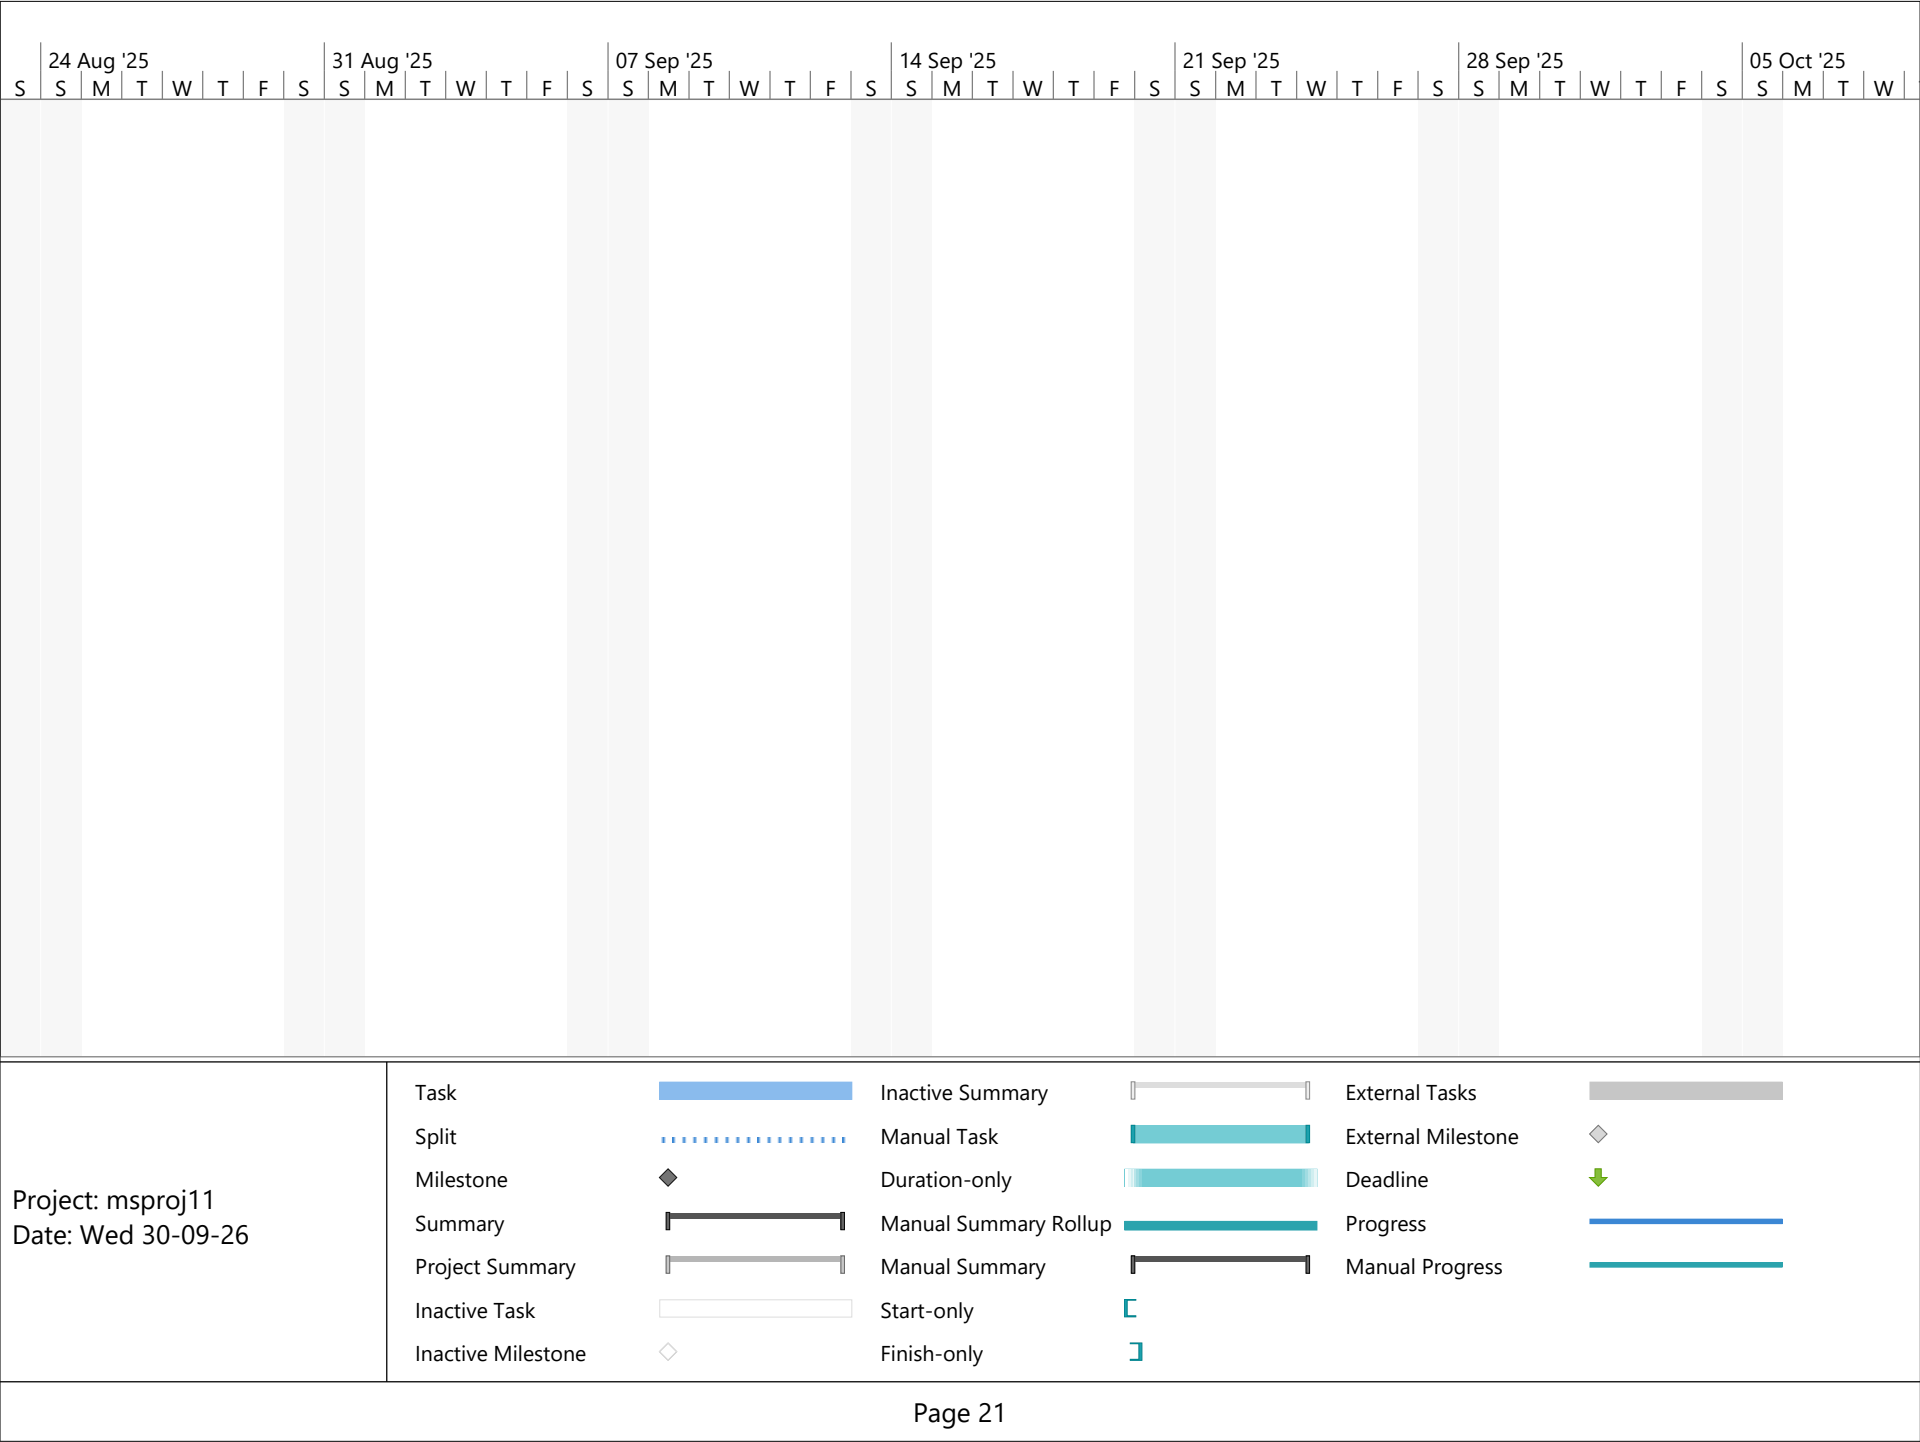

S

S

M

T

W

T

F

S

28 Sep '25

S

S

M

T

W

T

F

S

05 Oct '25

Project: msproj11

Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone


Deadline

Progress


Manual Progress

Page 21

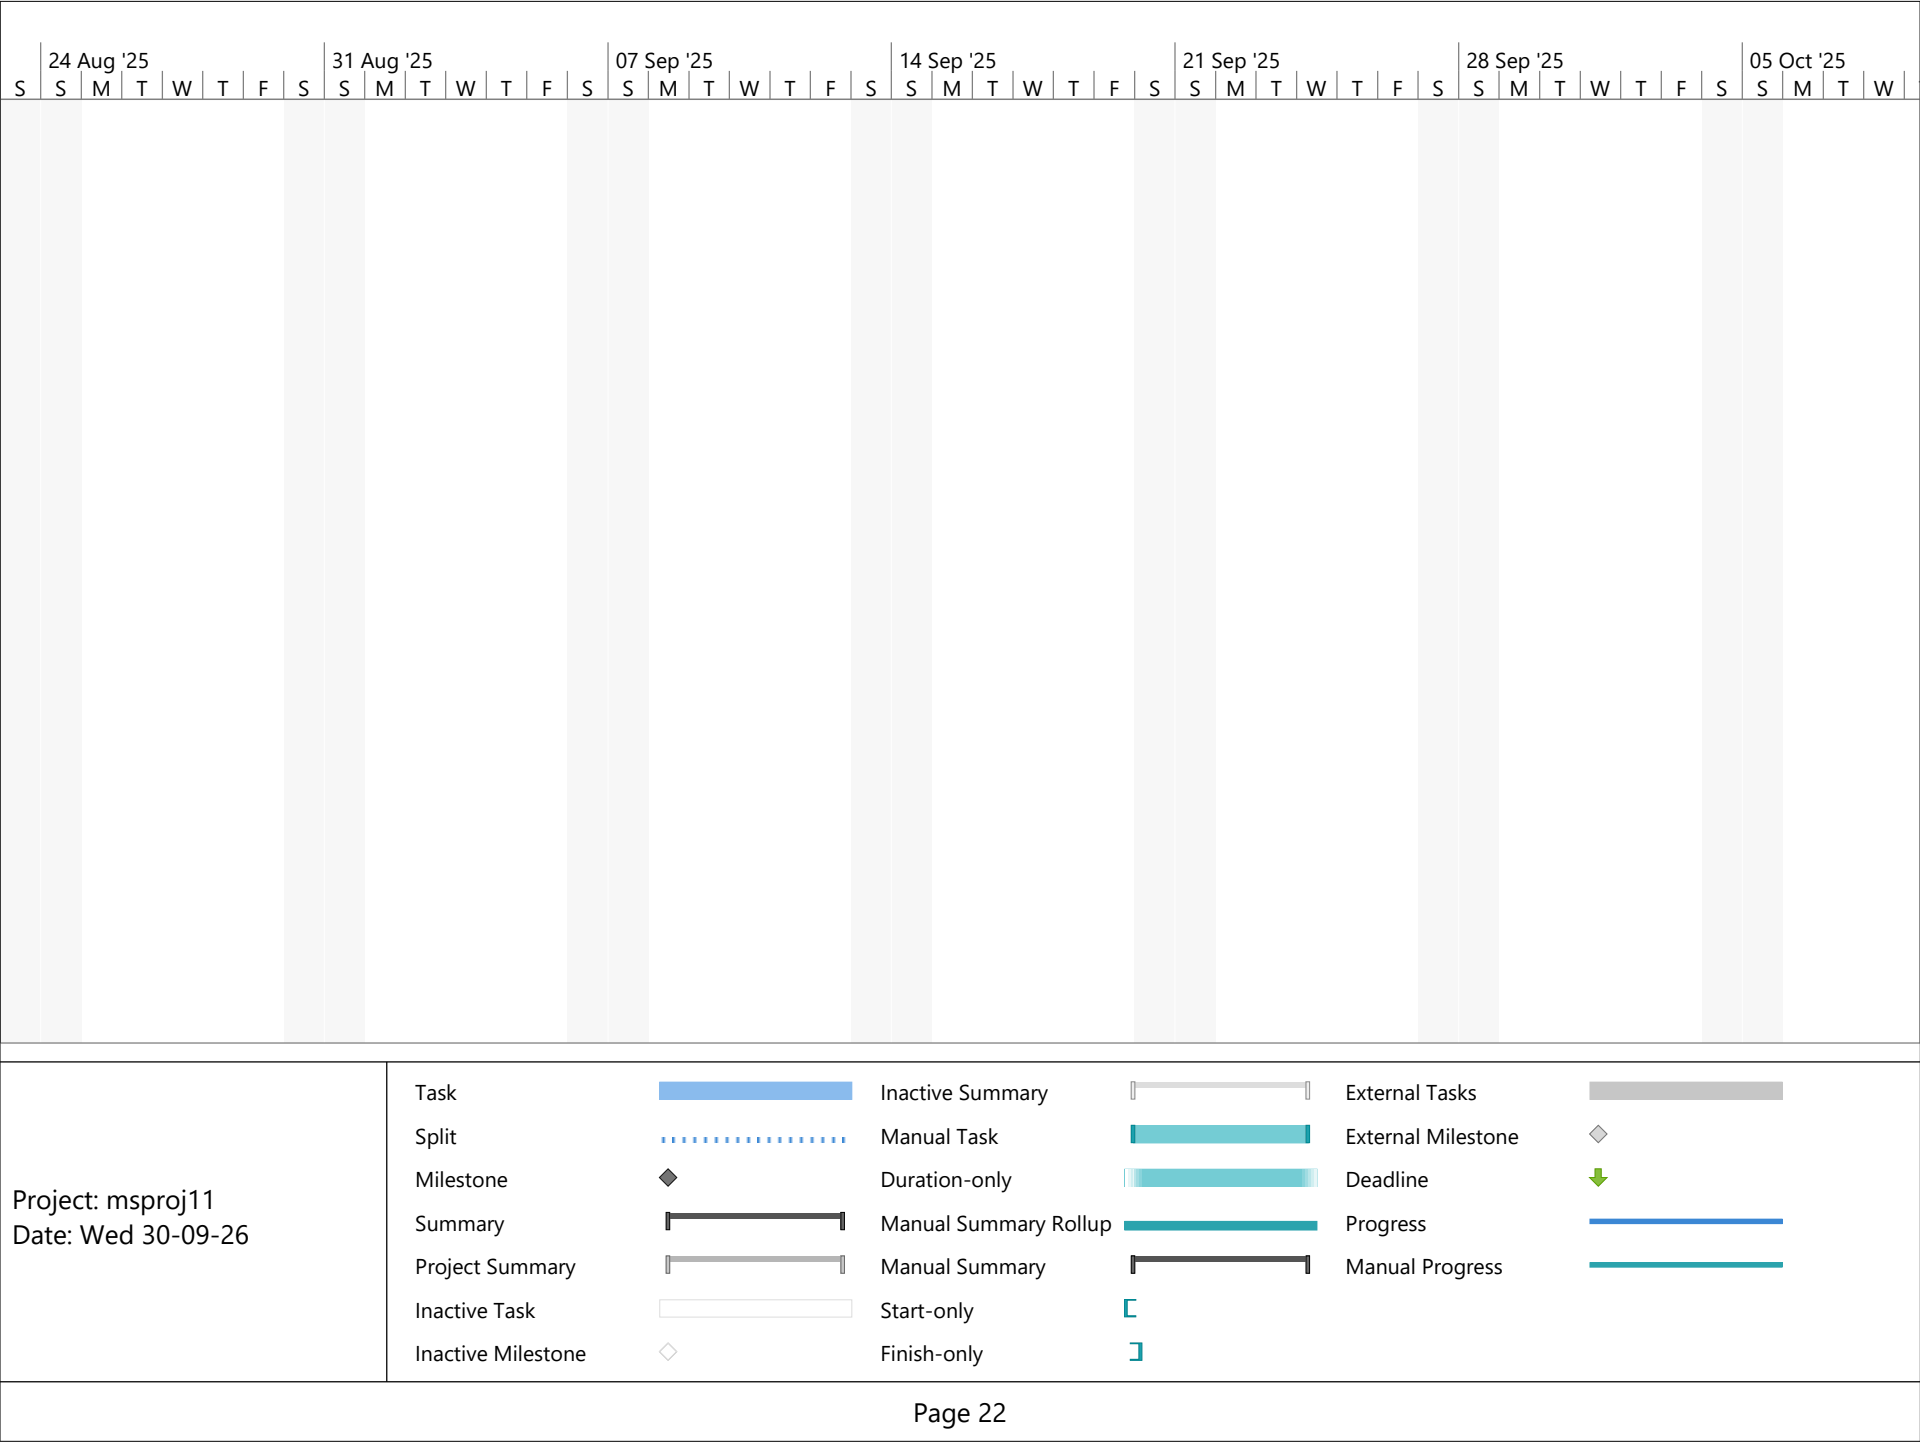

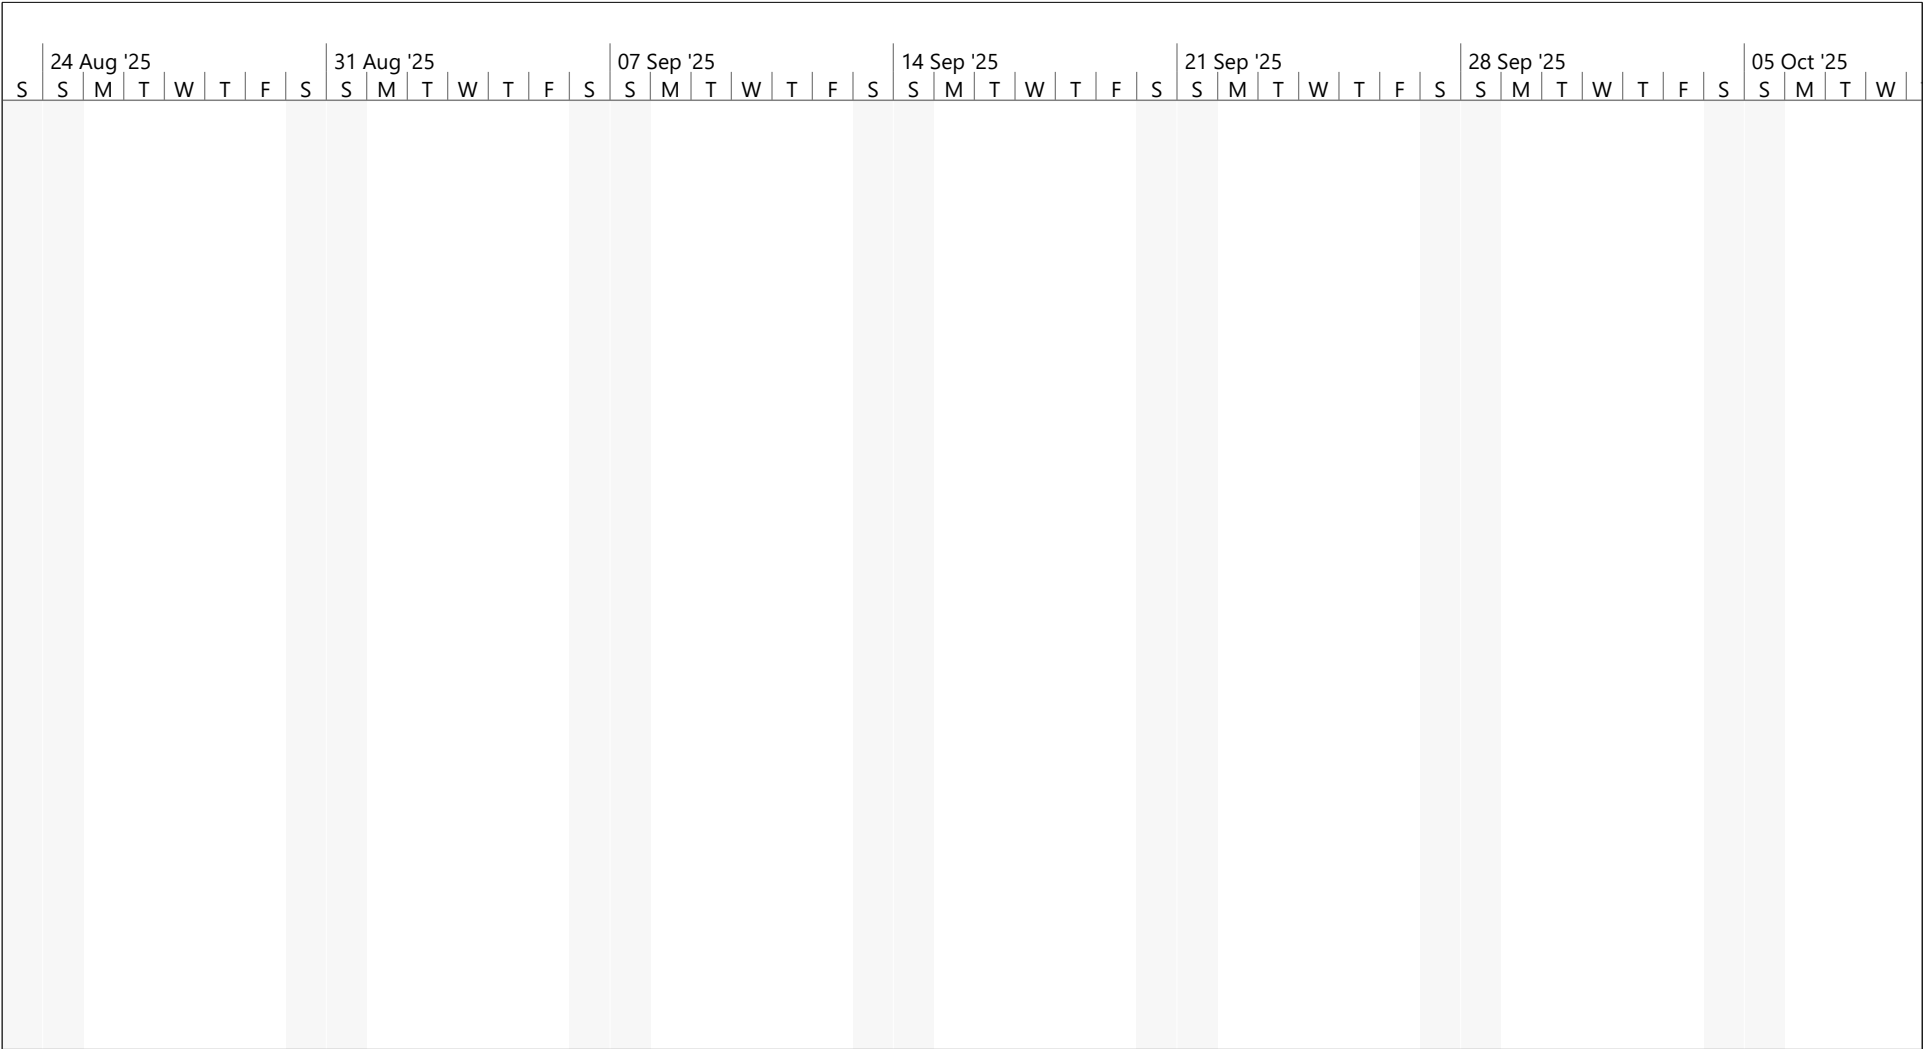

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

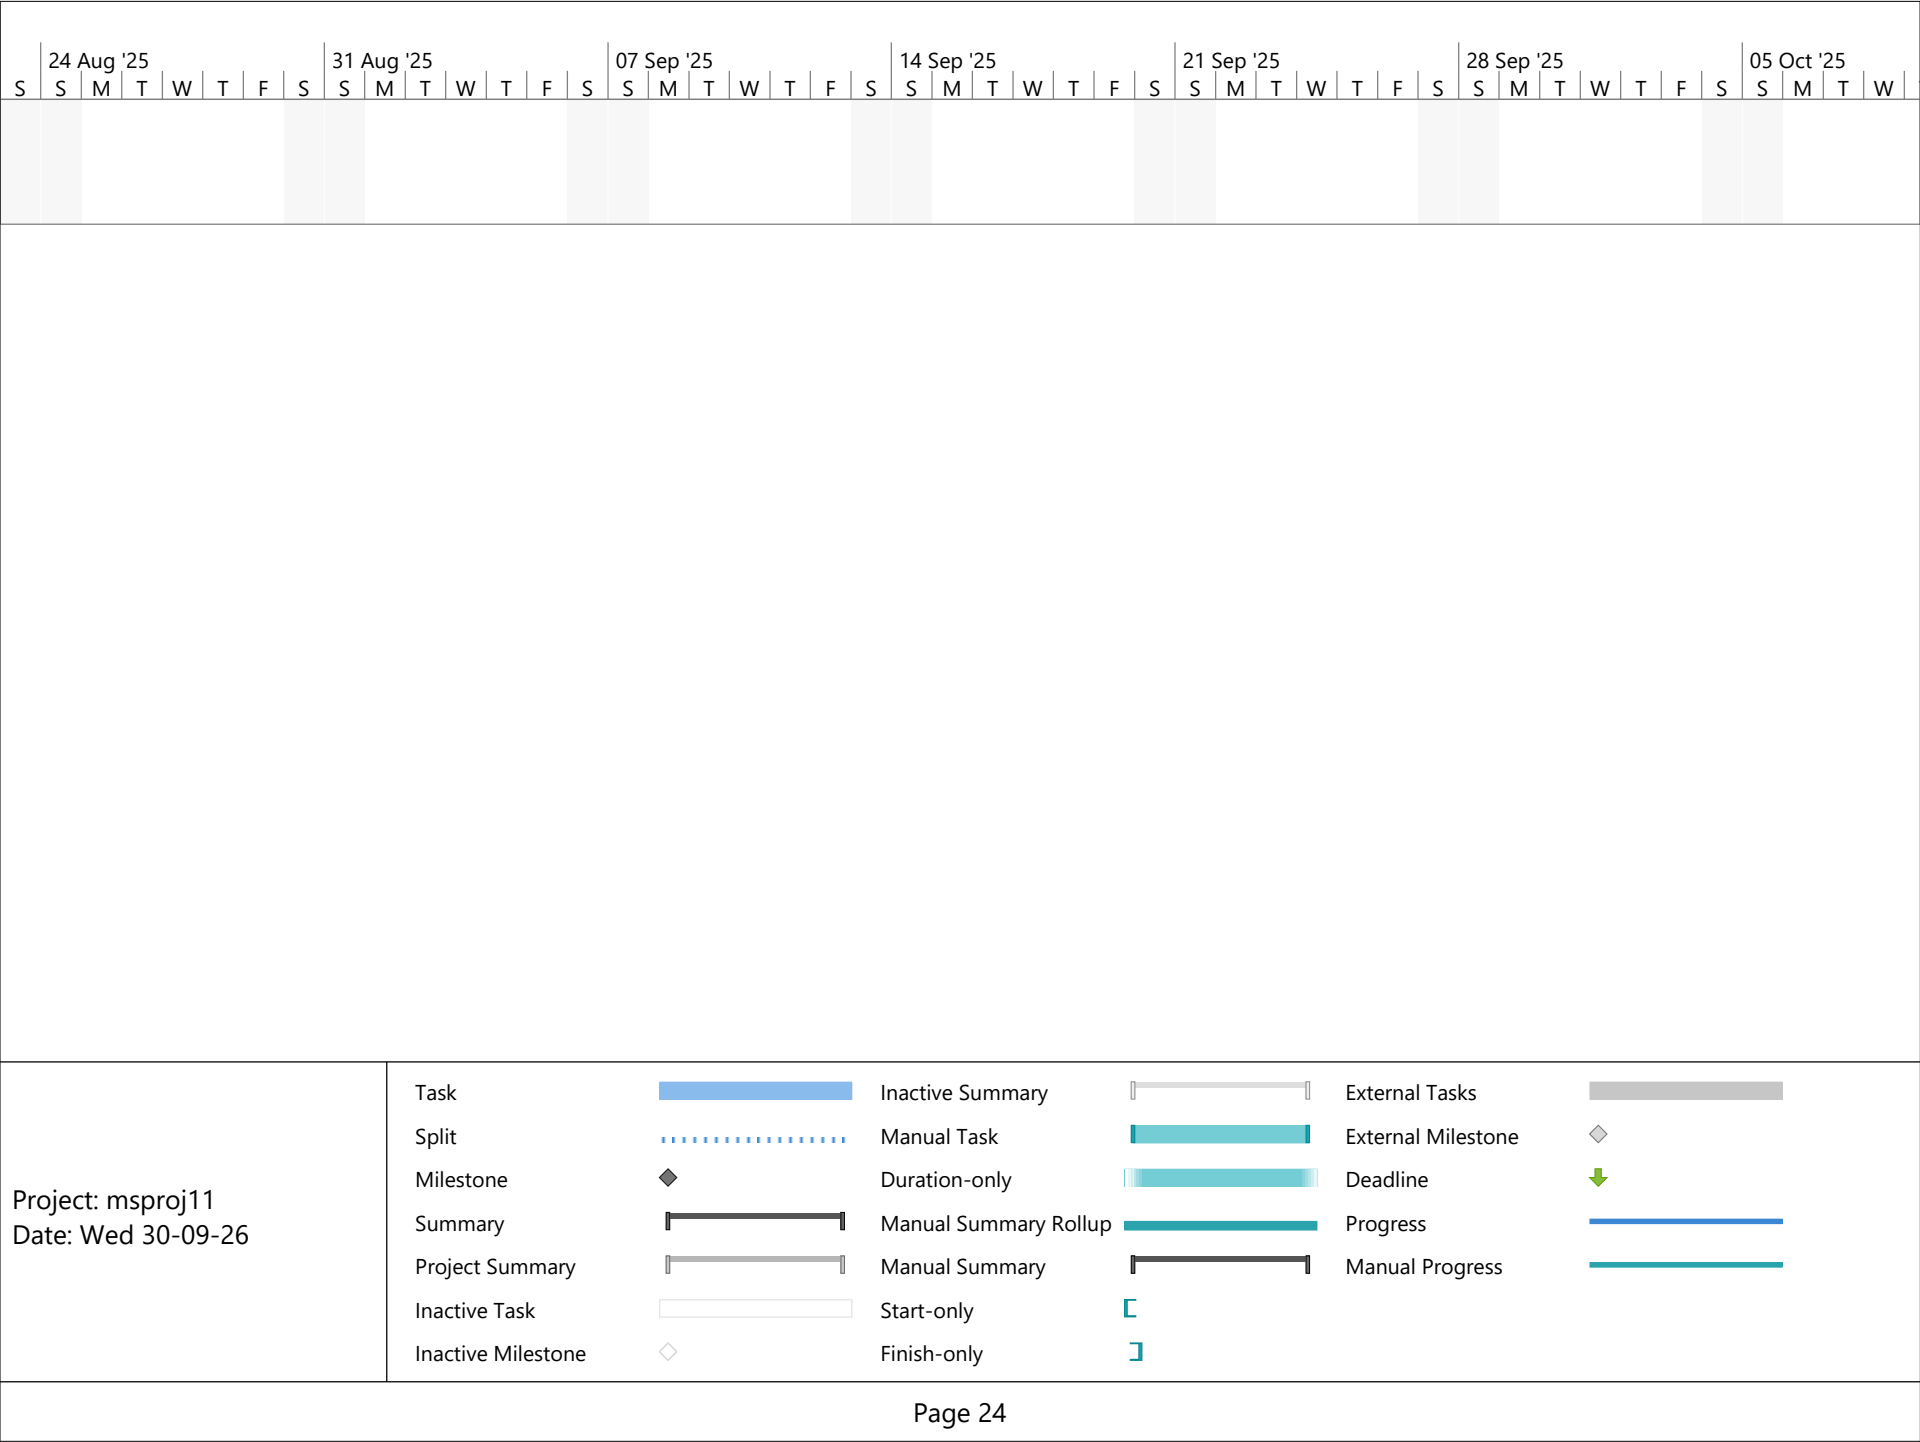

S

S

M

T

W

T

F

S

21 Sep '25

S

S

M

T

W

T

F

S

28 Sep '25

S

S

M

T

W

T

F

S

05 Oct '25

Project: msproj11

Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone


Deadline



Progress


Manual Progress


Page 24

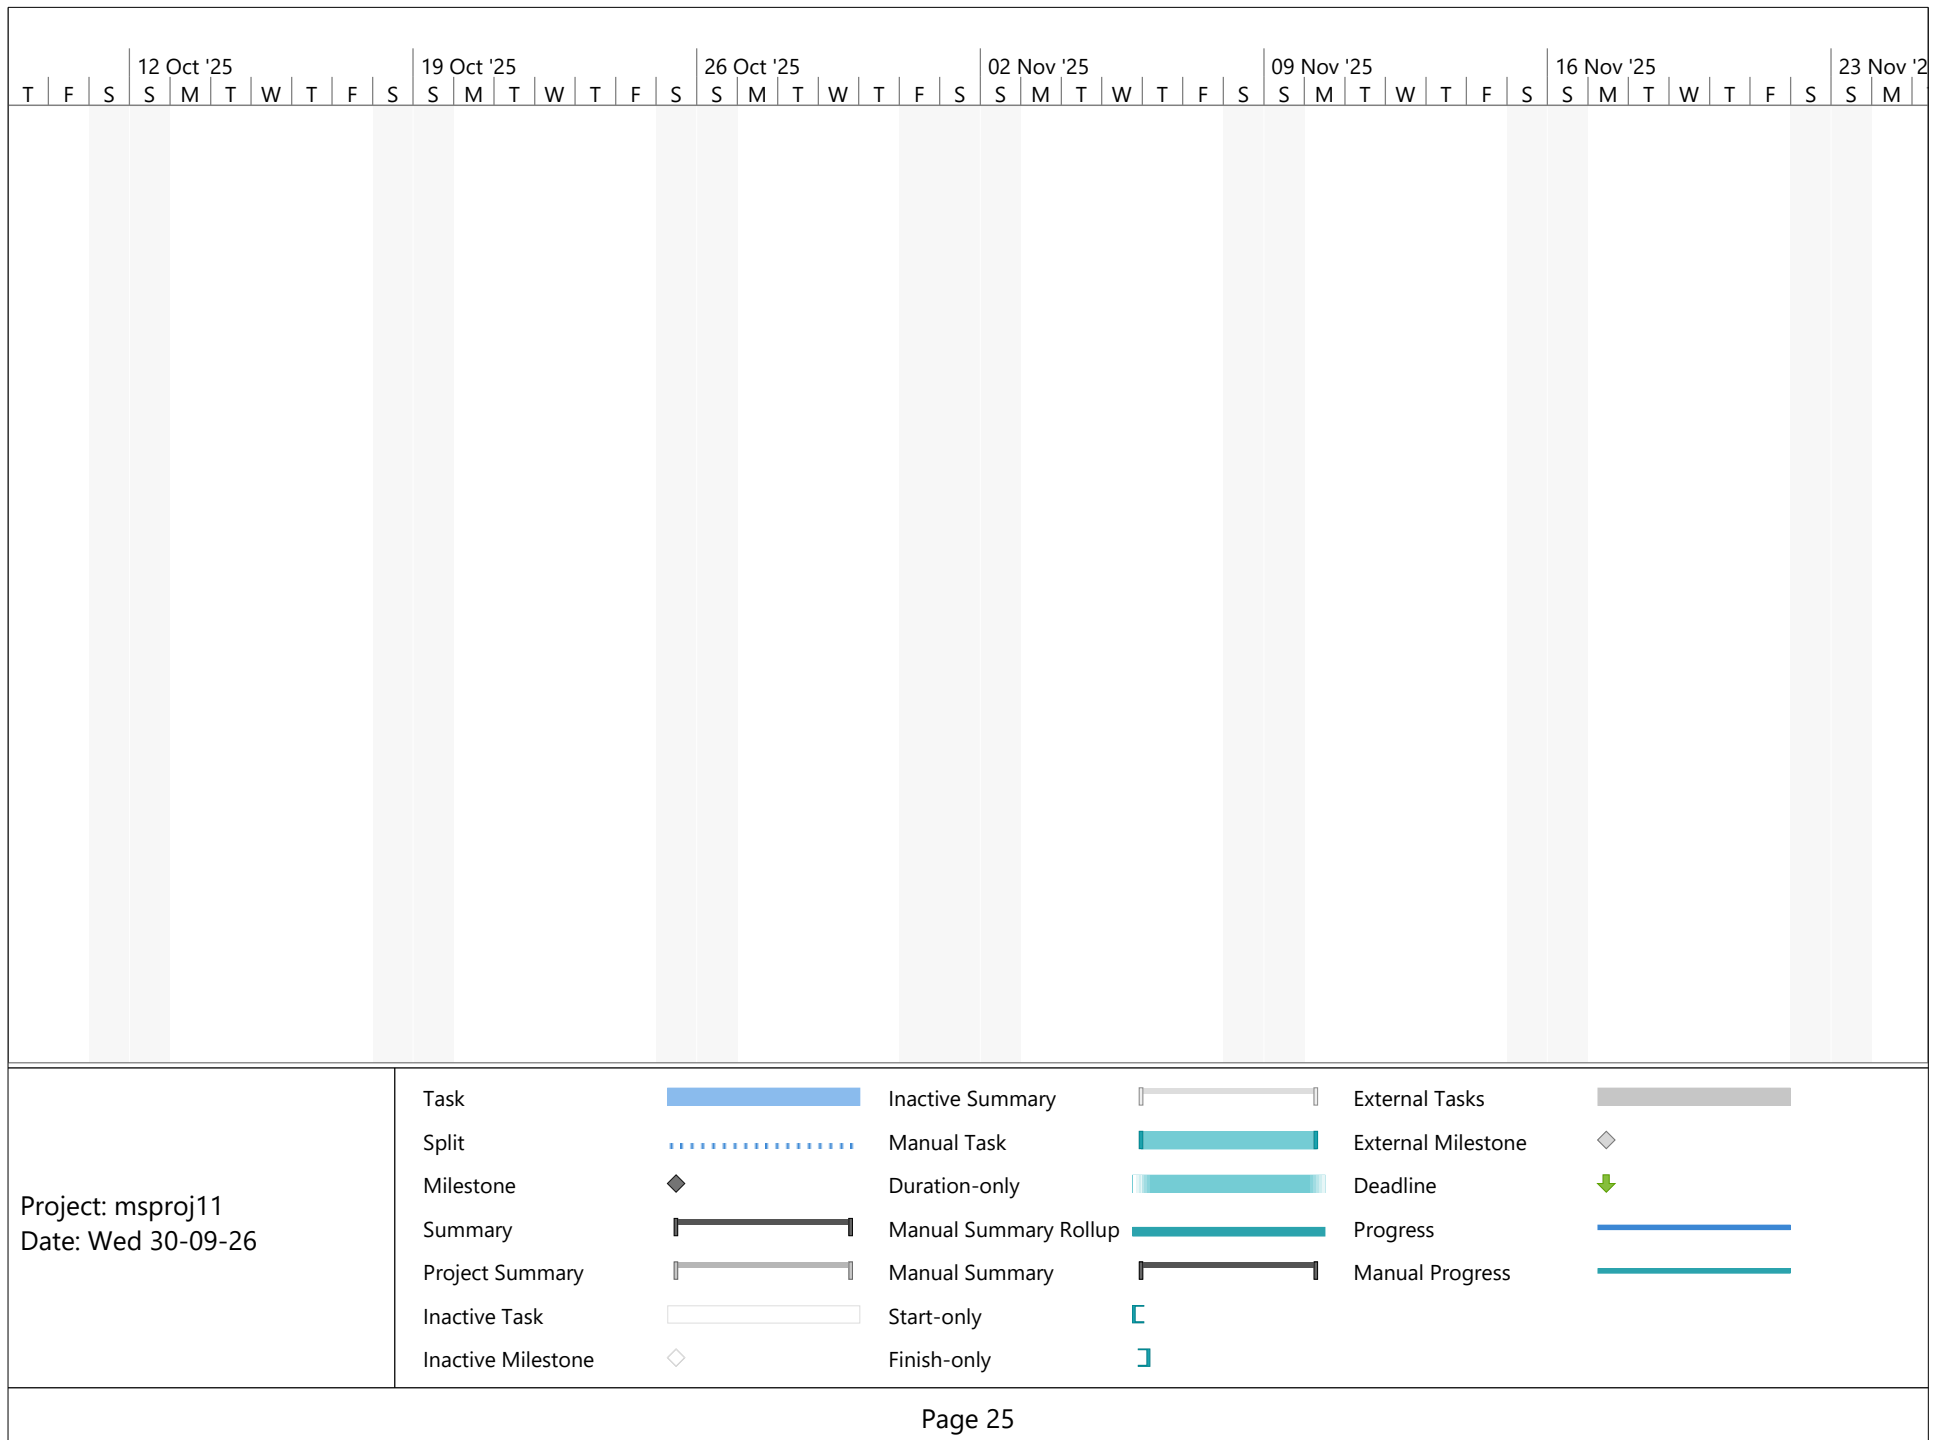

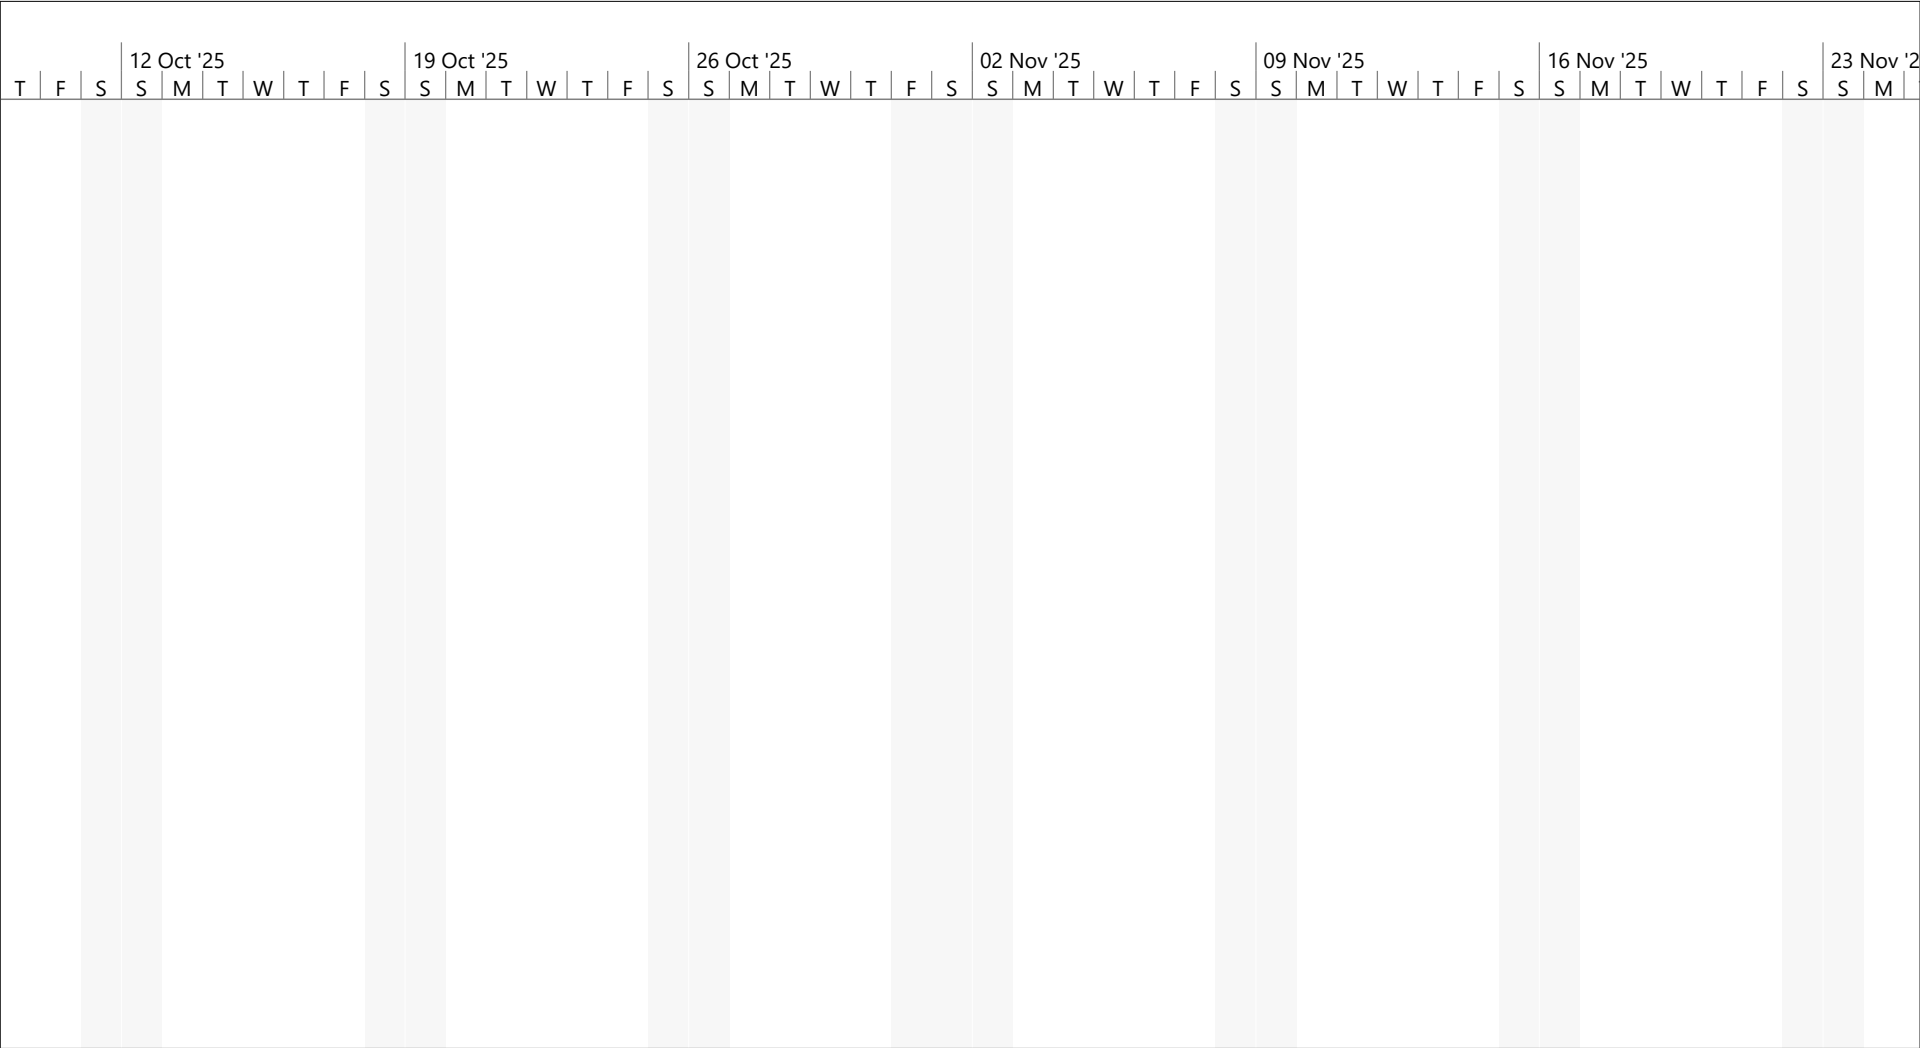


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

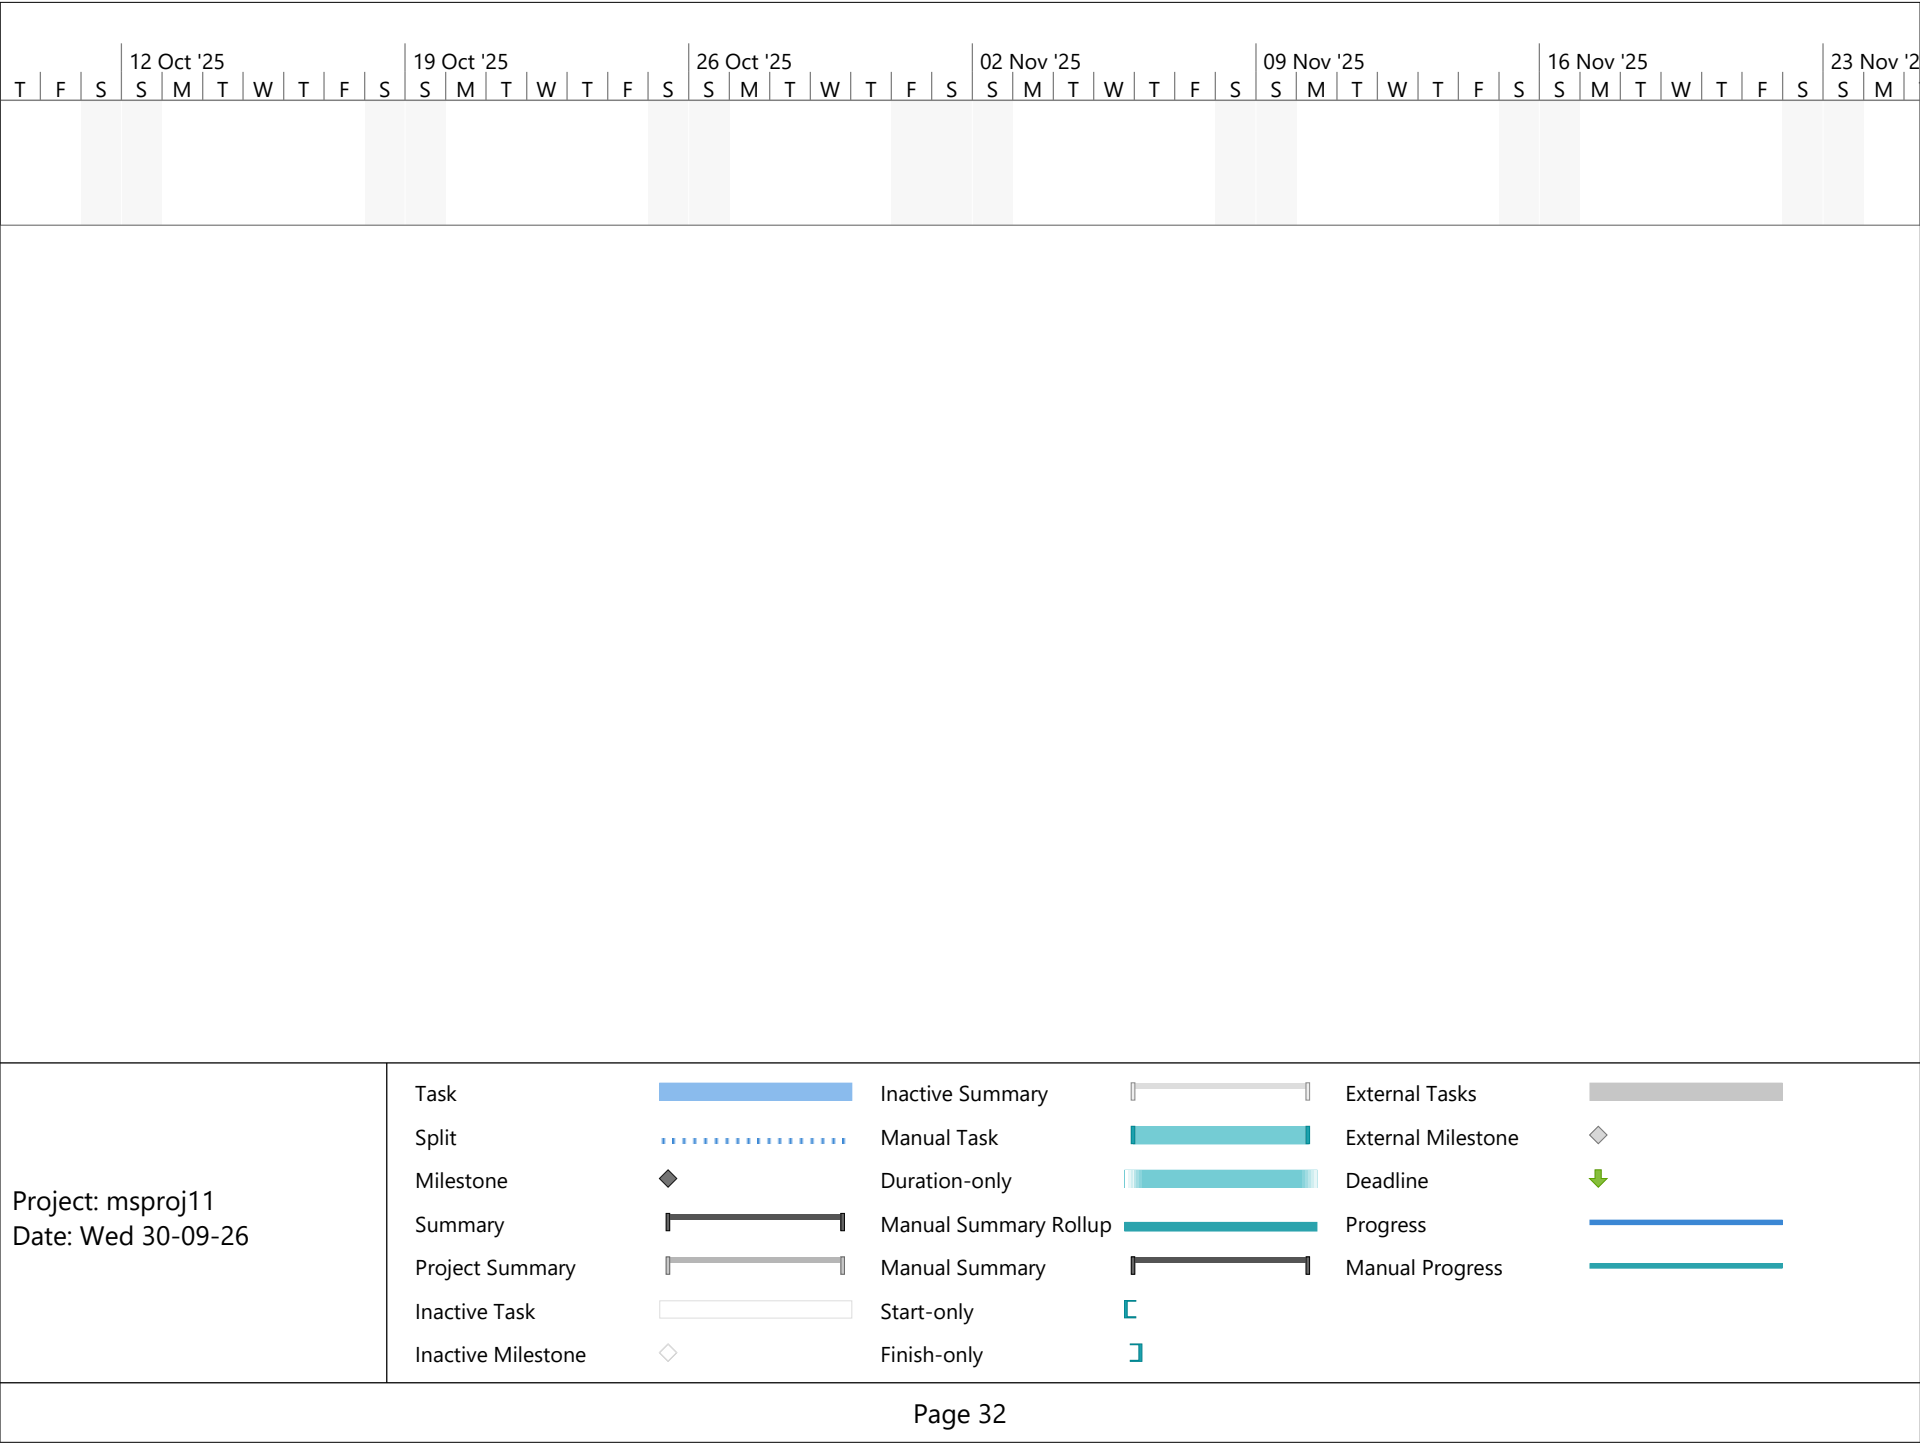

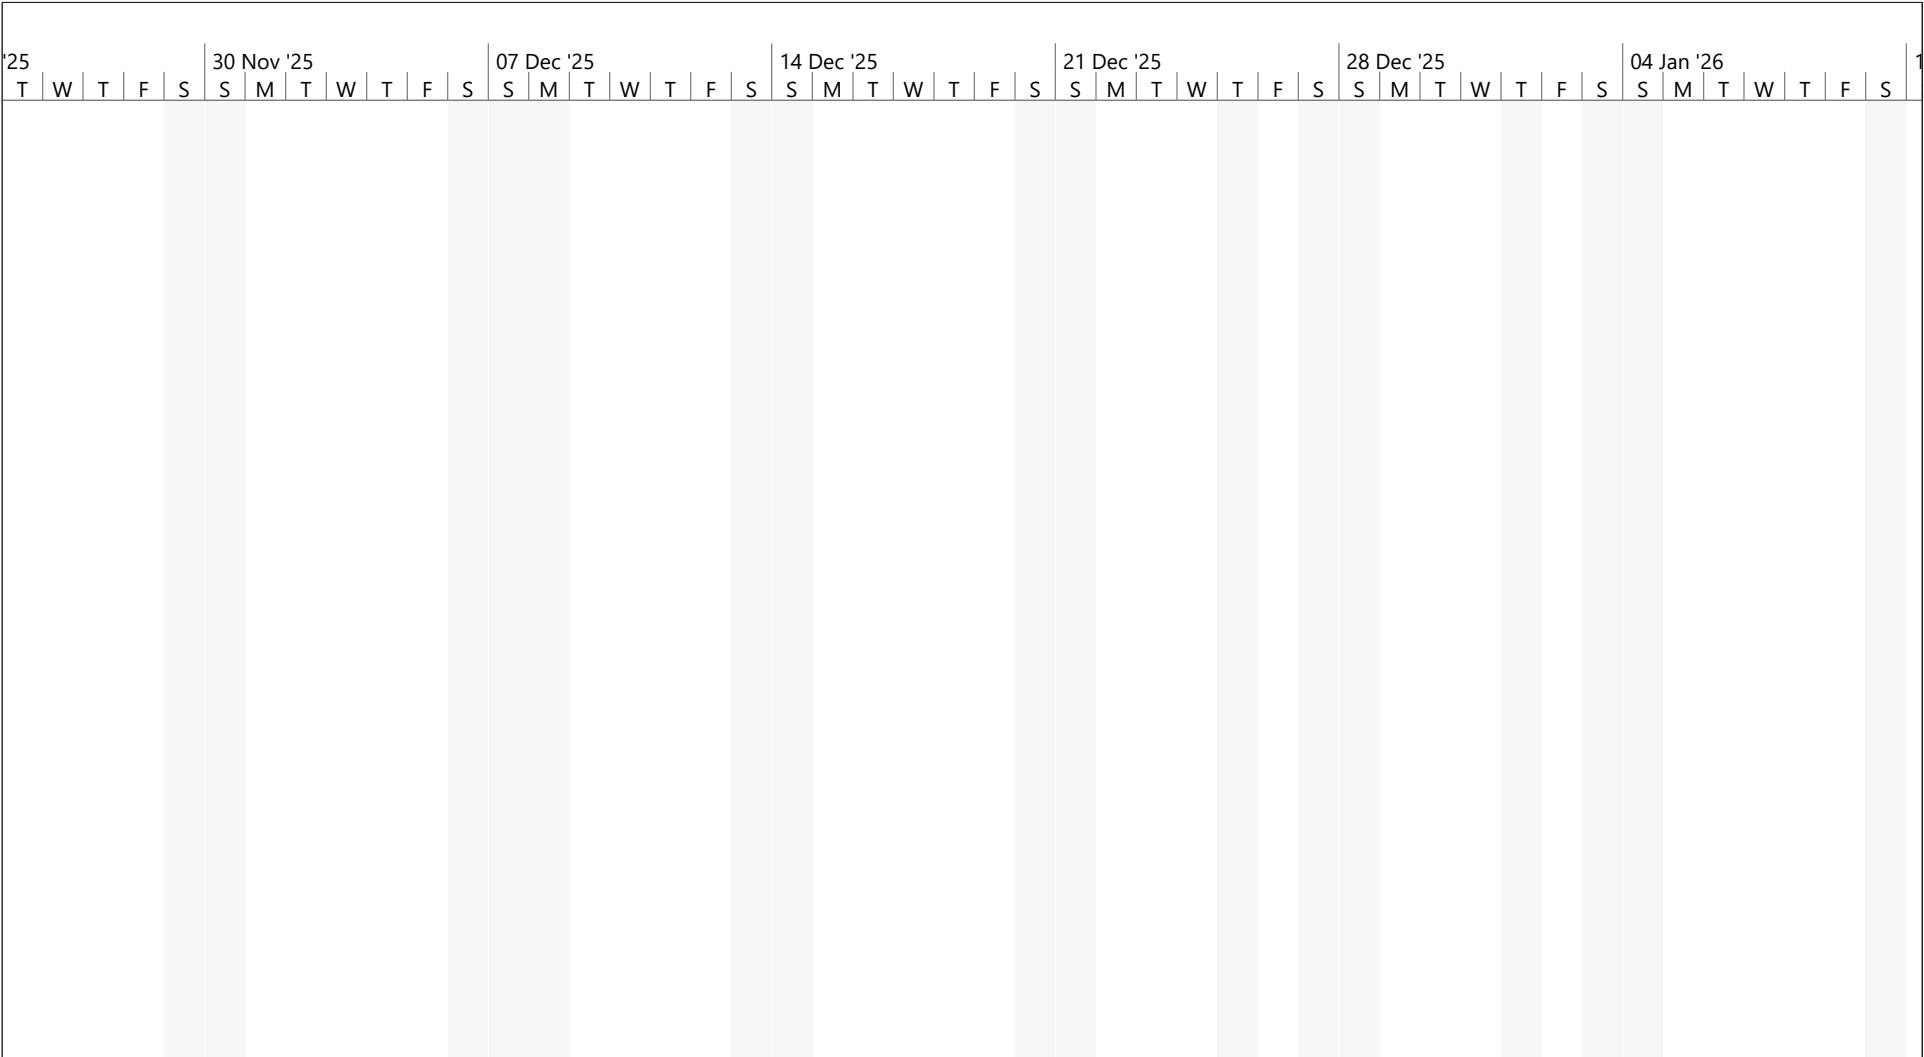

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

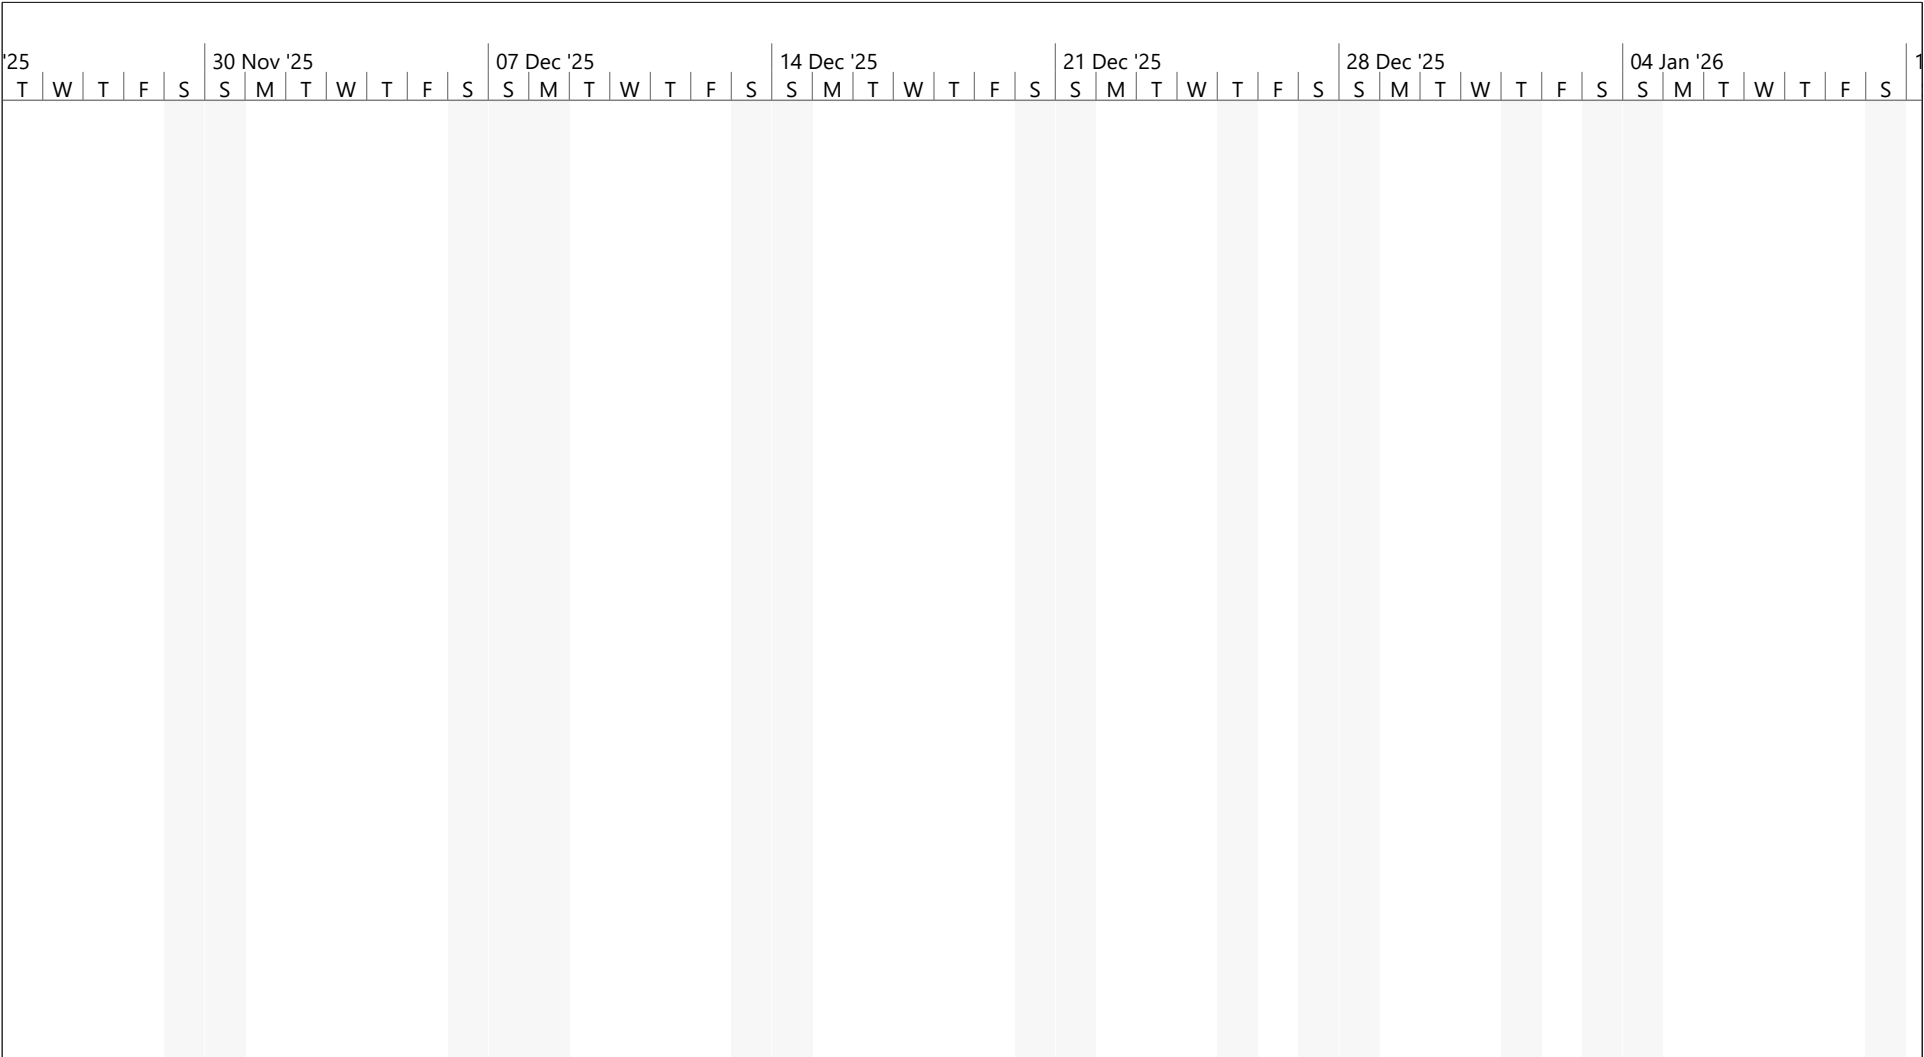

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

25
T

W

T

F

S

30 Nov '25
S

M

T

W

T

F

S

07 Dec '25
S

M

T

W

T

F

S

14 Dec '25
S

M

T

W

T

F

S

21 Dec '25
S

M

T

W

T

F

S

28 Dec '25
S

M

T

W

T

F

S

04 Jan '26
S

M

T

W

T

F

S

1

Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

25
T

W

T

F

S

30 Nov '25
S

M

T

W

T

F

S

07 Dec '25
S

M

T

W

T

F

S

14 Dec '25
S

M

T

W

T

F

S

21 Dec '25
S

M

T

W

T

F

S

28 Dec '25
S

M

T

W

T

F

S

04 Jan '26
S

M

T

W

T

F

S

1

Project: msproj11
Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline


Progress

Manual Progress

Page 36

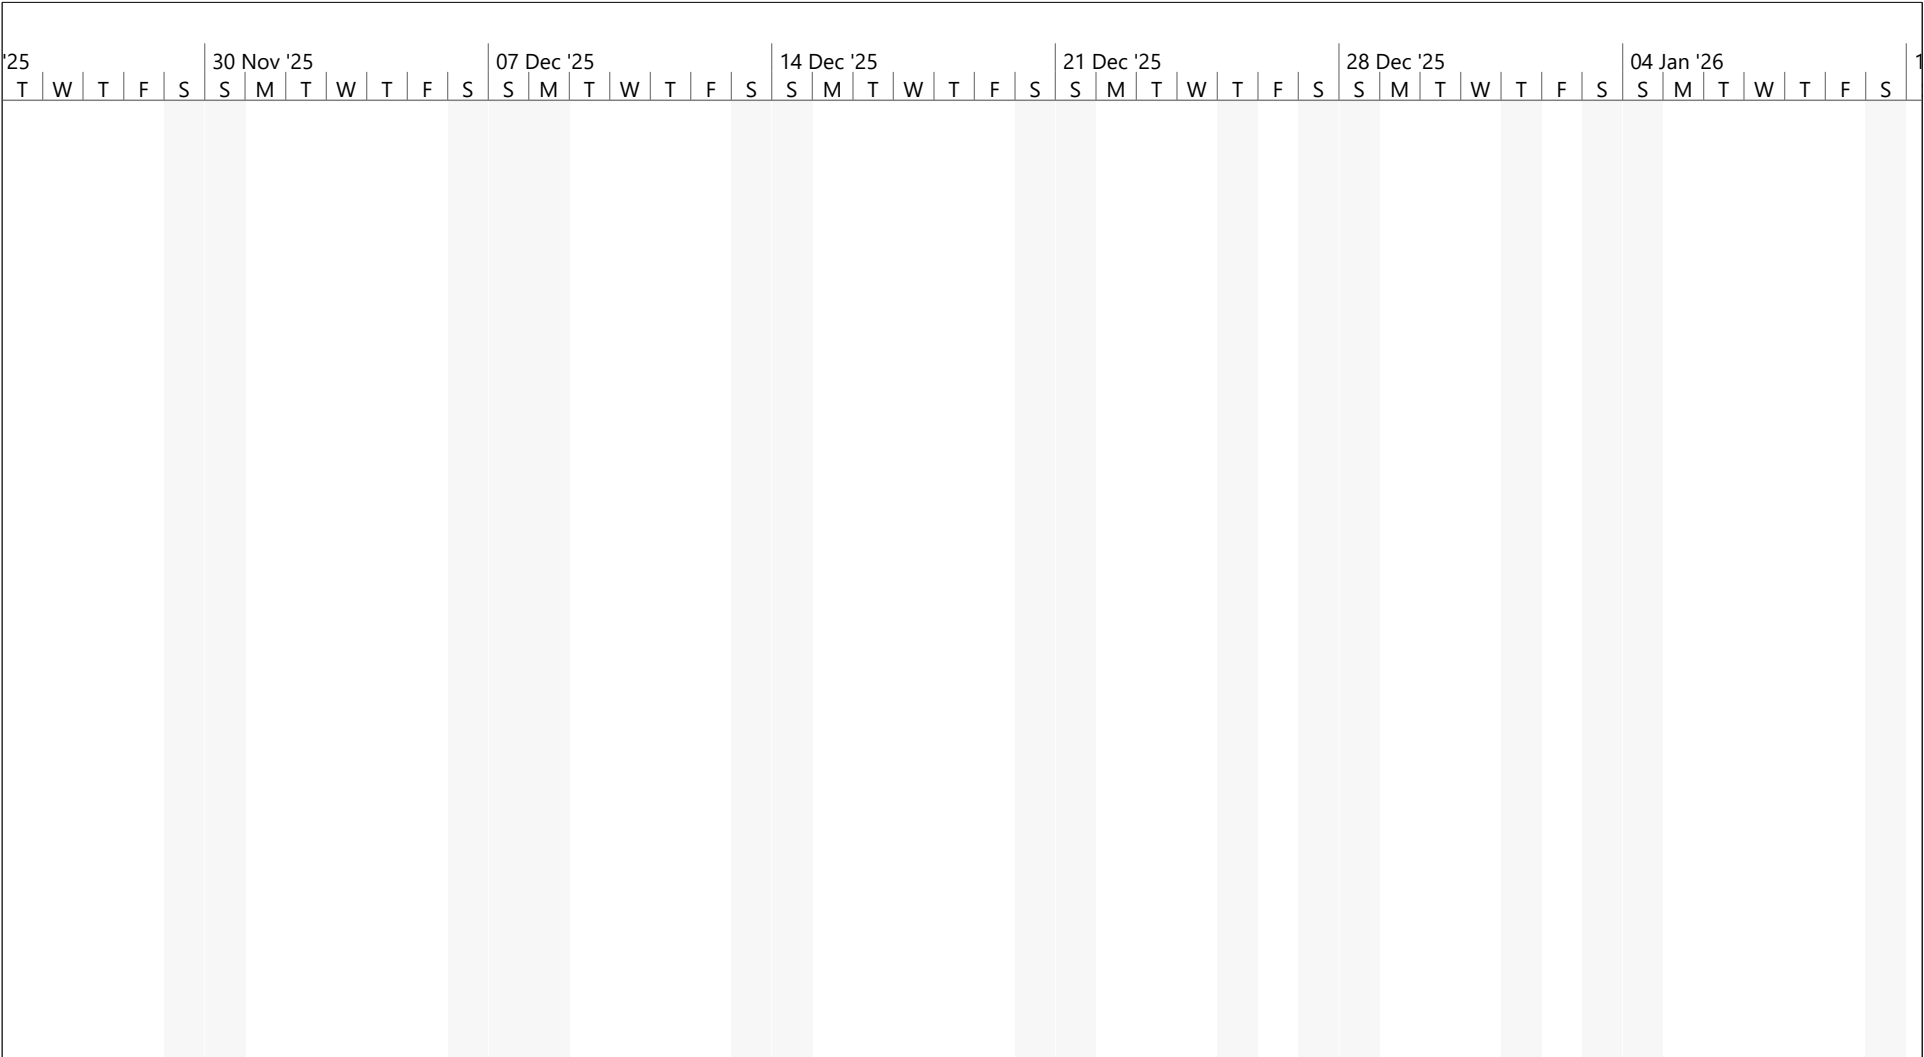

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

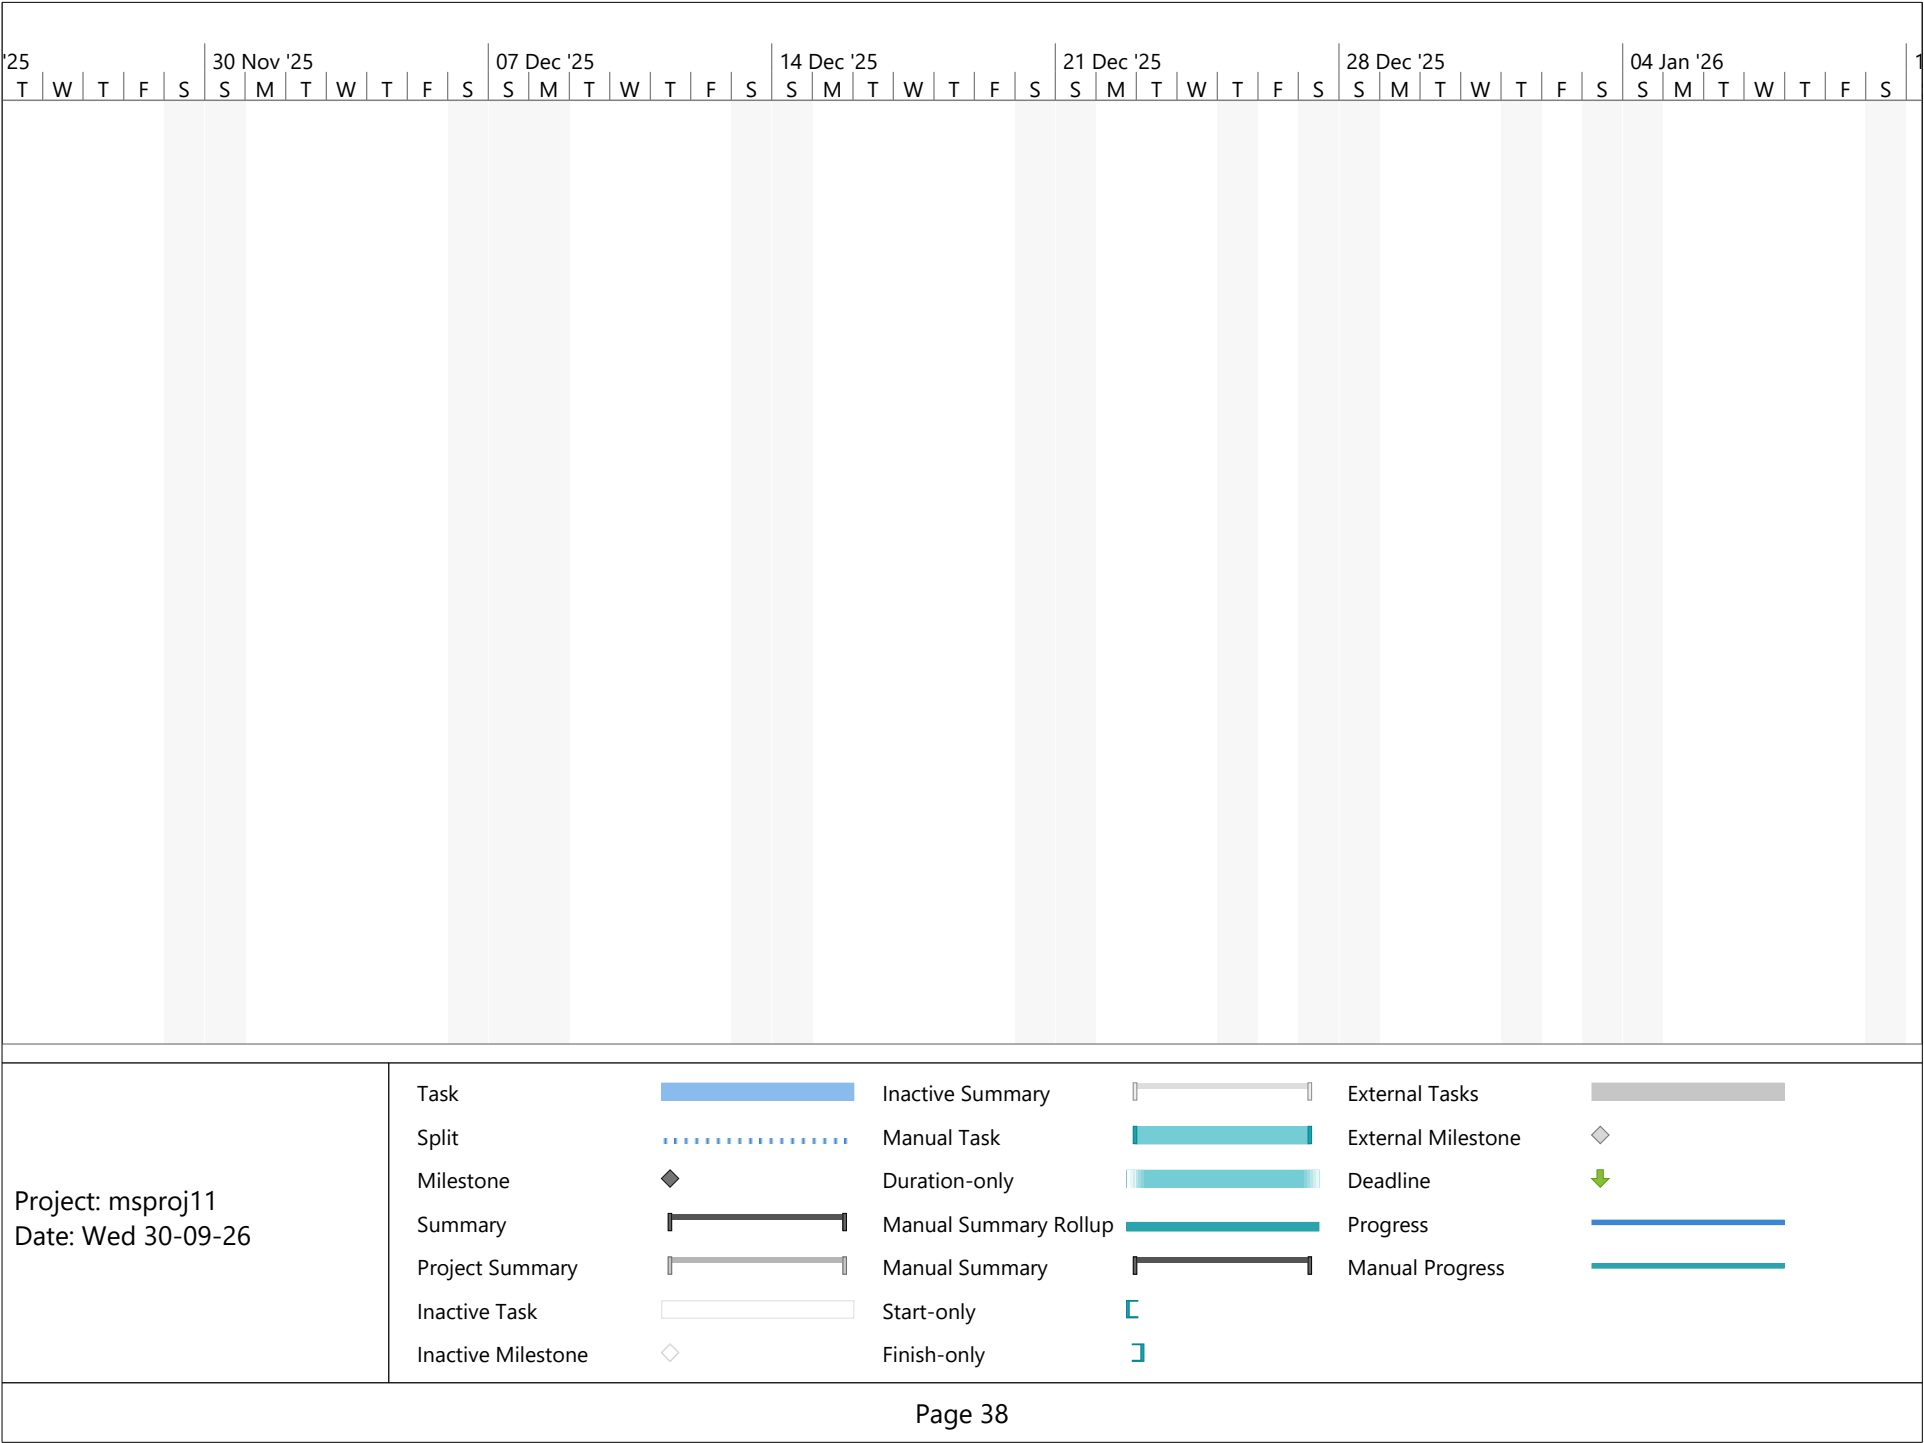

25
T

W

T

F

S

30 Nov '25
S

M

T

W

T

F

S

07 Dec '25
S

M

T

W

T

F

S

14 Dec '25
S

M

T

W

T

F

S

21 Dec '25
S

M

T

W

T

F

S

28 Dec '25
S

M

T

W

T

F

S

04 Jan '26
S

M

T

W

T

F

S

1

Project: msproj11
Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress



Manual Progress

Page 39

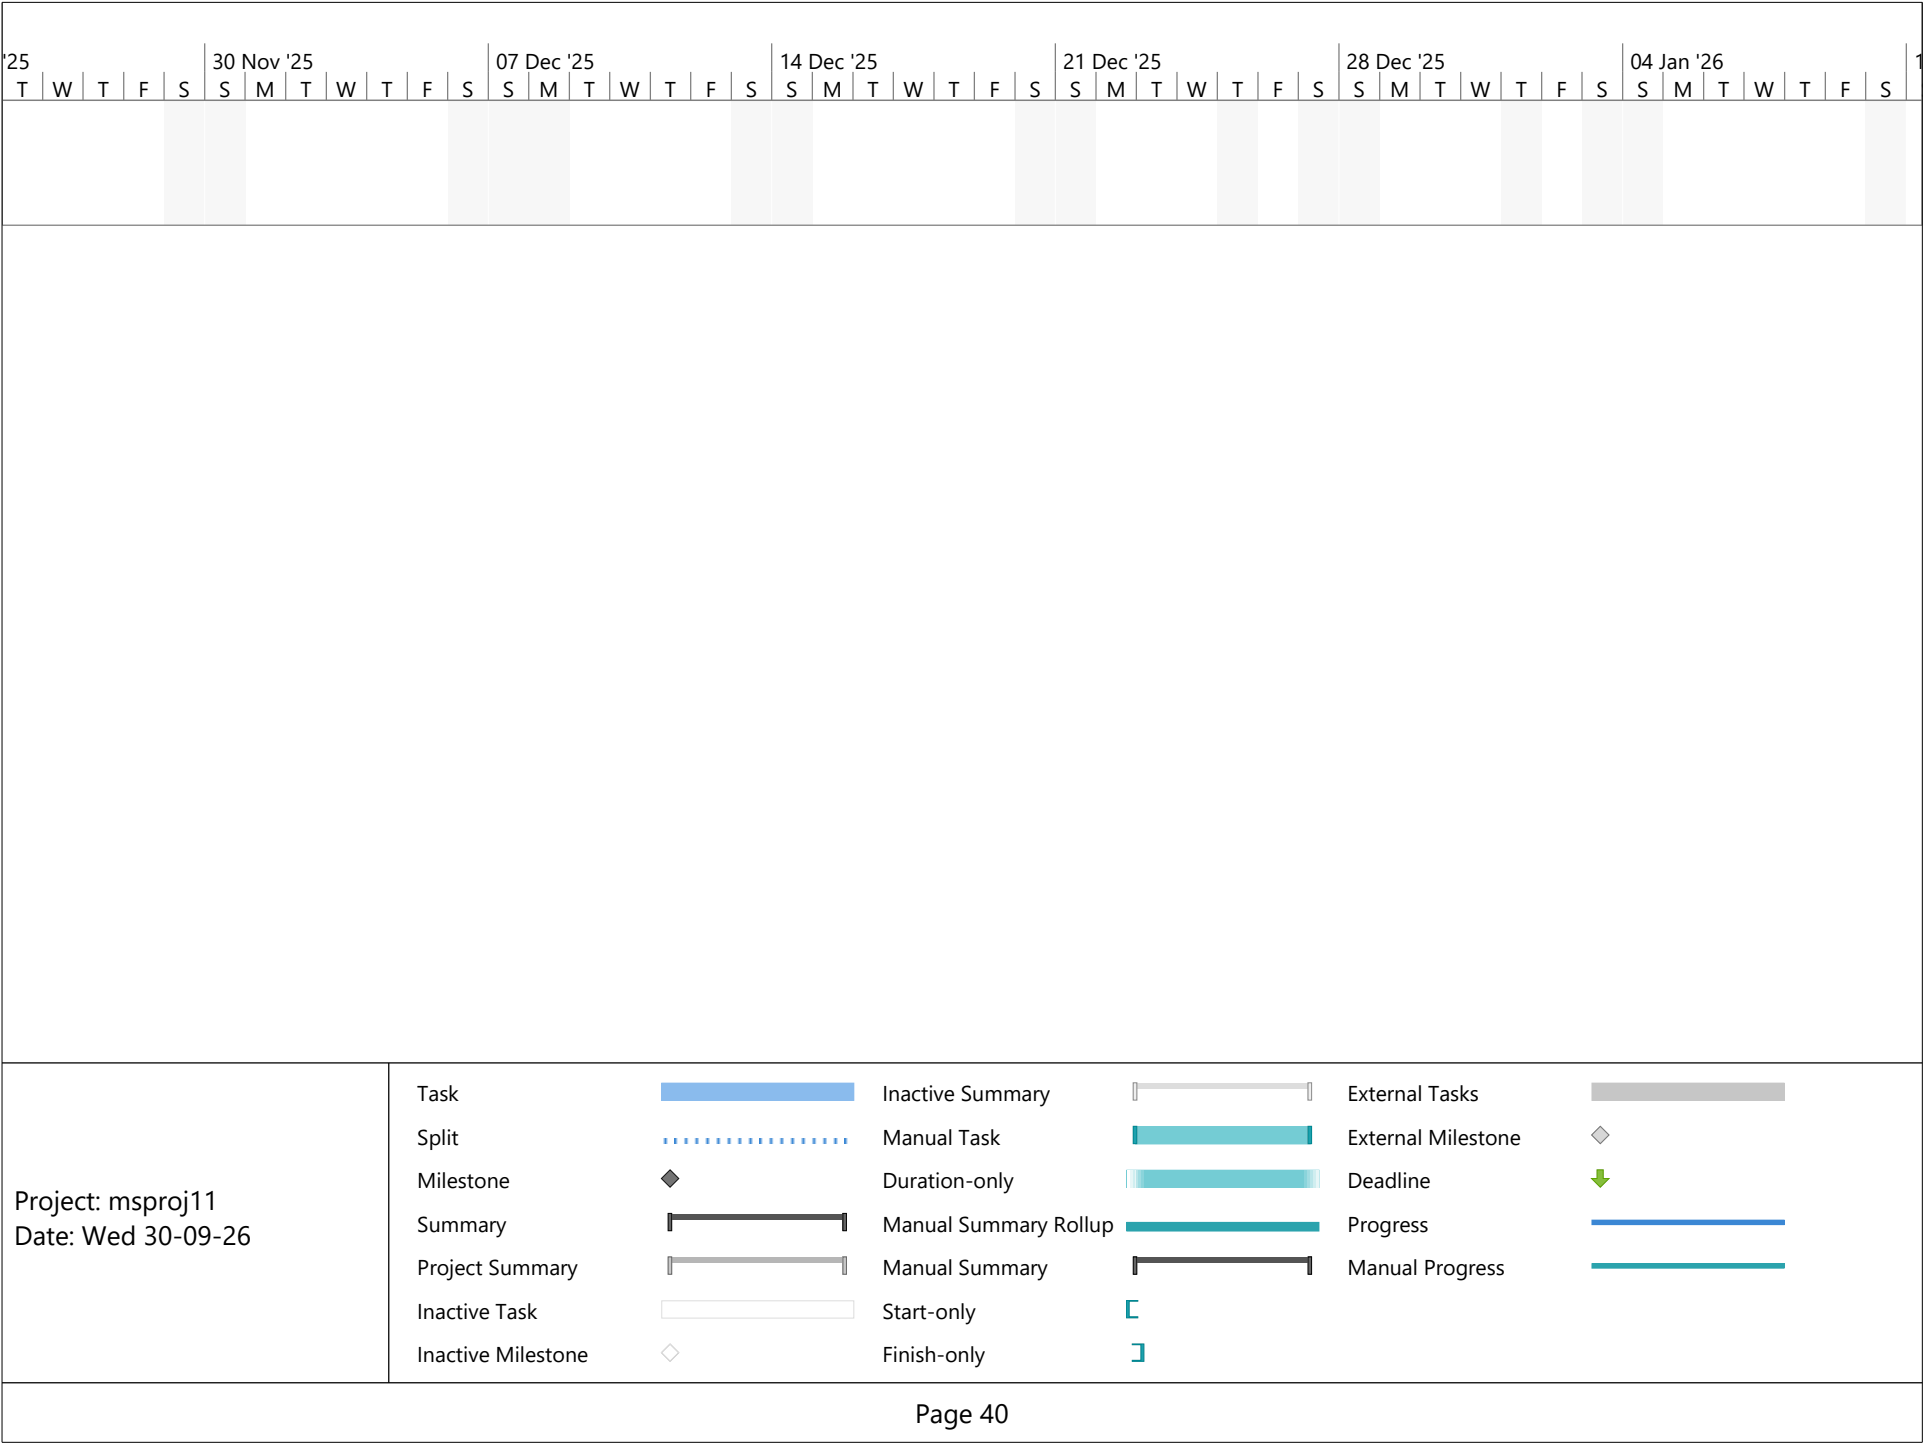

11 Jan '26 18 Jan '26 25 Jan '26 01 Feb '26 08 Feb '26 15 Feb '26 22 Feb '26
S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11 Jan '26

S

M

T

W

T

F

S

18 Jan '26

S

M

T

W

T

F

S

25 Jan '26

S

M

T

W

T

F

S

01 Feb '26

S

M

T

W

T

F

S

08 Feb '26

S

M

T

W

T

F

S

15 Feb '26

S

M

T

W

T

F

S

22 Feb '26

S

M



T

W

T

Project: msproj11

Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11 Jan '26

S

M

T

W

T

F

S

18 Jan '26

S

M

T

W

T

F

S

25 Jan '26

S

M

T

W

T

F

S

01 Feb '26

S

M

T

W

T

F

S

08 Feb '26

S

M

T

W

T

F

S

15 Feb '26

S

M

T

W

T

F

S

22 Feb '26

S

M



T

W

T

Project: msproj11

Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11 Jan '26

S

M

T

W

T

F

S

18 Jan '26

S

M

T

W

T

F

S

25 Jan '26

S

M

T

W

T

F

S

01 Feb '26

S

M

T

W

T

F

S

08 Feb '26

S

M

T

W

T

F

S

15 Feb '26

S

M

T

W

T

F

S

22 Feb '26

S

M



T

W

T

Project: msproj11

Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11 Jan '26

S

M

T

W

T

F

S

18 Jan '26

S

M

T

W

T

F

S

25 Jan '26

S

M

T

W

T

F

S

01 Feb '26

S

M

T

W

T

F

S

08 Feb '26

S

M

T

W

T

F

S

15 Feb '26

S

M

T

W

T

F

S

22 Feb '26

S

M

T

W

T

Project: msproj11
Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 45

11 Jan '26

S

M

T

W

T

F

S

18 Jan '26

S

M

T

W

T

F

S

25 Jan '26

S

M

T

W

T

F

S

01 Feb '26

S

M

T

W

T

F

S

08 Feb '26

S

M

T

W

T

F

S

15 Feb '26

S

M

T

W

T

F

S

22 Feb '26

S

M



T

W

T



Project: msproj11


Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11 Jan '26							18 Jan '26							25 Jan '26							01 Feb '26							08 Feb '26							15 Feb '26							22 Feb '26				
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T							


Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			





Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

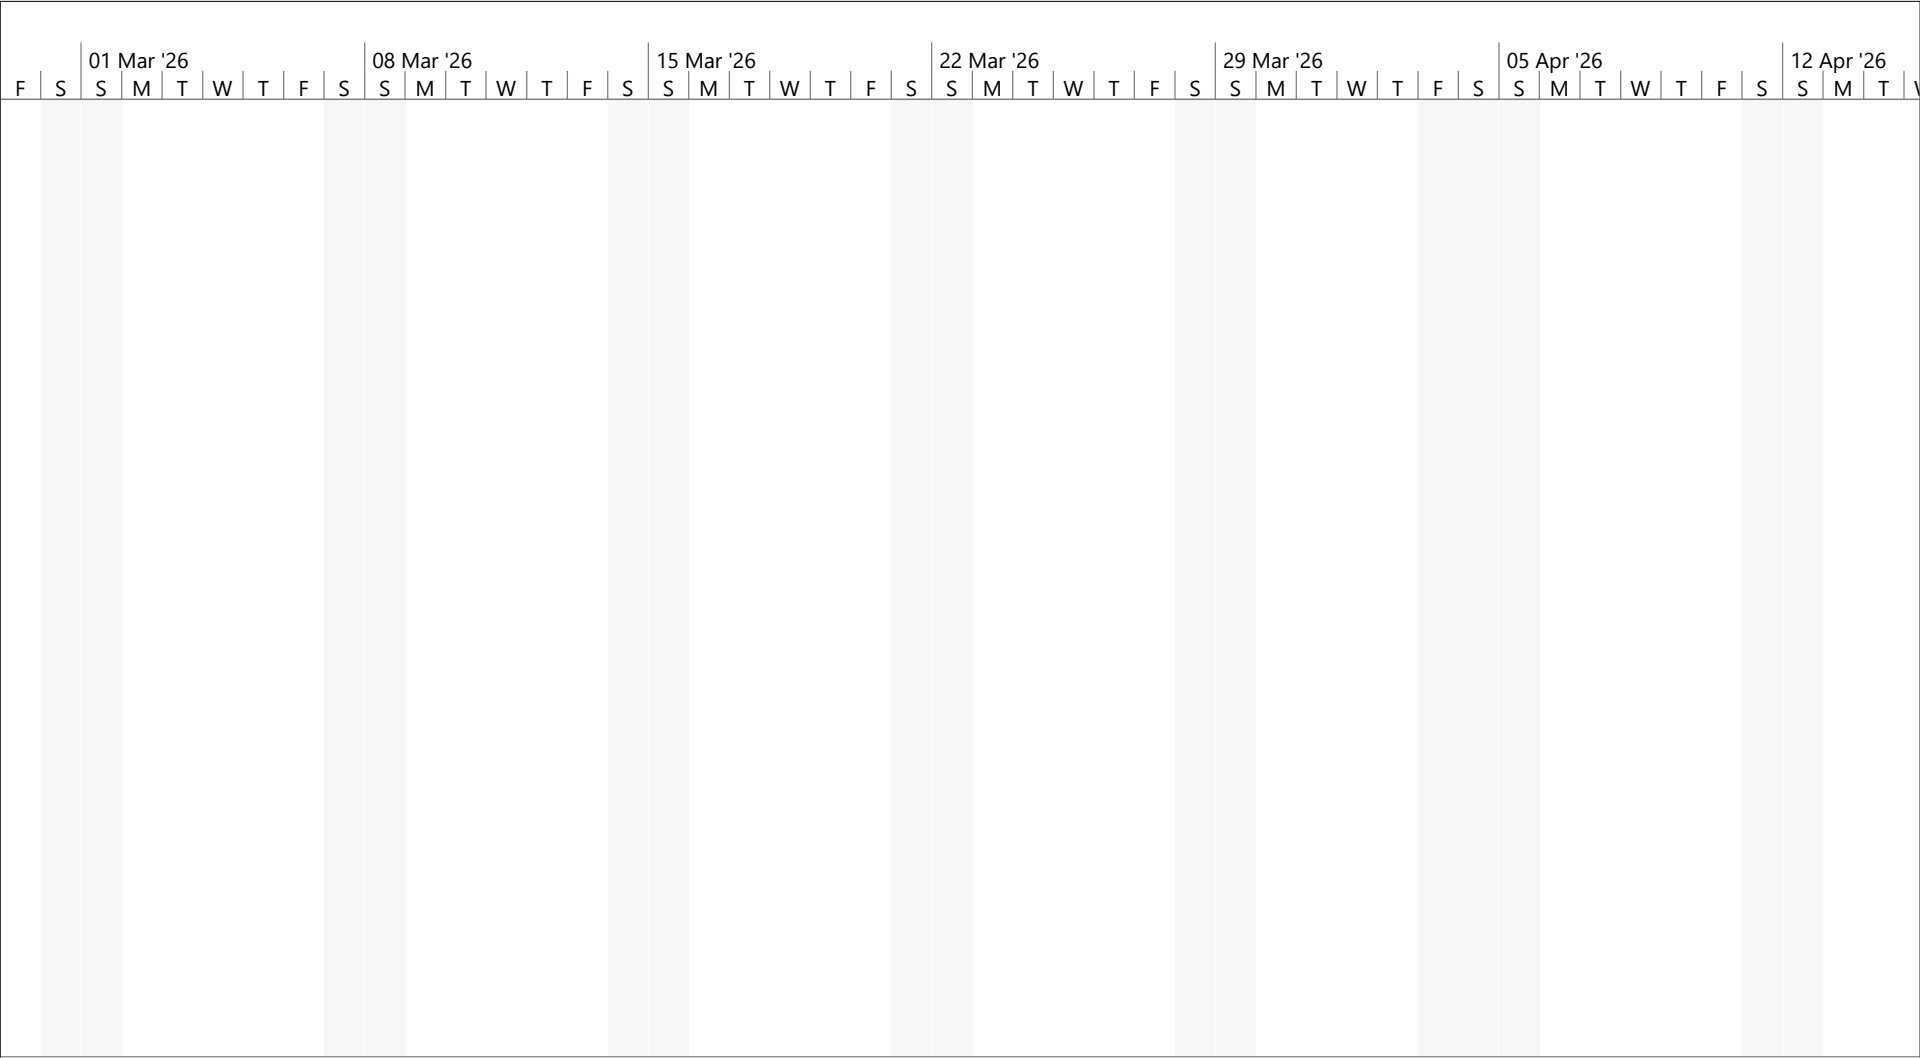


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

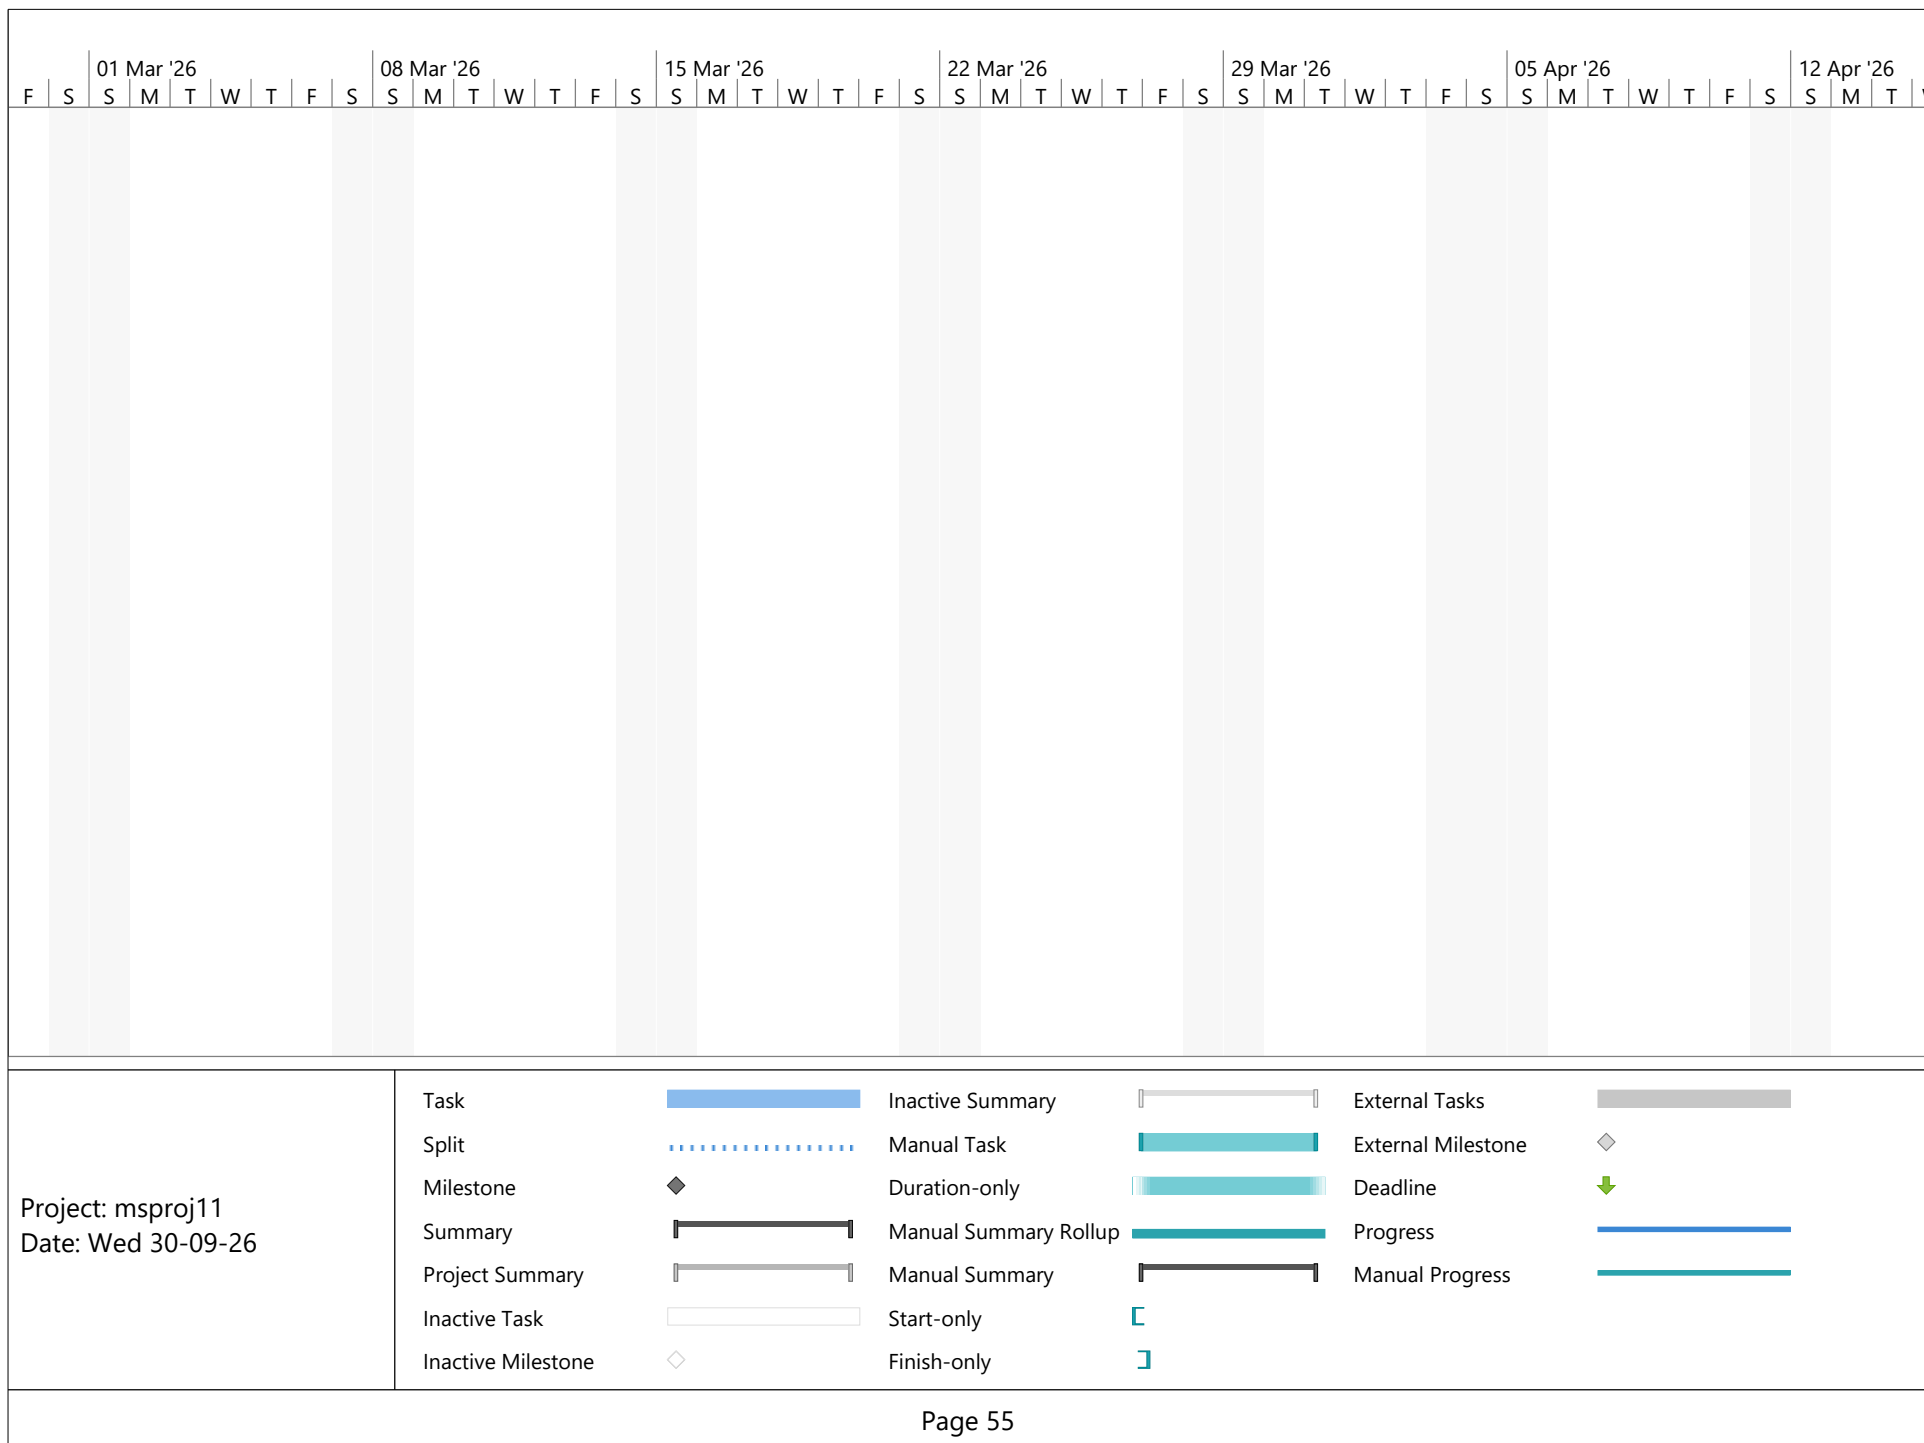


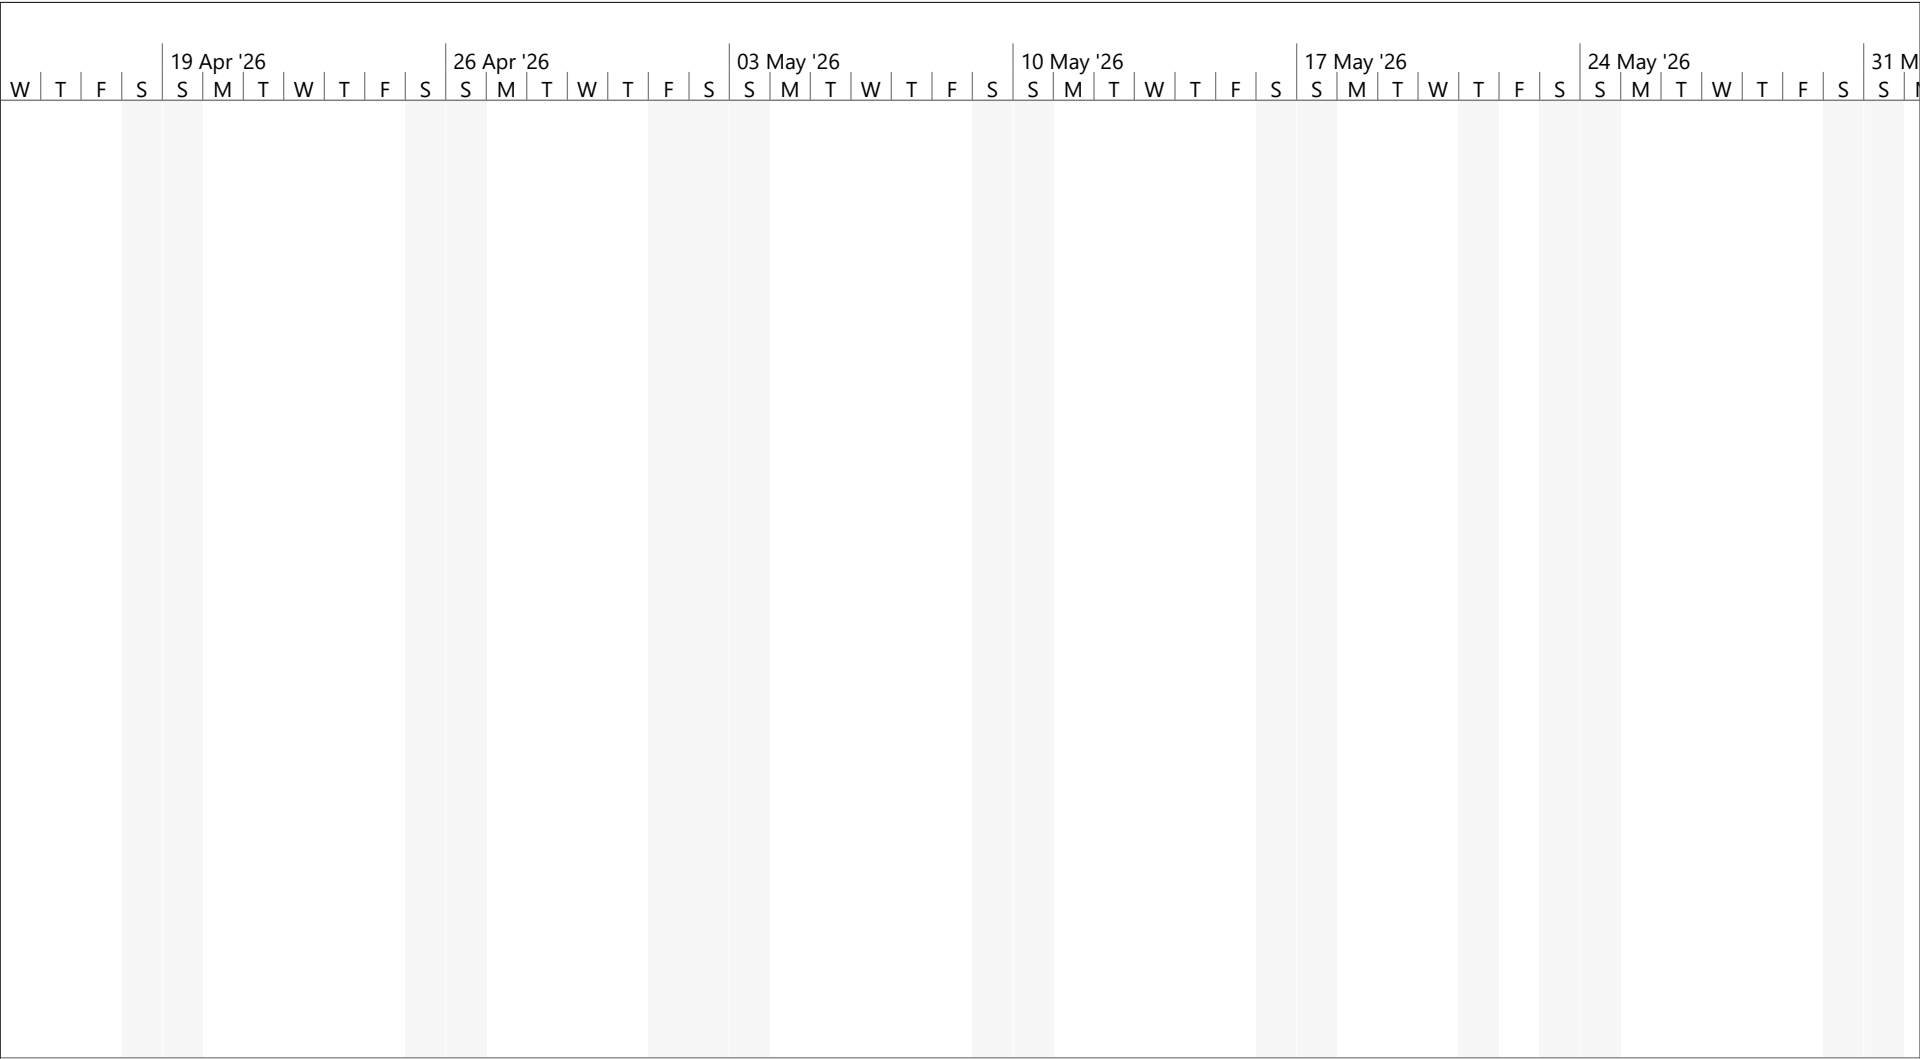

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

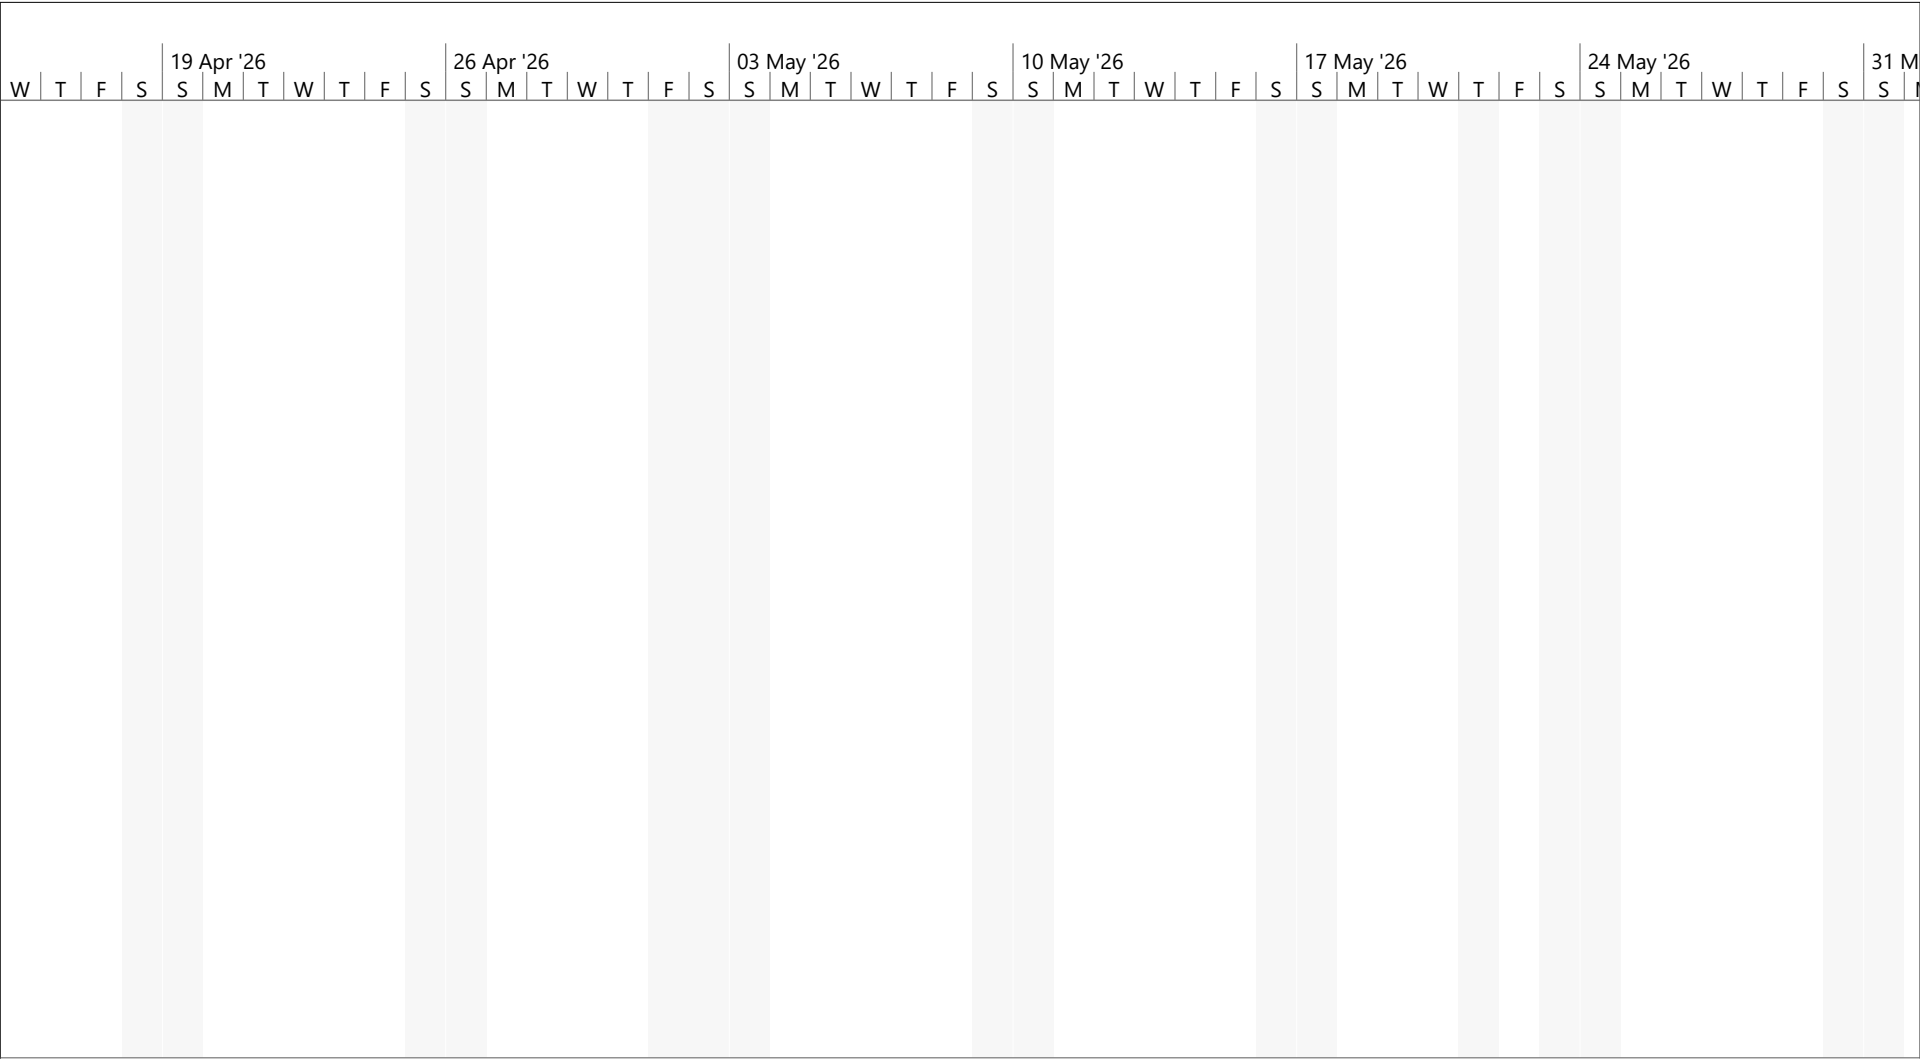

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

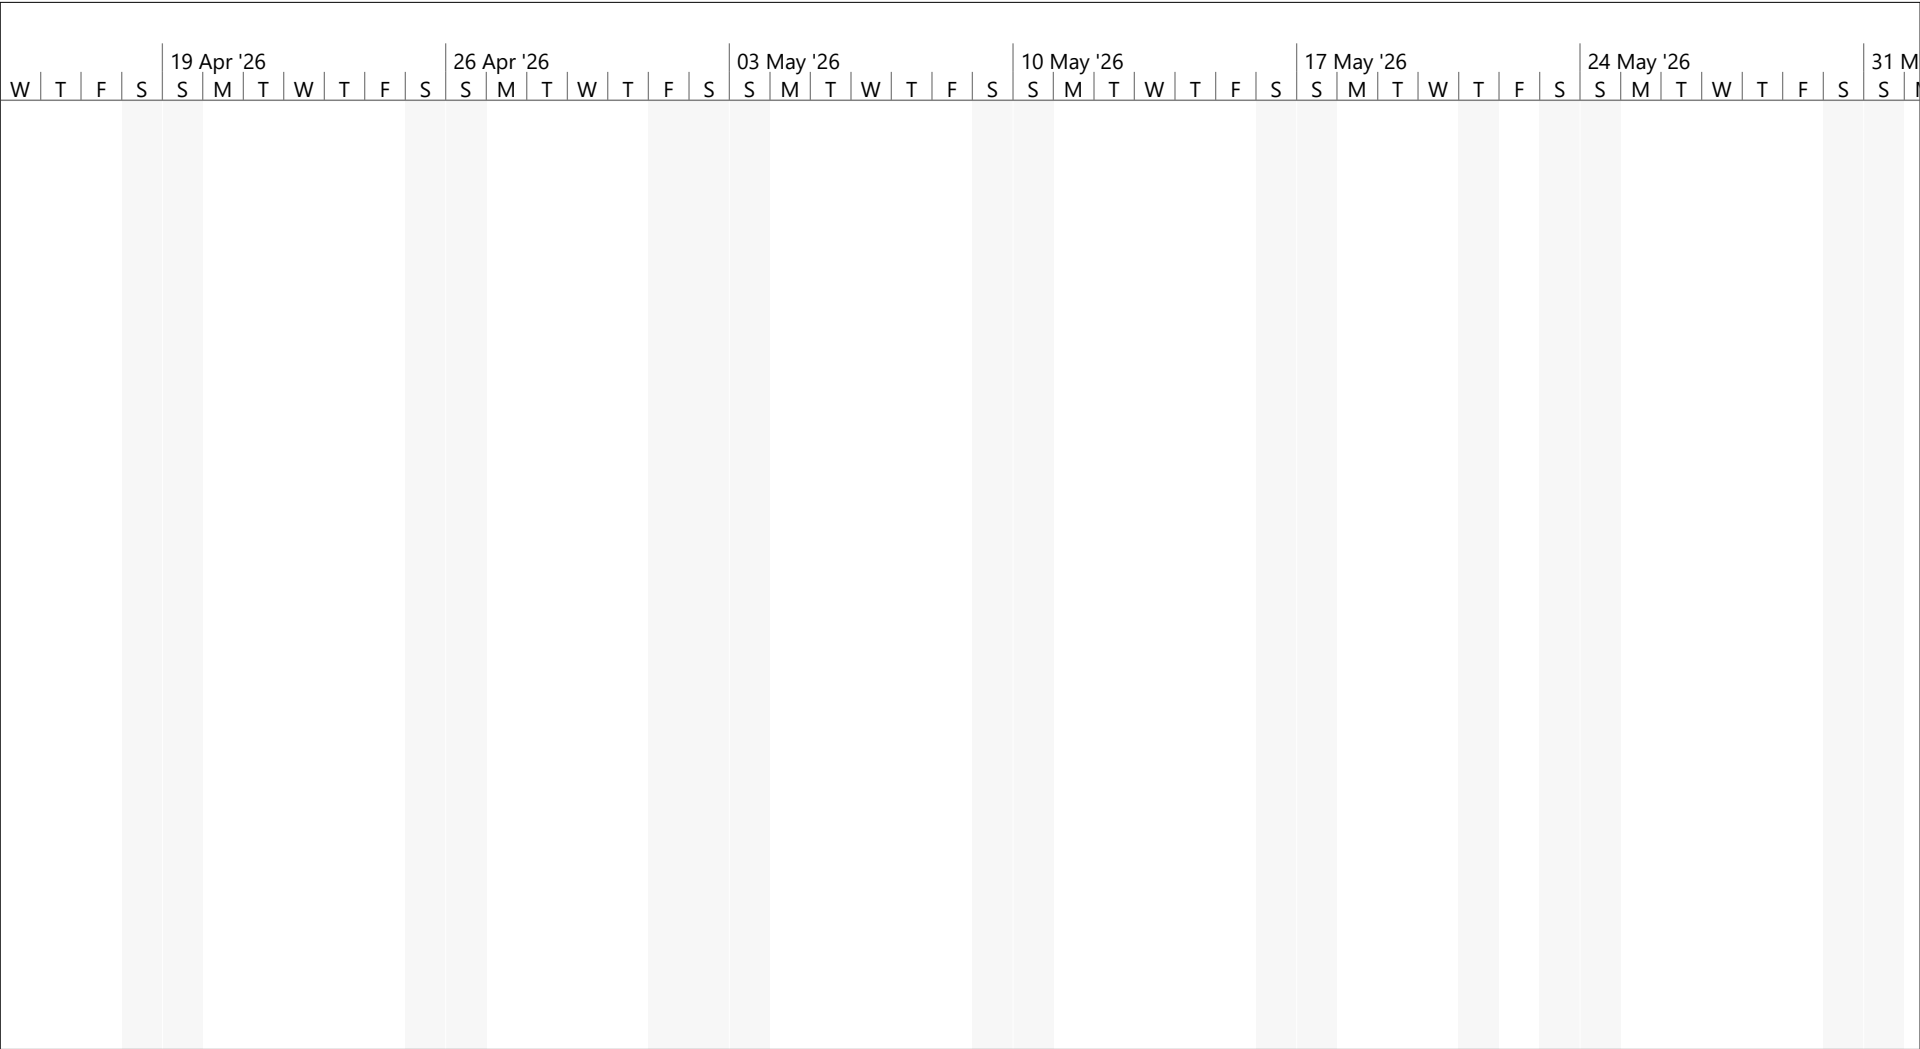

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

May '26

M | T | W | T | F | S

07 Jun '26

S | M | T | W | T | F | S

14 Jun '26

S | M | T | W | T | F | S

21 Jun '26

S | M | T | W | T | F | S

28 Jun '26


S | M | T | W | T | F | S

05 Jul '26

S | M | T | W | T | F | S

12 Jul '26

S | M | T | W | T | F

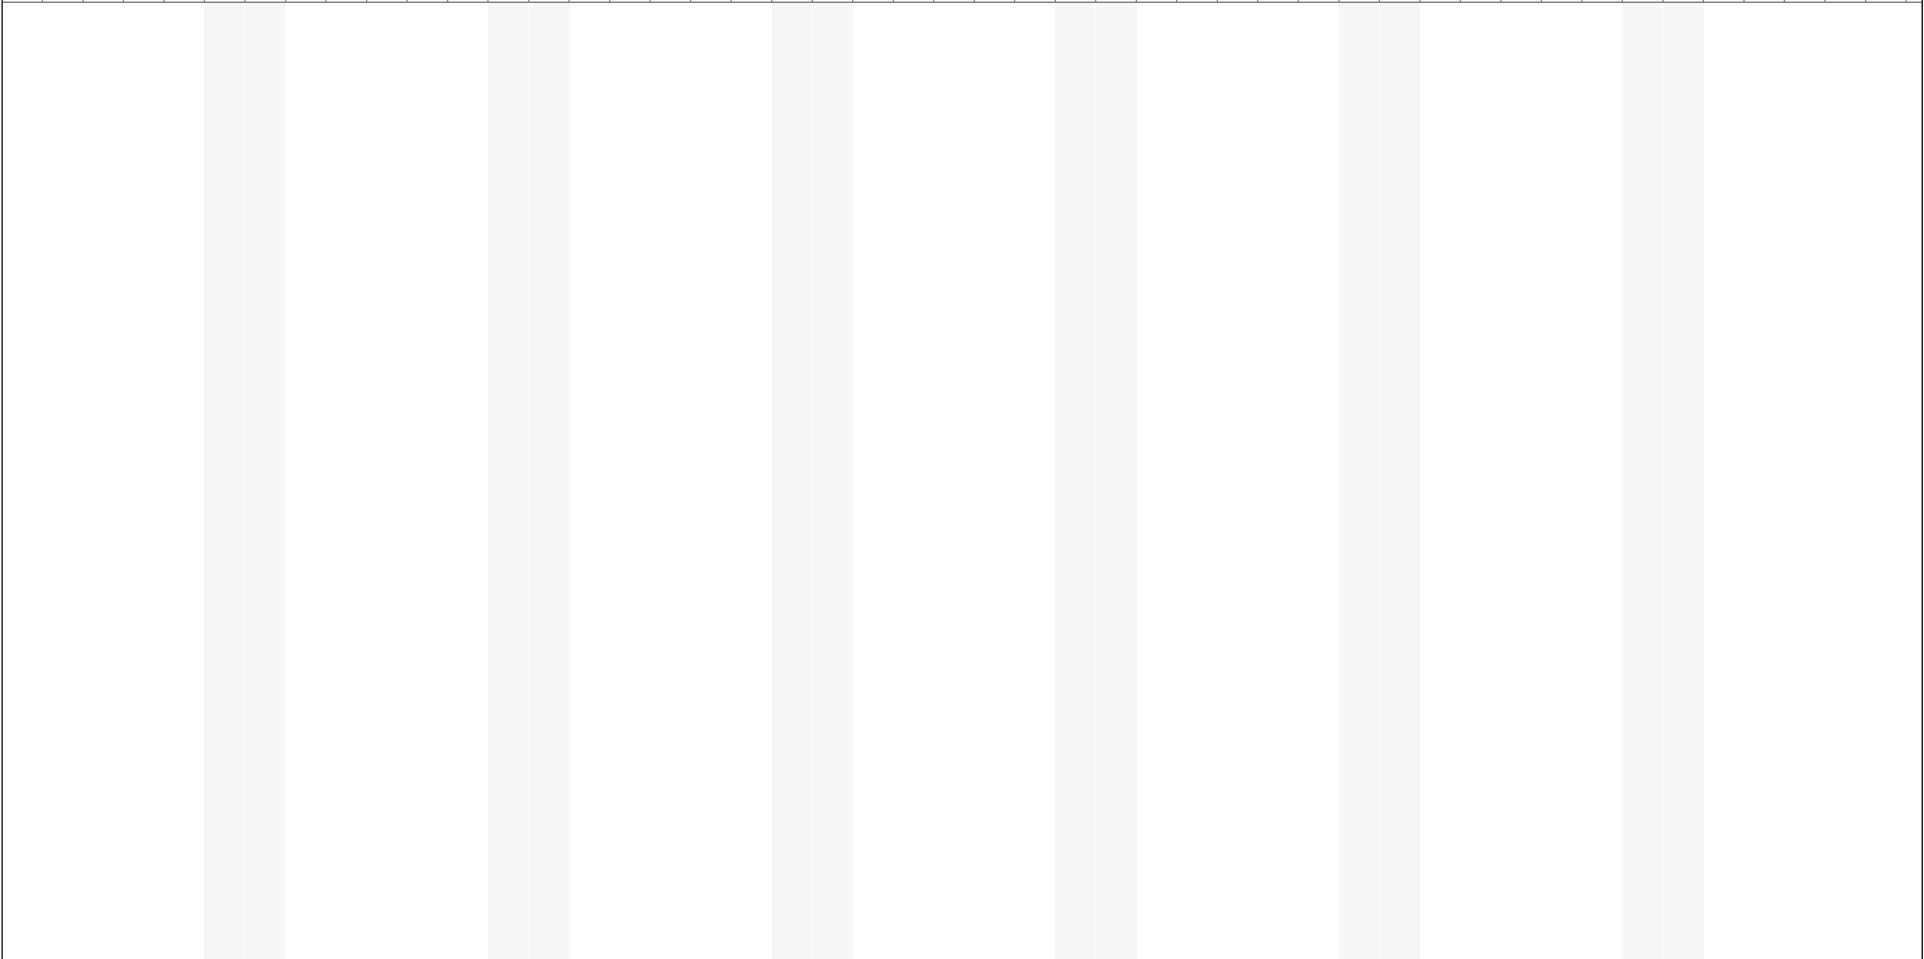

Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

May '26

M

T

W

T

F

S

07 Jun '26

S

M

T

W

T

F

S

14 Jun '26

S

M

T

W

T

F

S

21 Jun '26

S

M

T

W

T

F

S

28 Jun '26

S

M

T

W

T

F

S

05 Jul '26

S

M

T

W

T

F

S

12 Jul '26

S


M

T

W

T

F

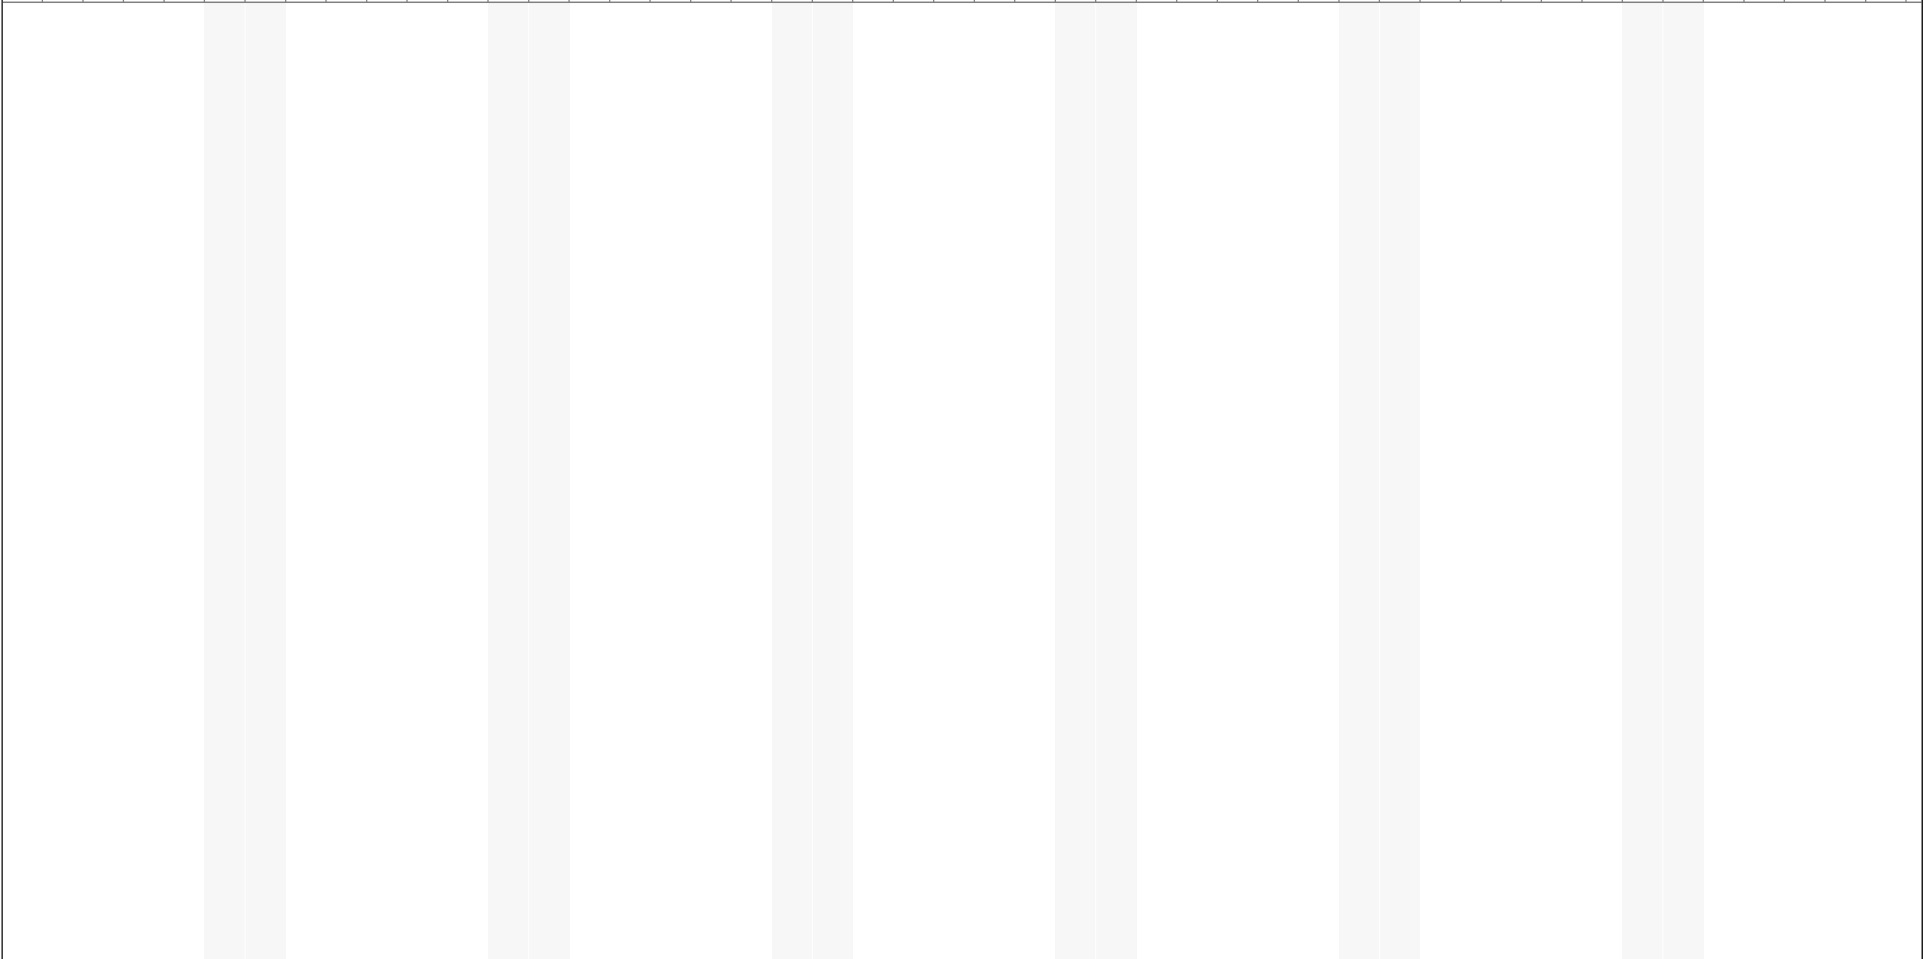

Project: msproj11
Date: Wed 30-09-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

May '26

M

T

W

T

F

S

07 Jun '26

S

M

T

W

T

F

S

14 Jun '26

S

M

T

W

T

F

S

21 Jun '26

S

M

T

W

T

F

S

28 Jun '26

S

M

T

W

T

F

S

05 Jul '26

S

M

T

W

T

F

S

12 Jul '26

S


M



T

W

T

F

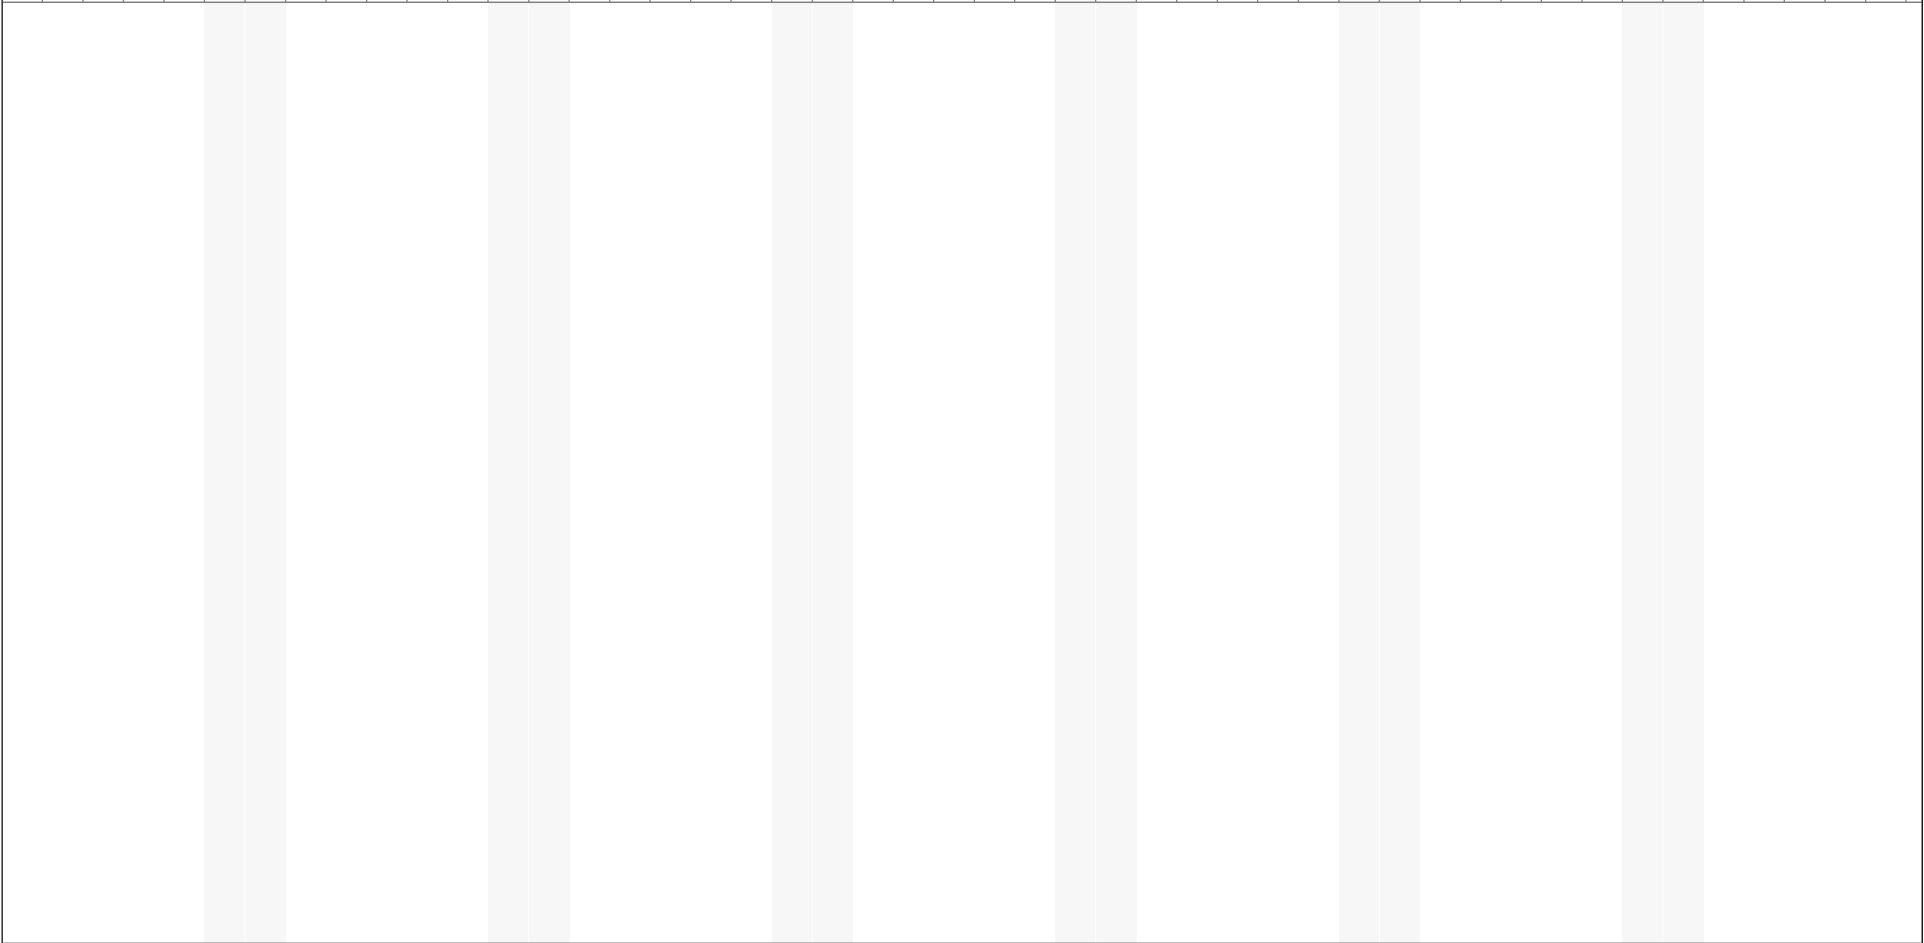

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

May '26

M

T

W

T

F

S

07 Jun '26

S

M

T

W

T

F

S

14 Jun '26

S

M

T

W

T

F

S

21 Jun '26

S

M

T

W

T

F

S

28 Jun '26

S

M

T

W

T

F

S

05 Jul '26

S

M

T

W

T

F

S

12 Jul '26

S


M


T


W

T

F

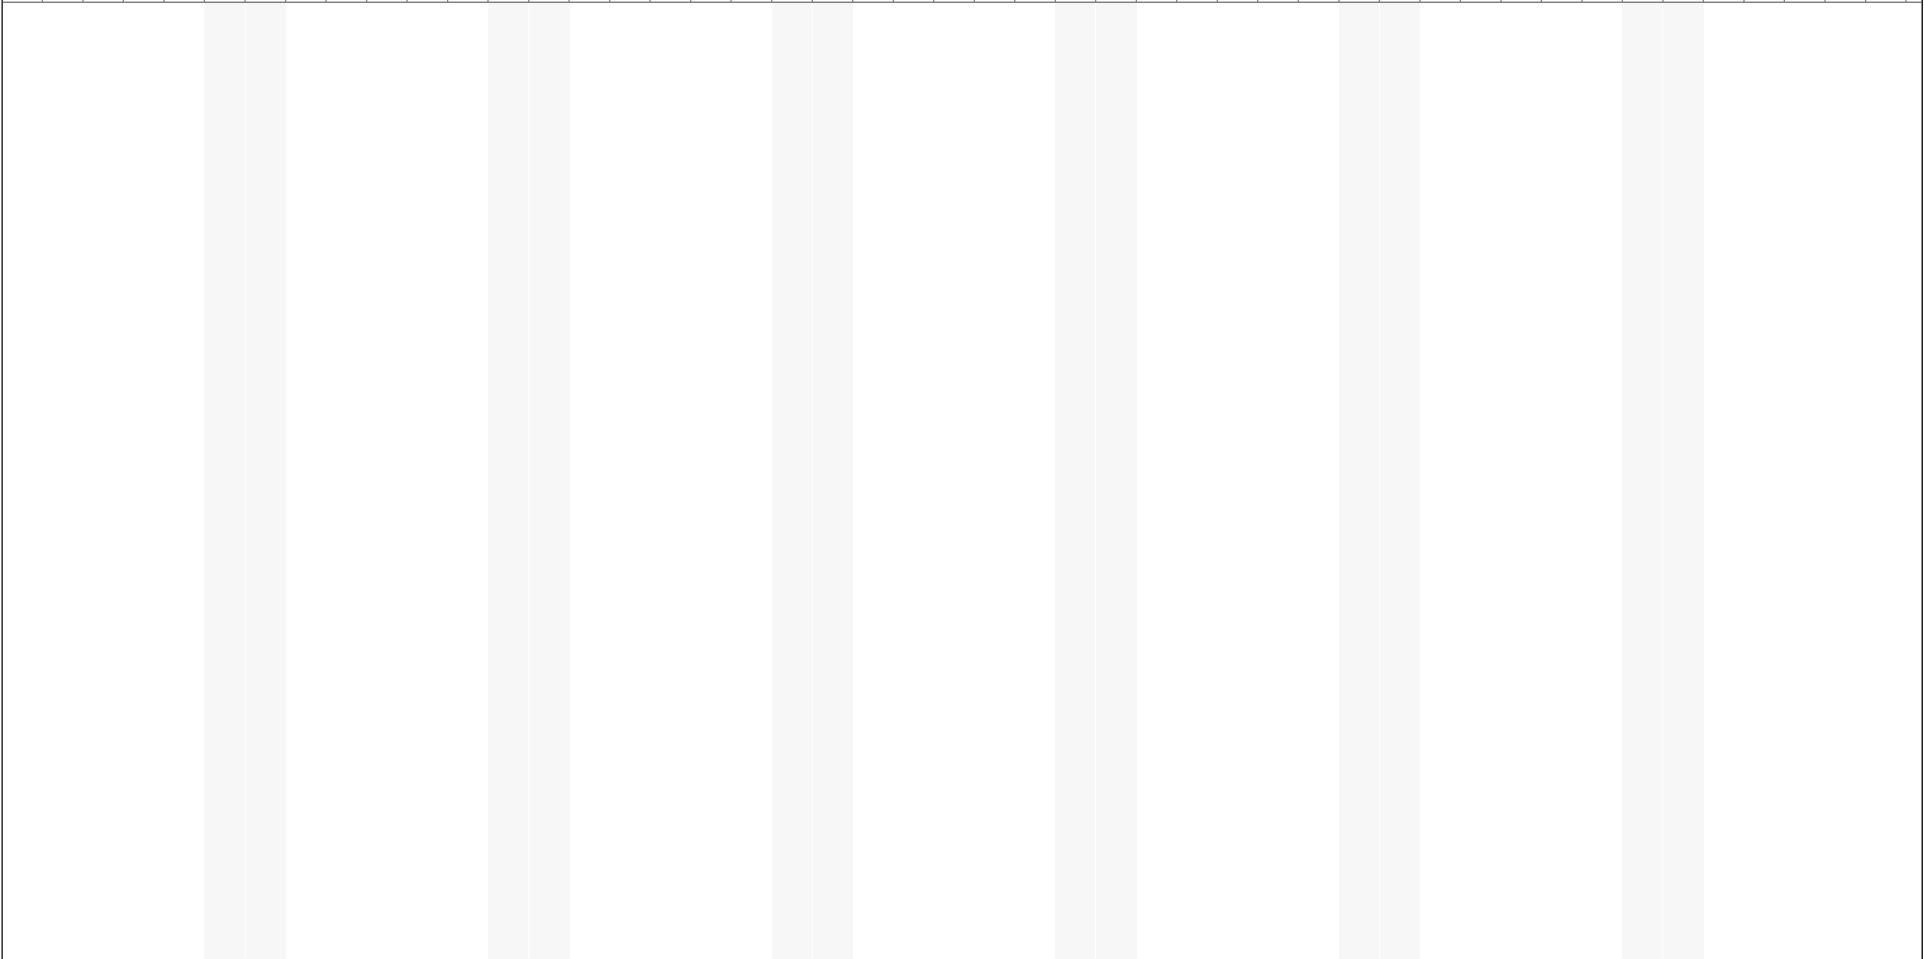

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

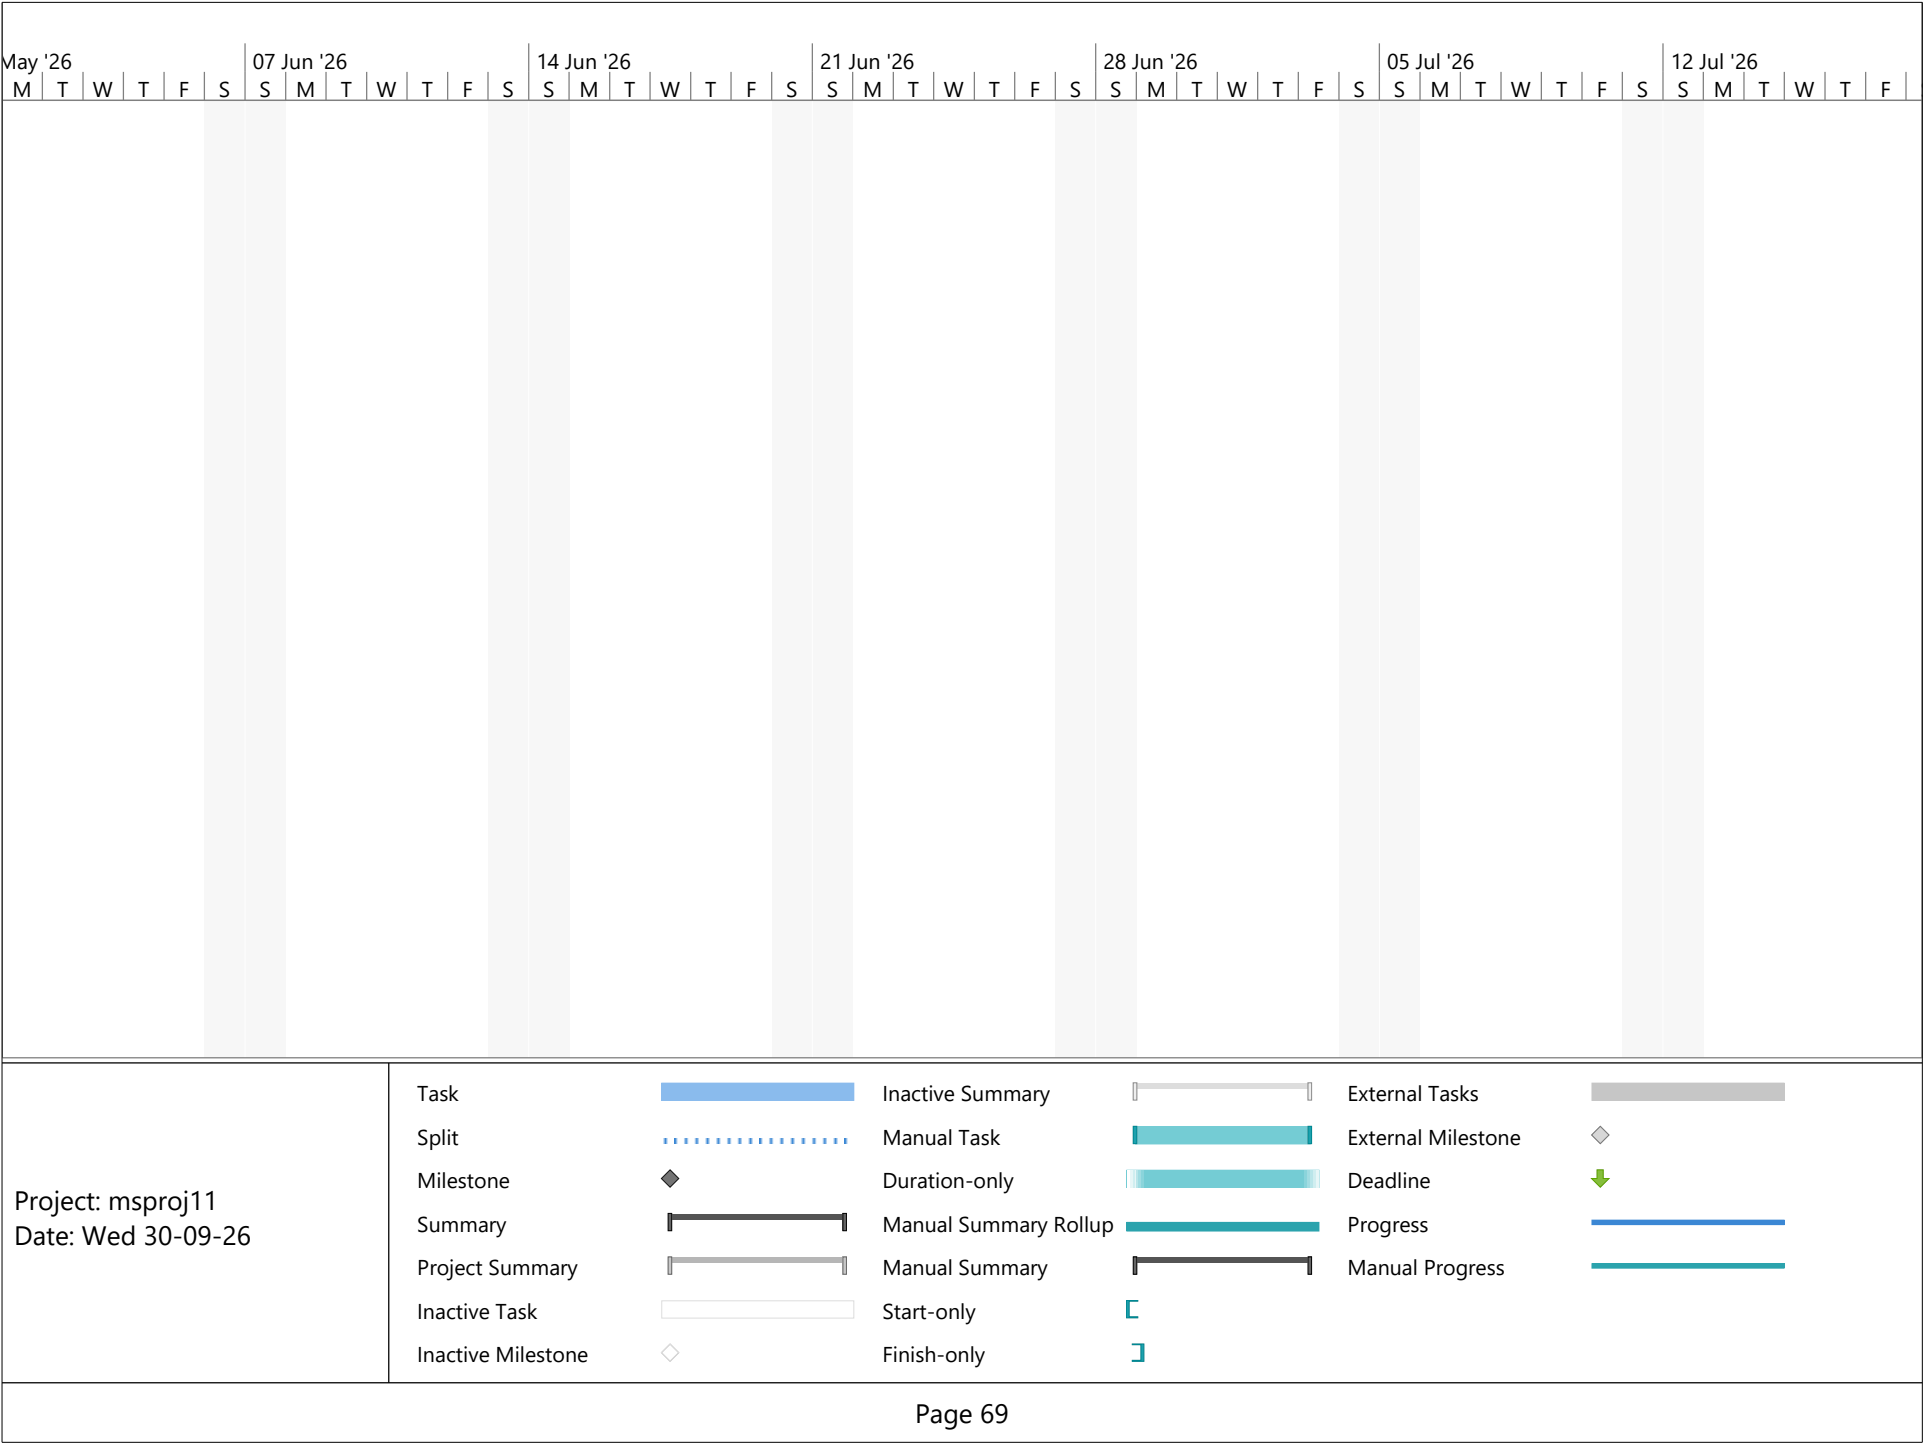

Page 69

May '26

M

T

W

T

F

S

07 Jun '26

S

M

T

W

T

F

S

14 Jun '26

S

M

T

W

T

F

S

21 Jun '26

S

M

T

W

T

F

S

28 Jun '26

S

M

T

W

T

F

S

05 Jul '26

S

M

T

W

T

F

S

12 Jul '26

S


M



T

W

T

F

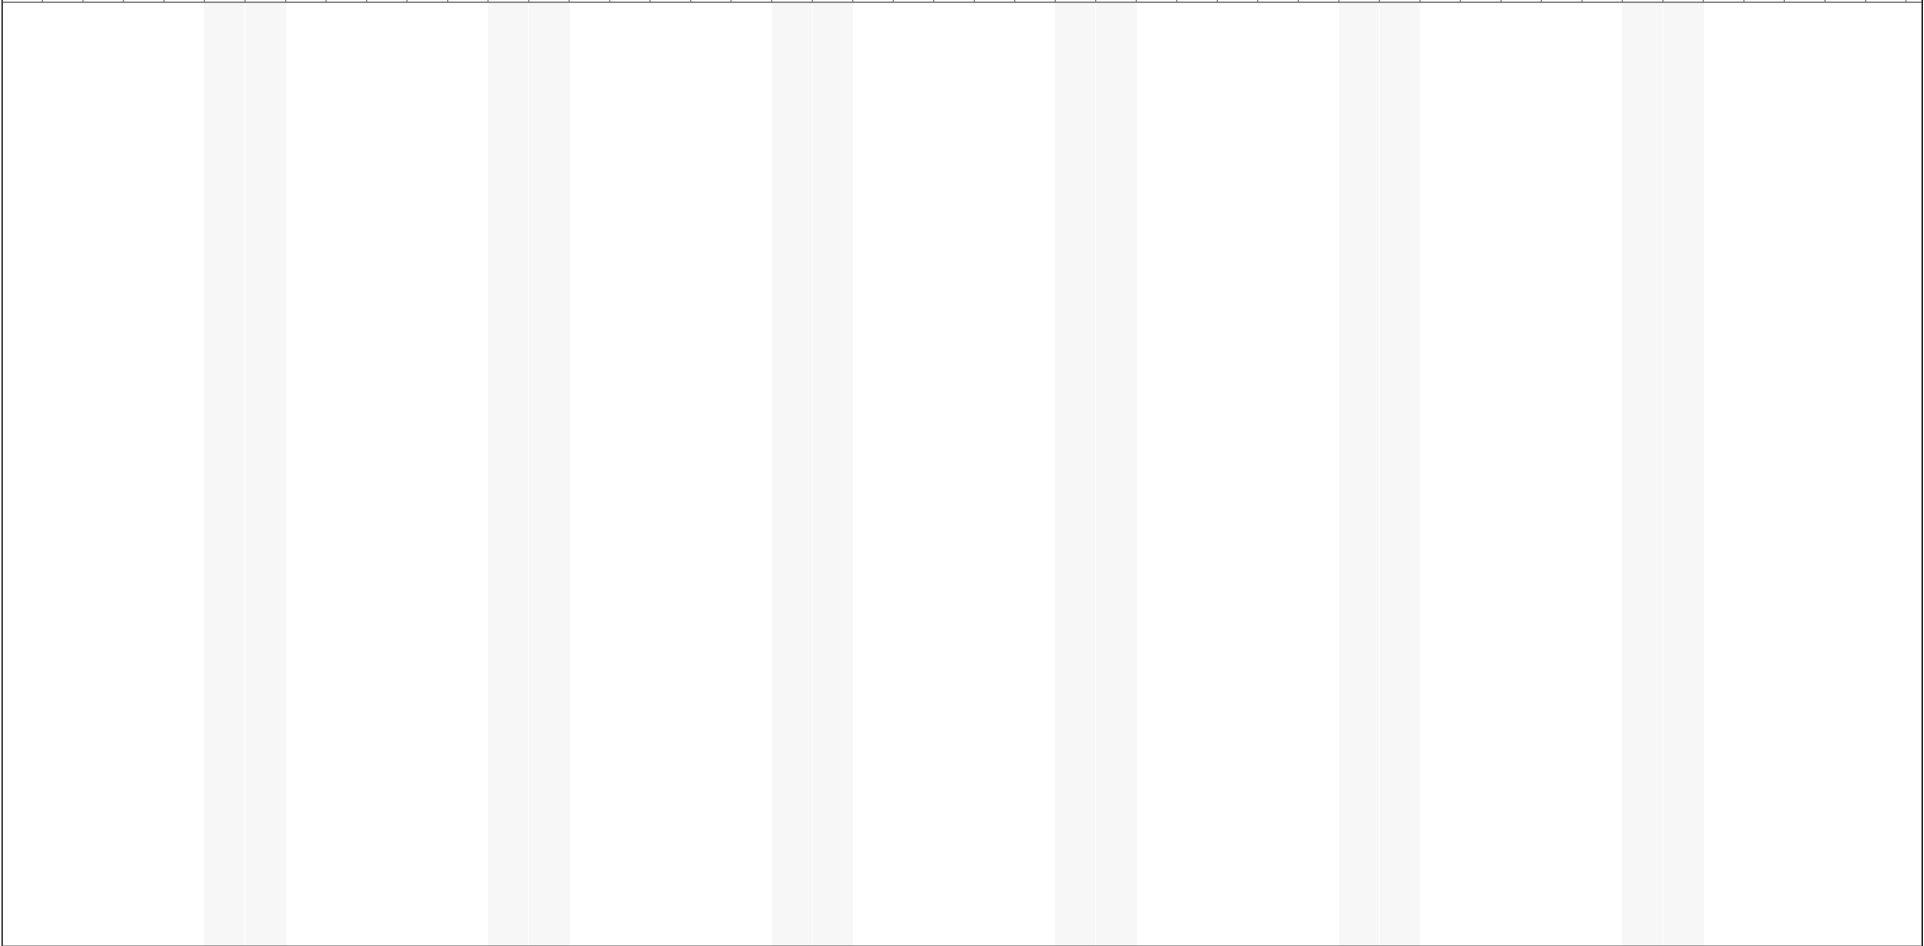

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

May '26

M

T

W

T

F

S

07 Jun '26

S

M

T

W

T

F

S

14 Jun '26

S

M

T

W

T

F

S

21 Jun '26

S

M

T

W

T

F

S

28 Jun '26

S

M

T

W

T

F

S

05 Jul '26

S

M

T

W

T

F

S

12 Jul '26

S


M



T


W



T


F

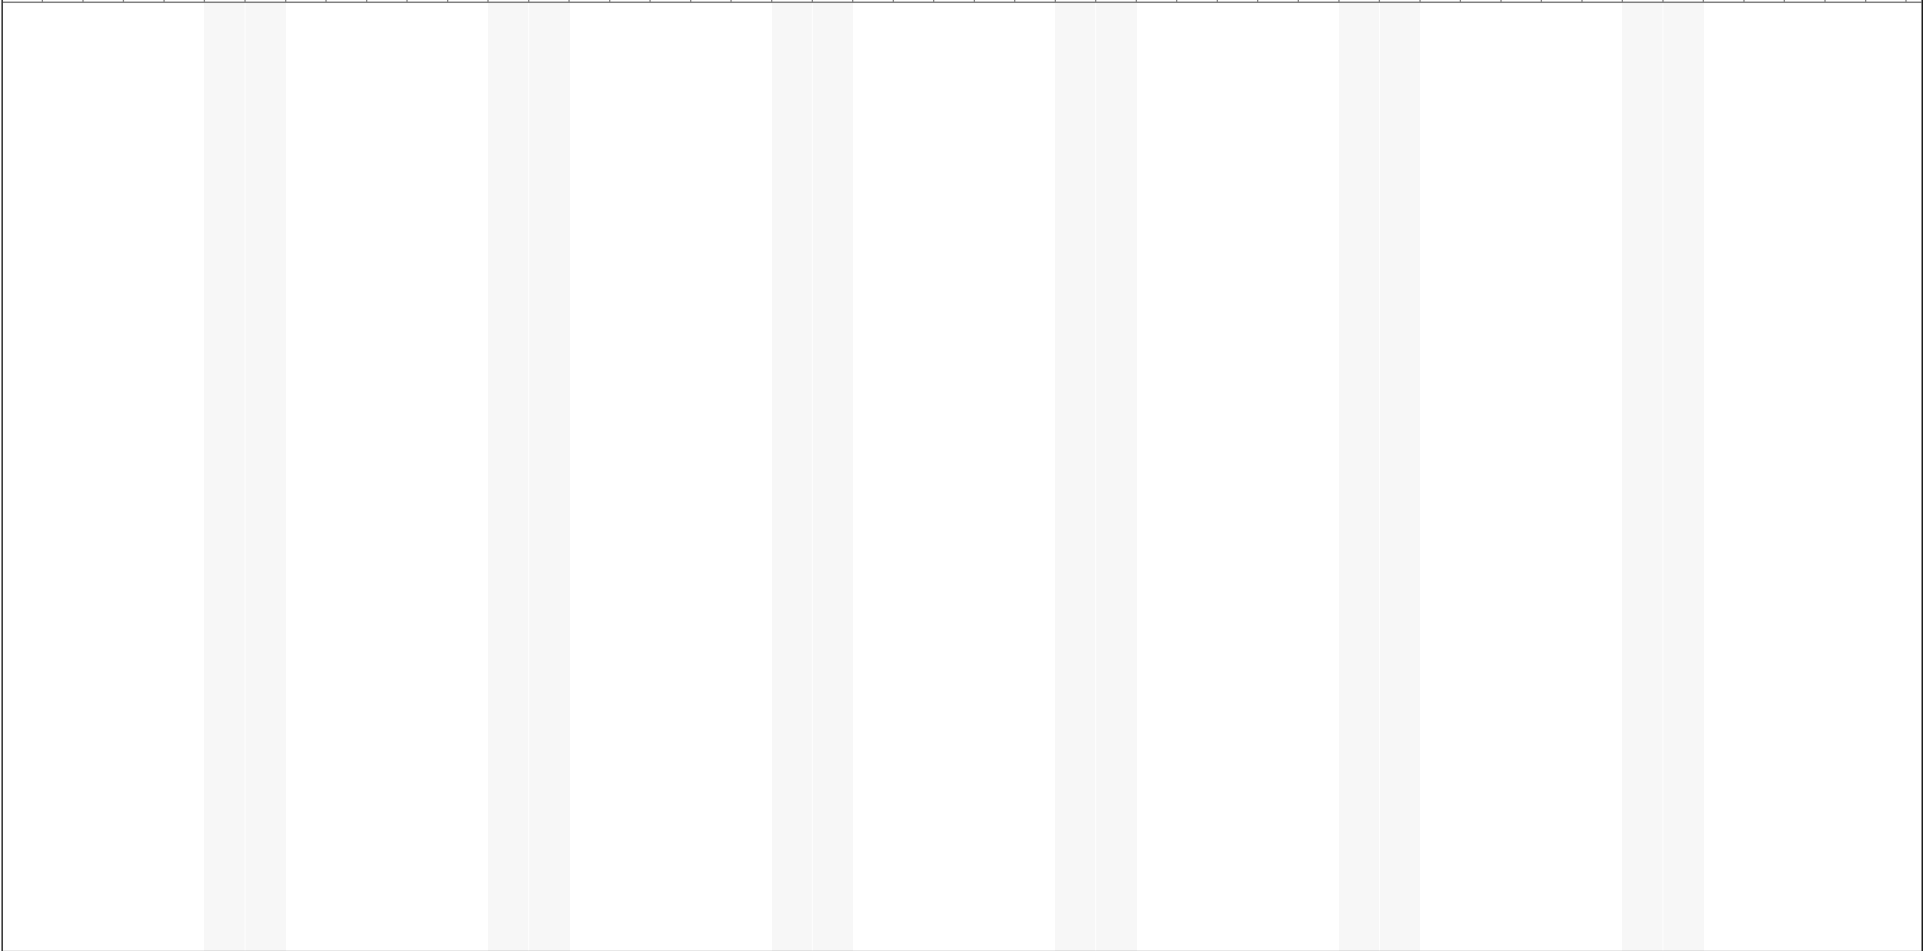




Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

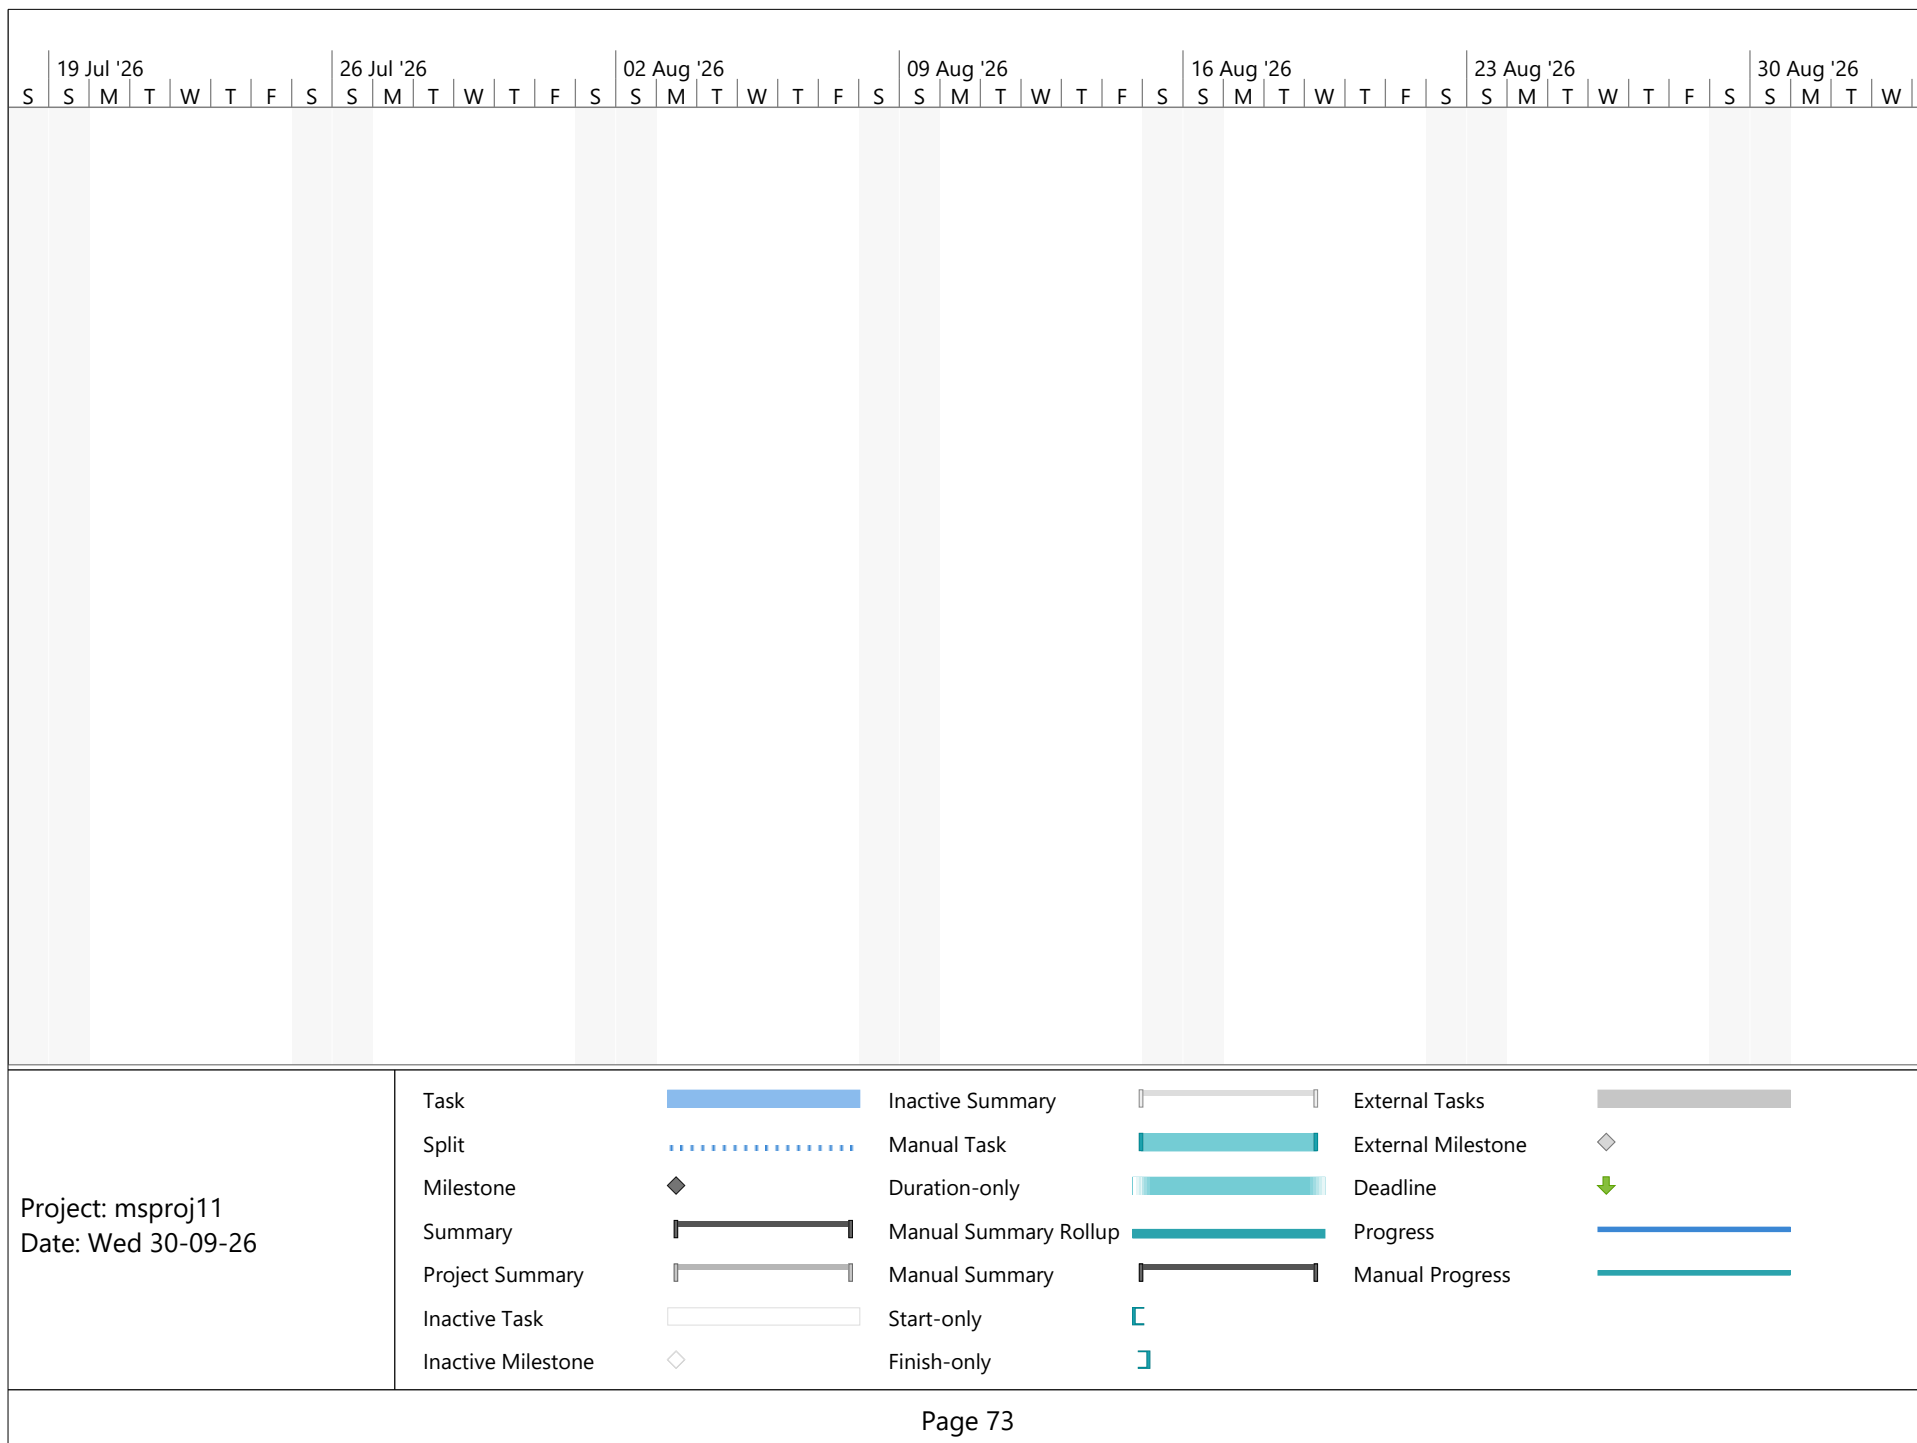

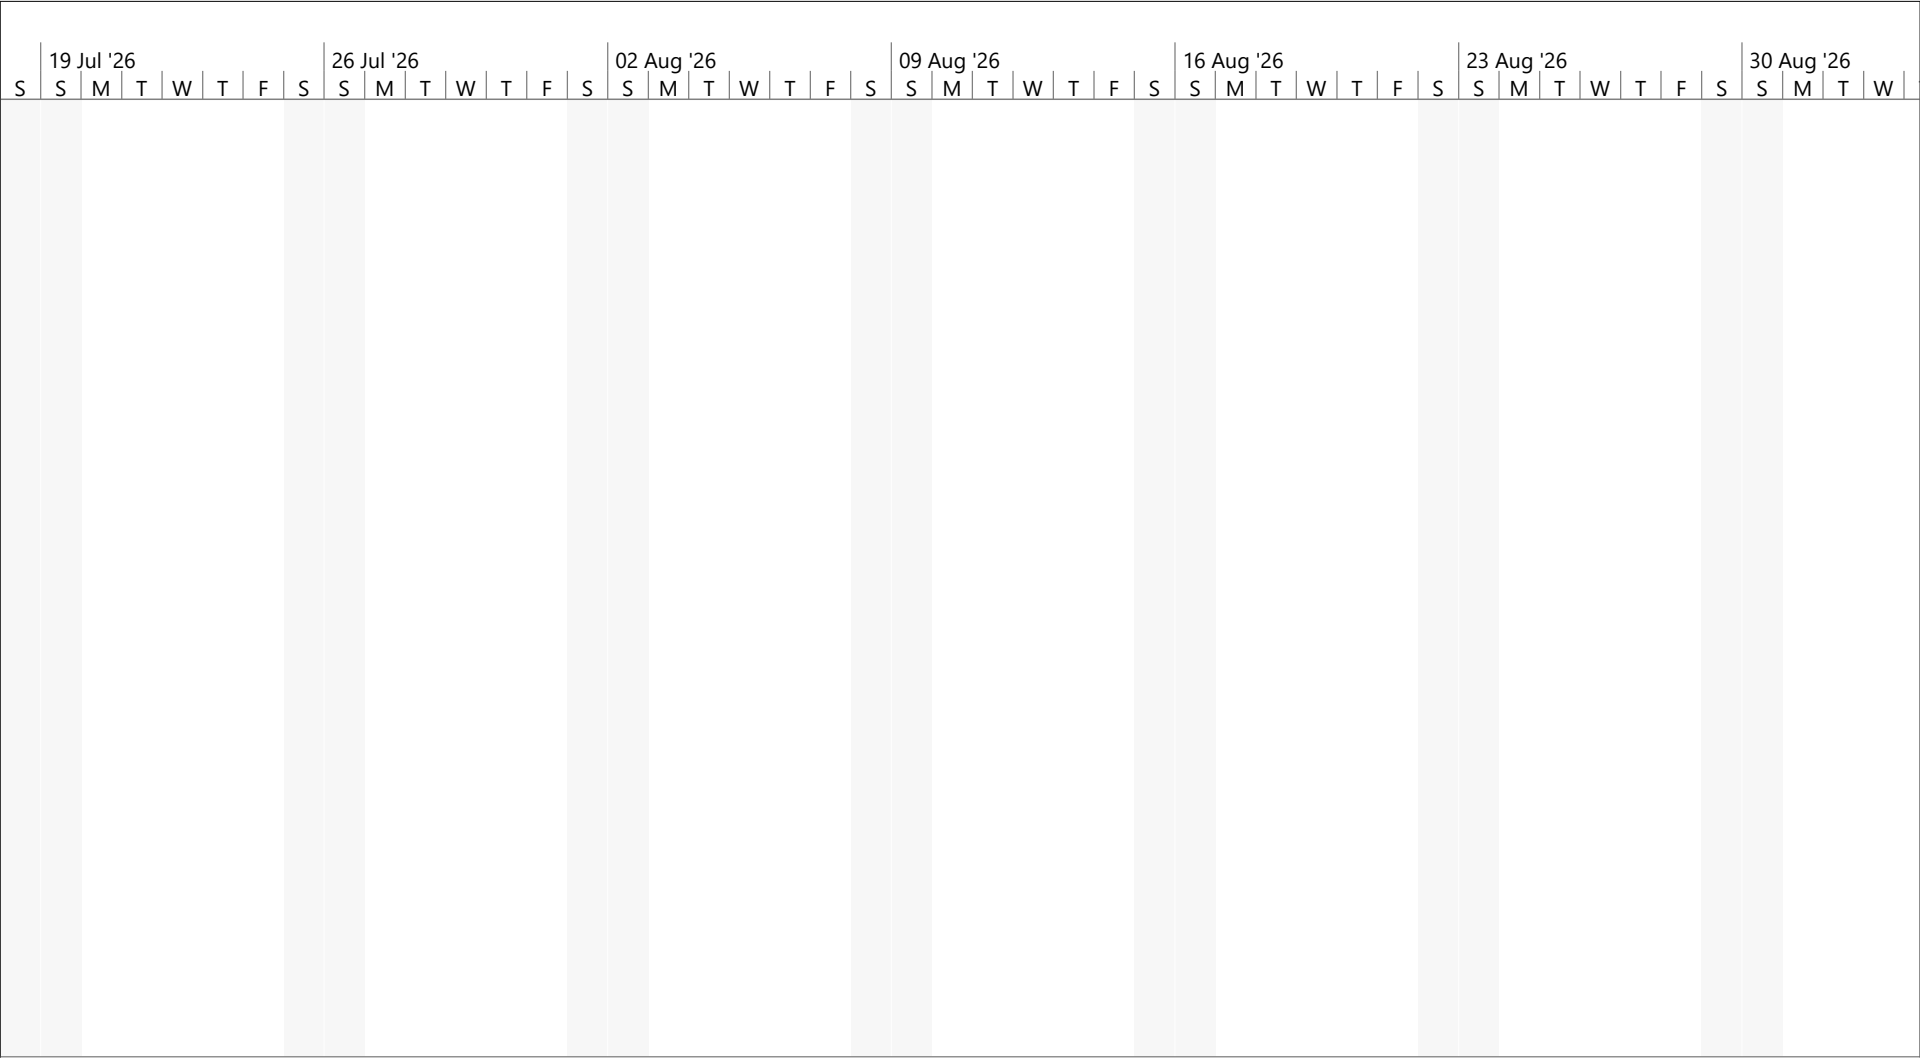


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

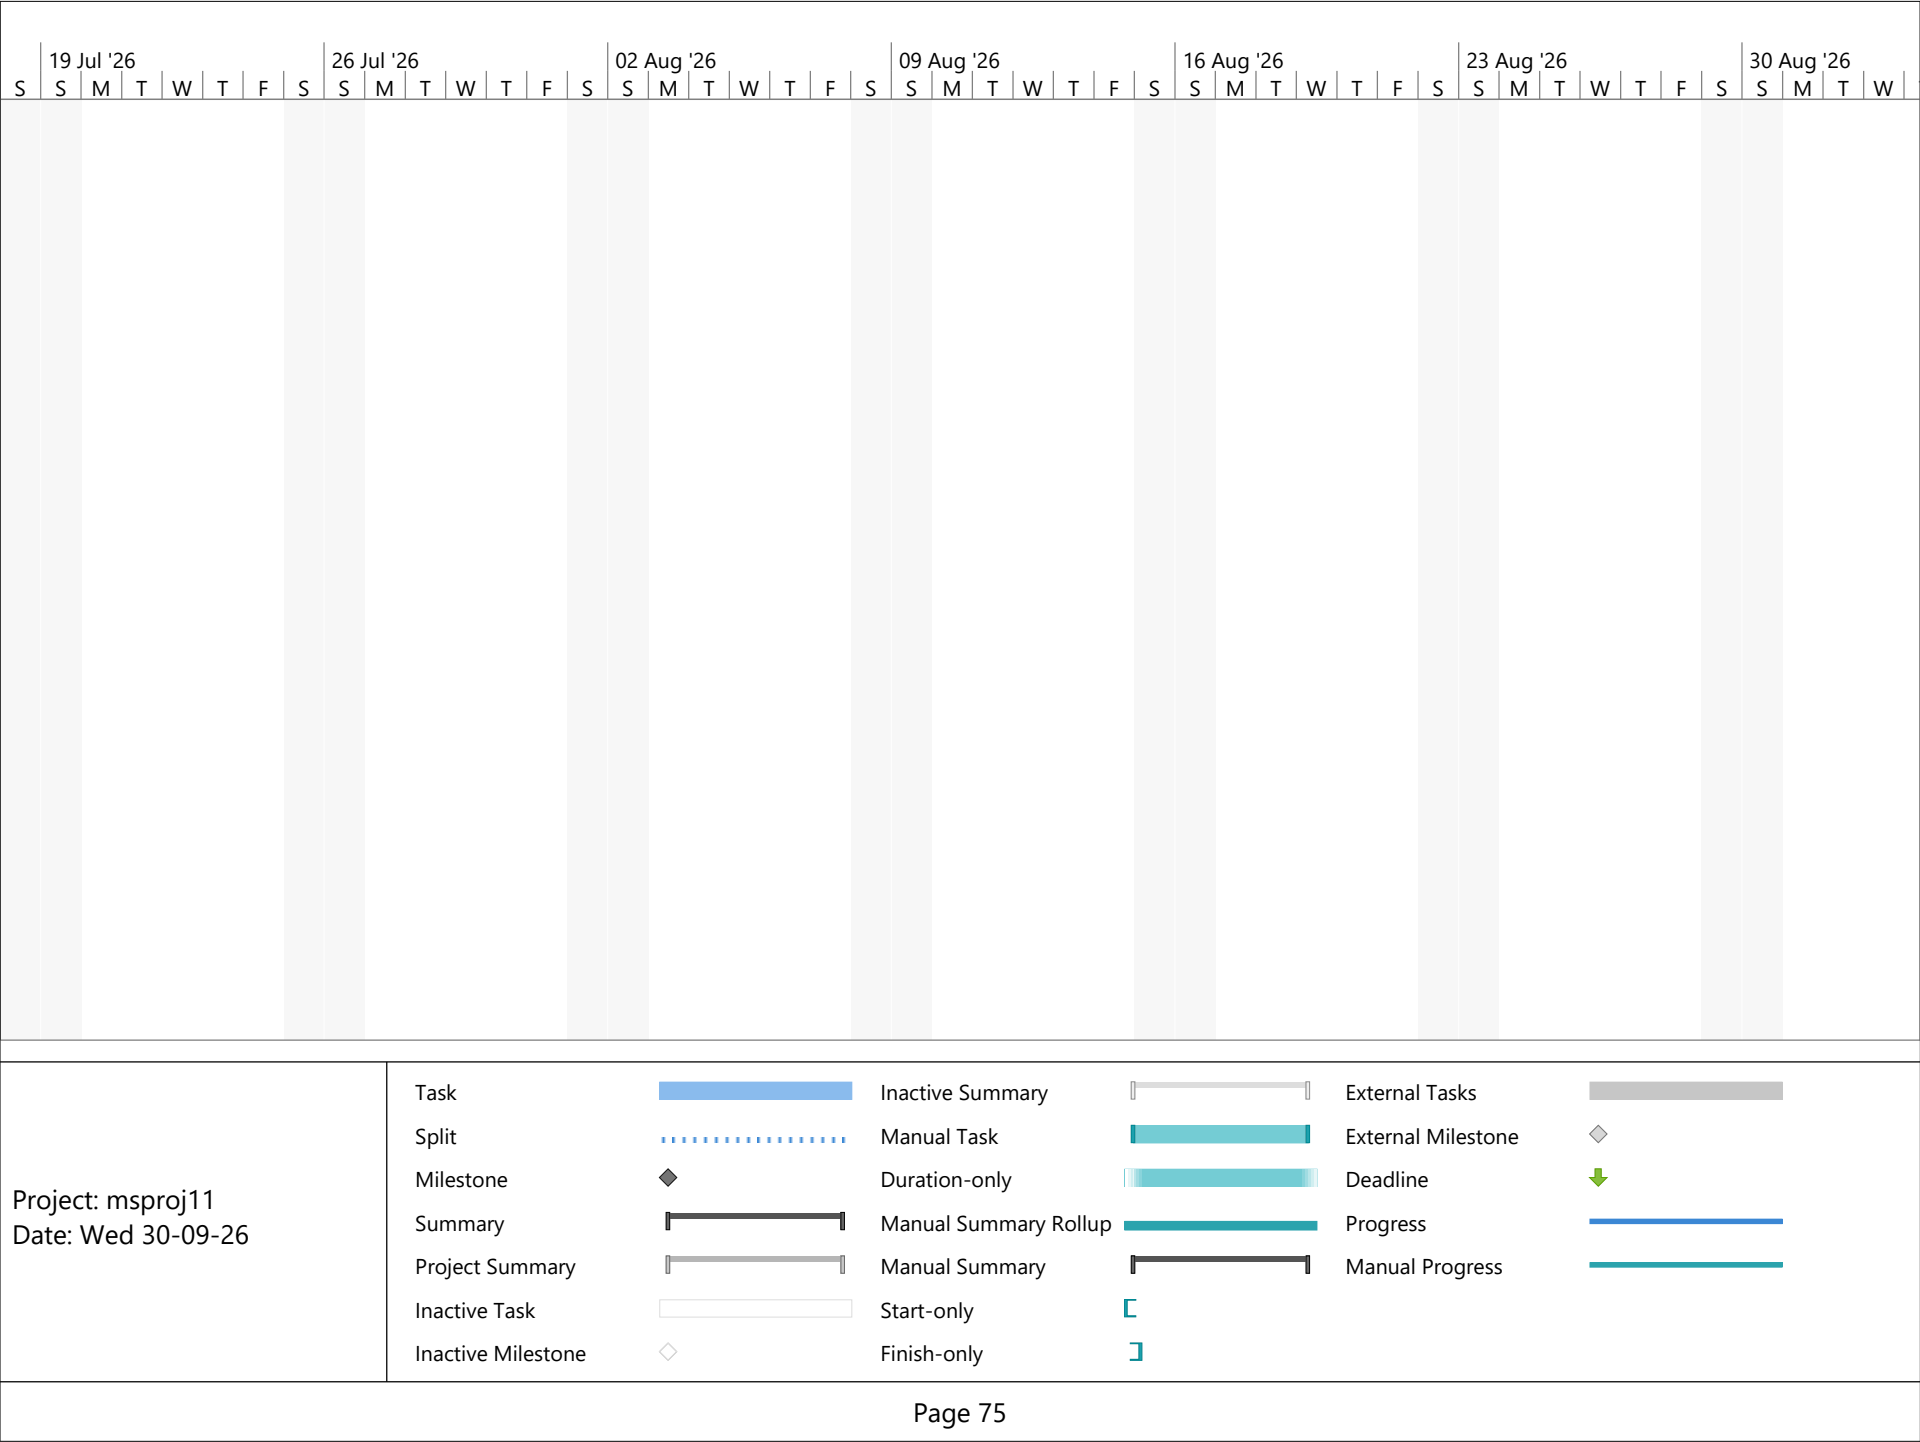


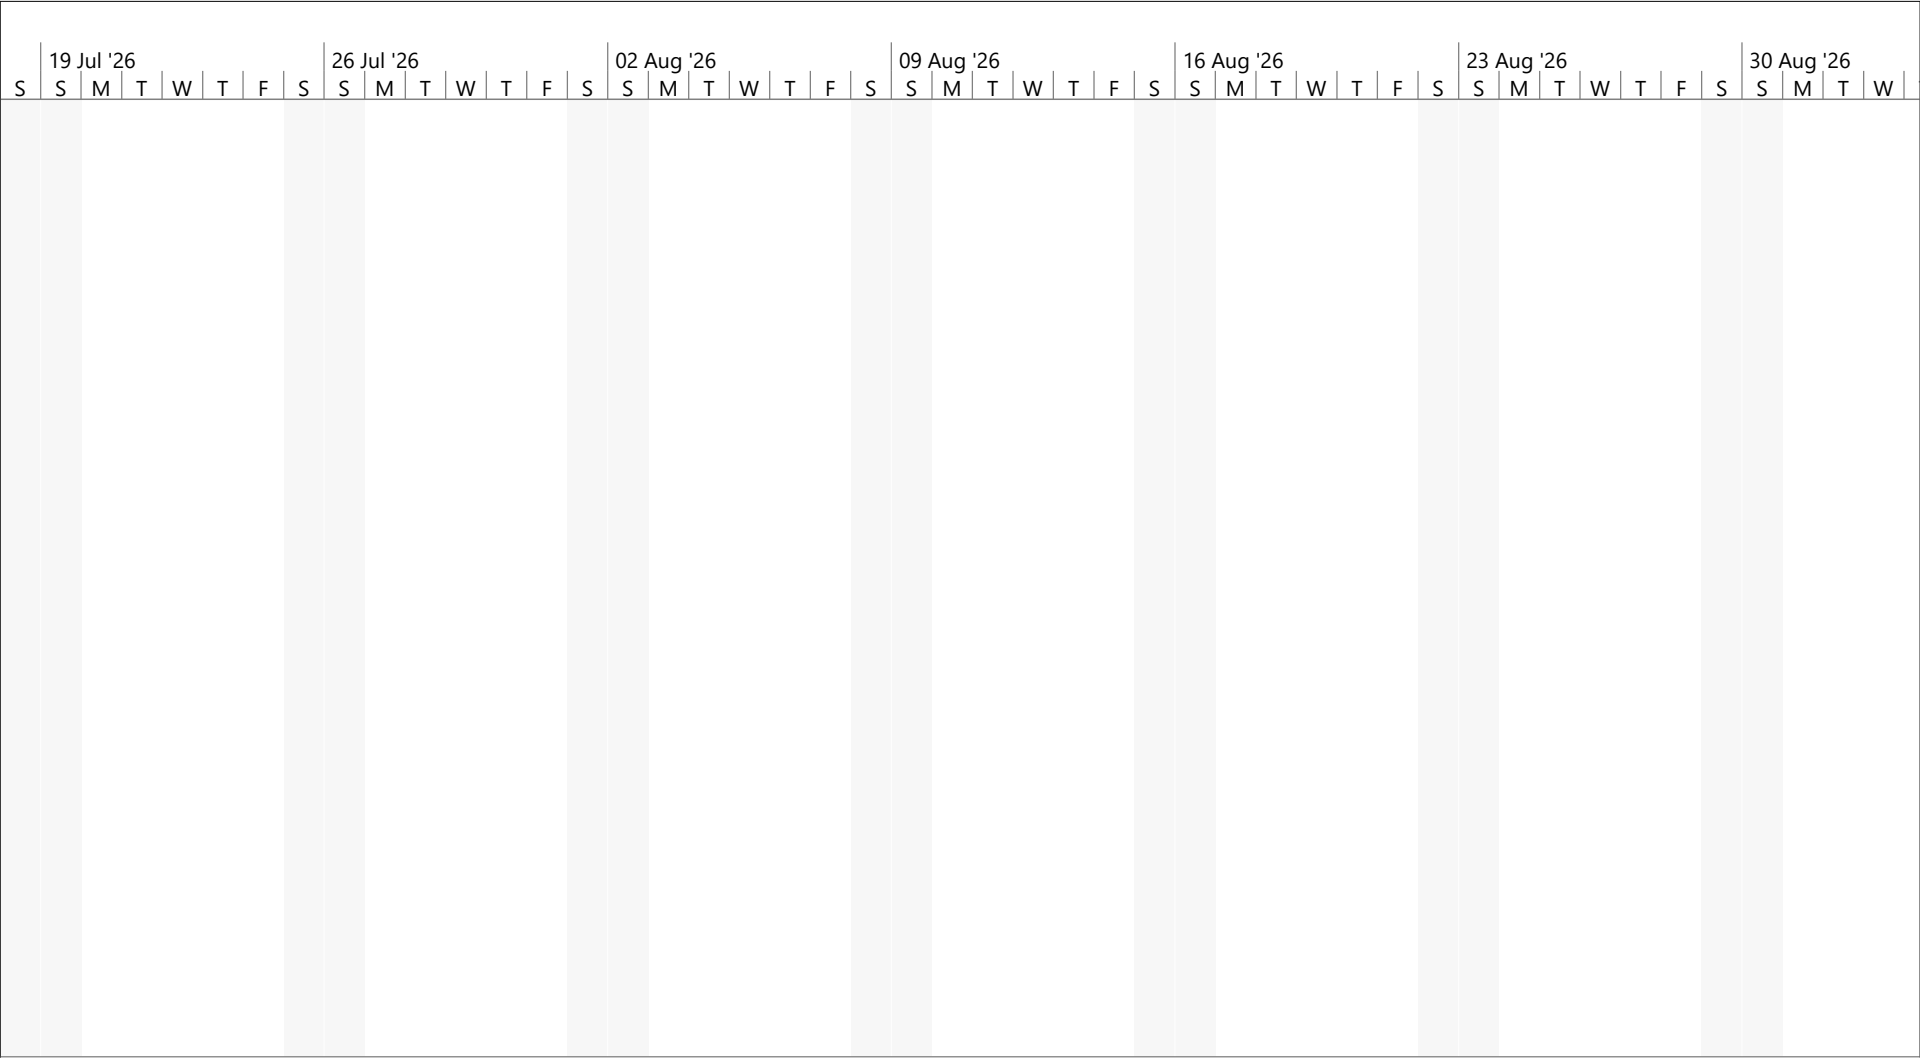


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

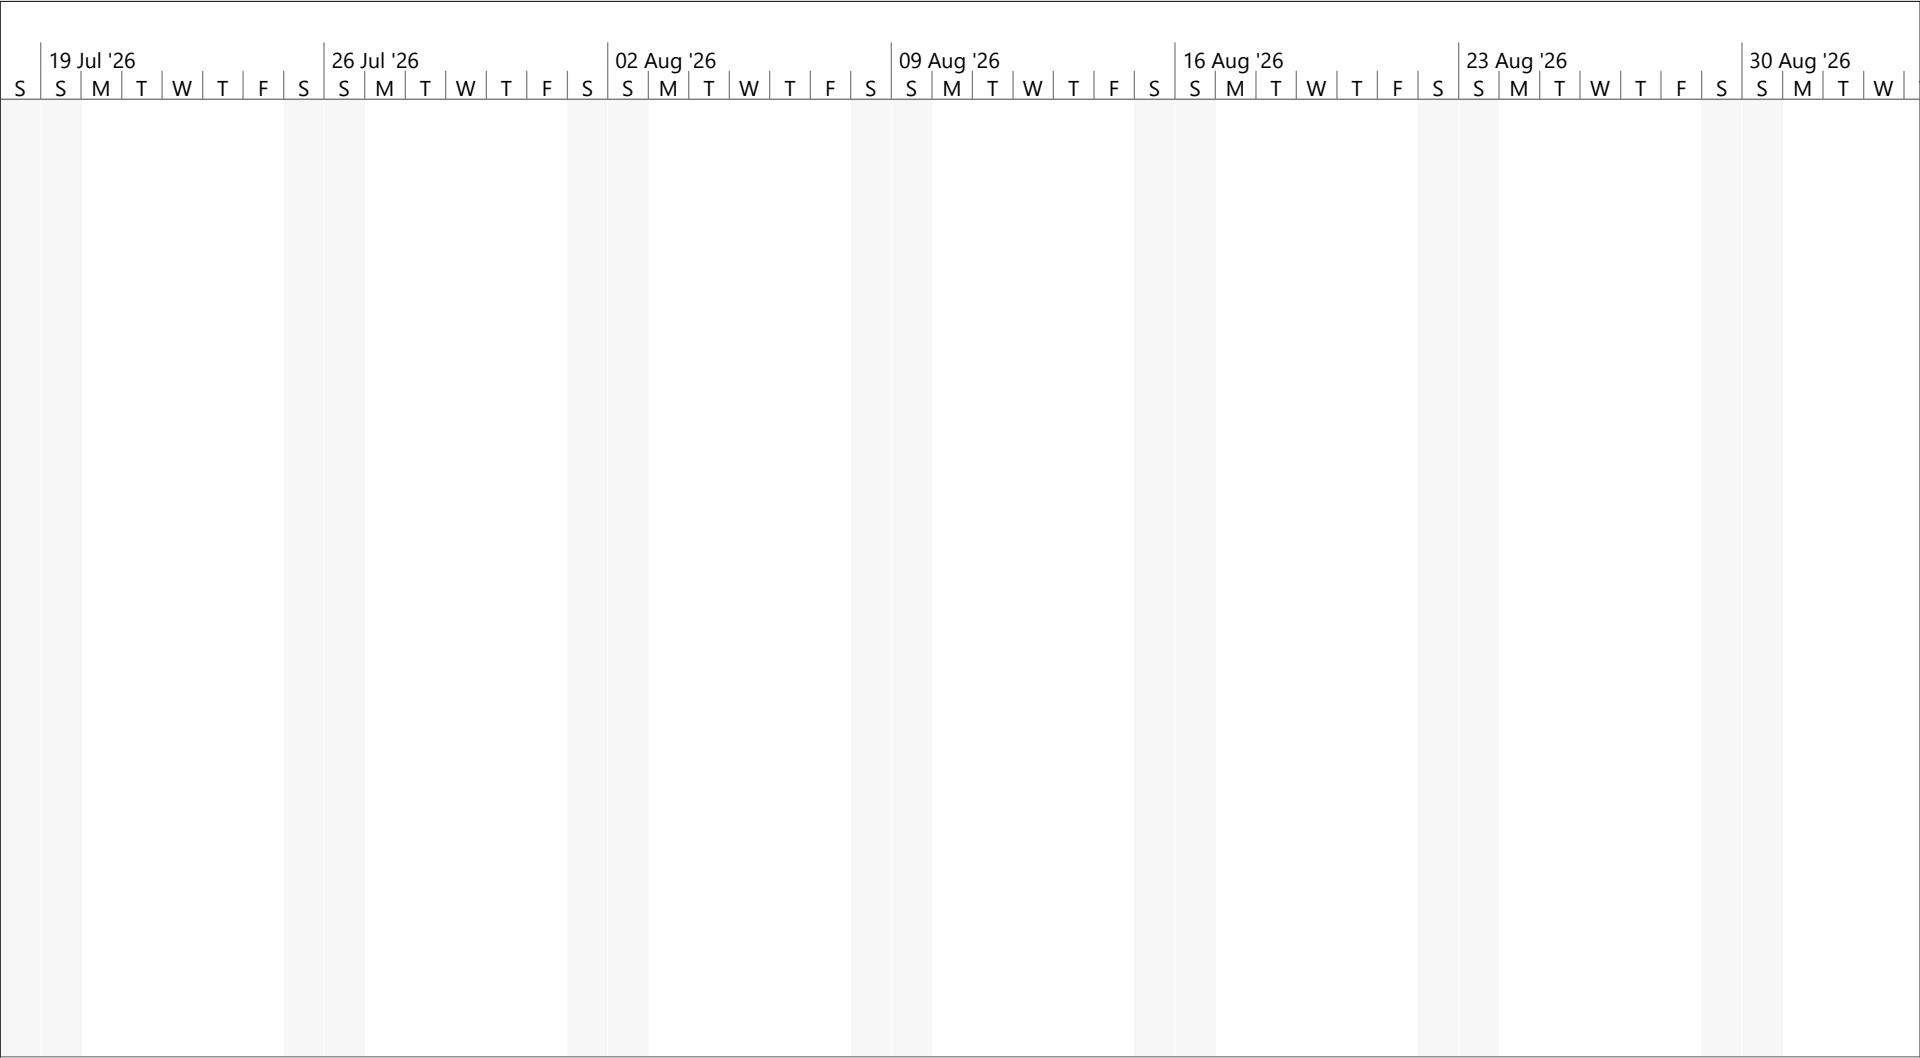

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

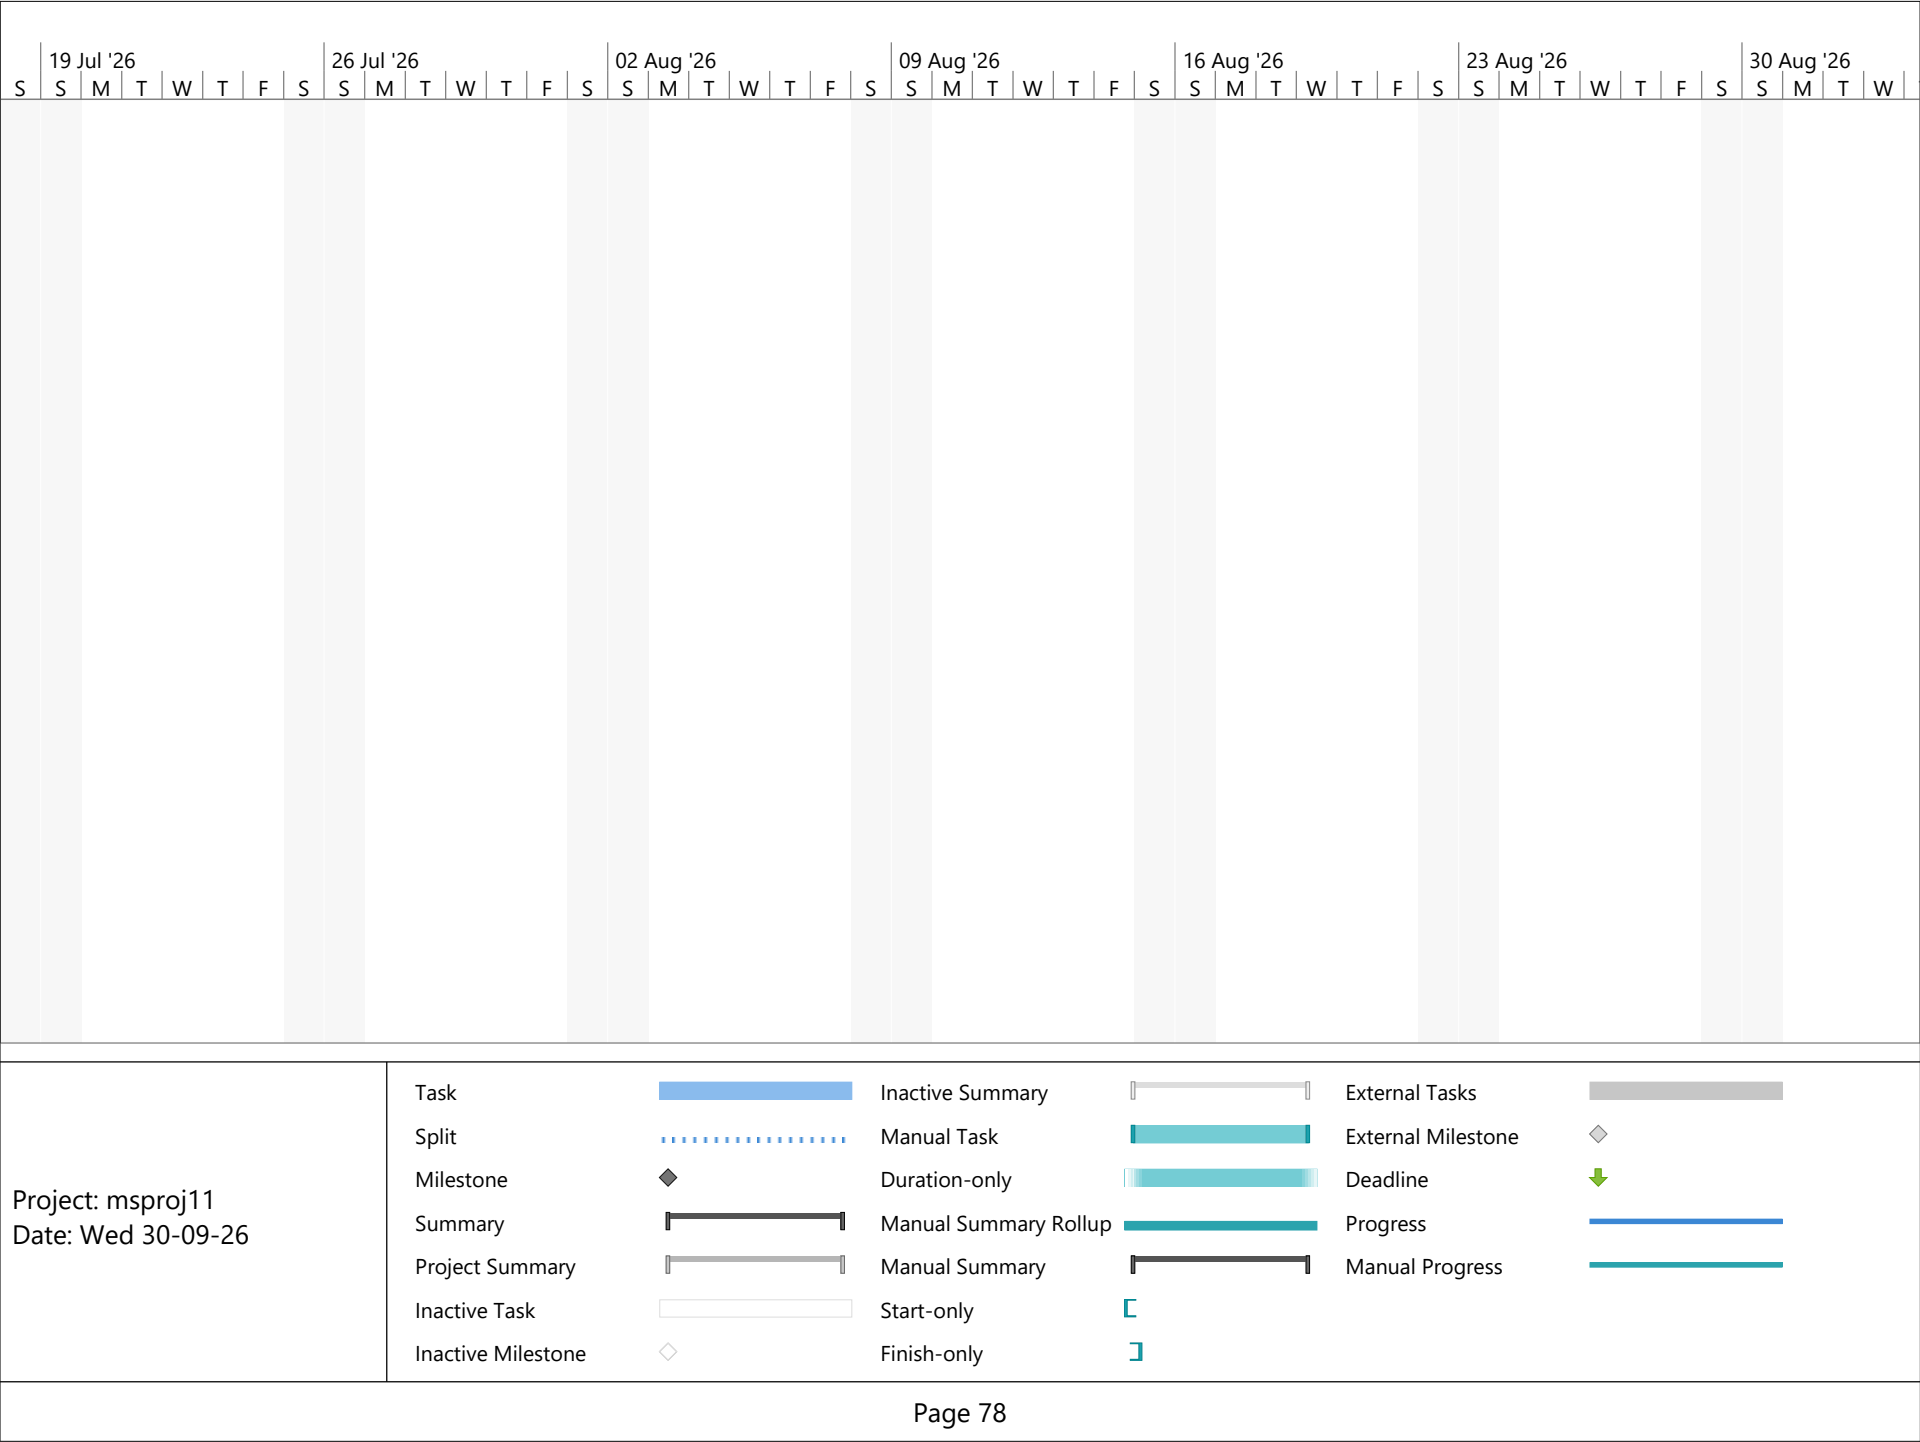

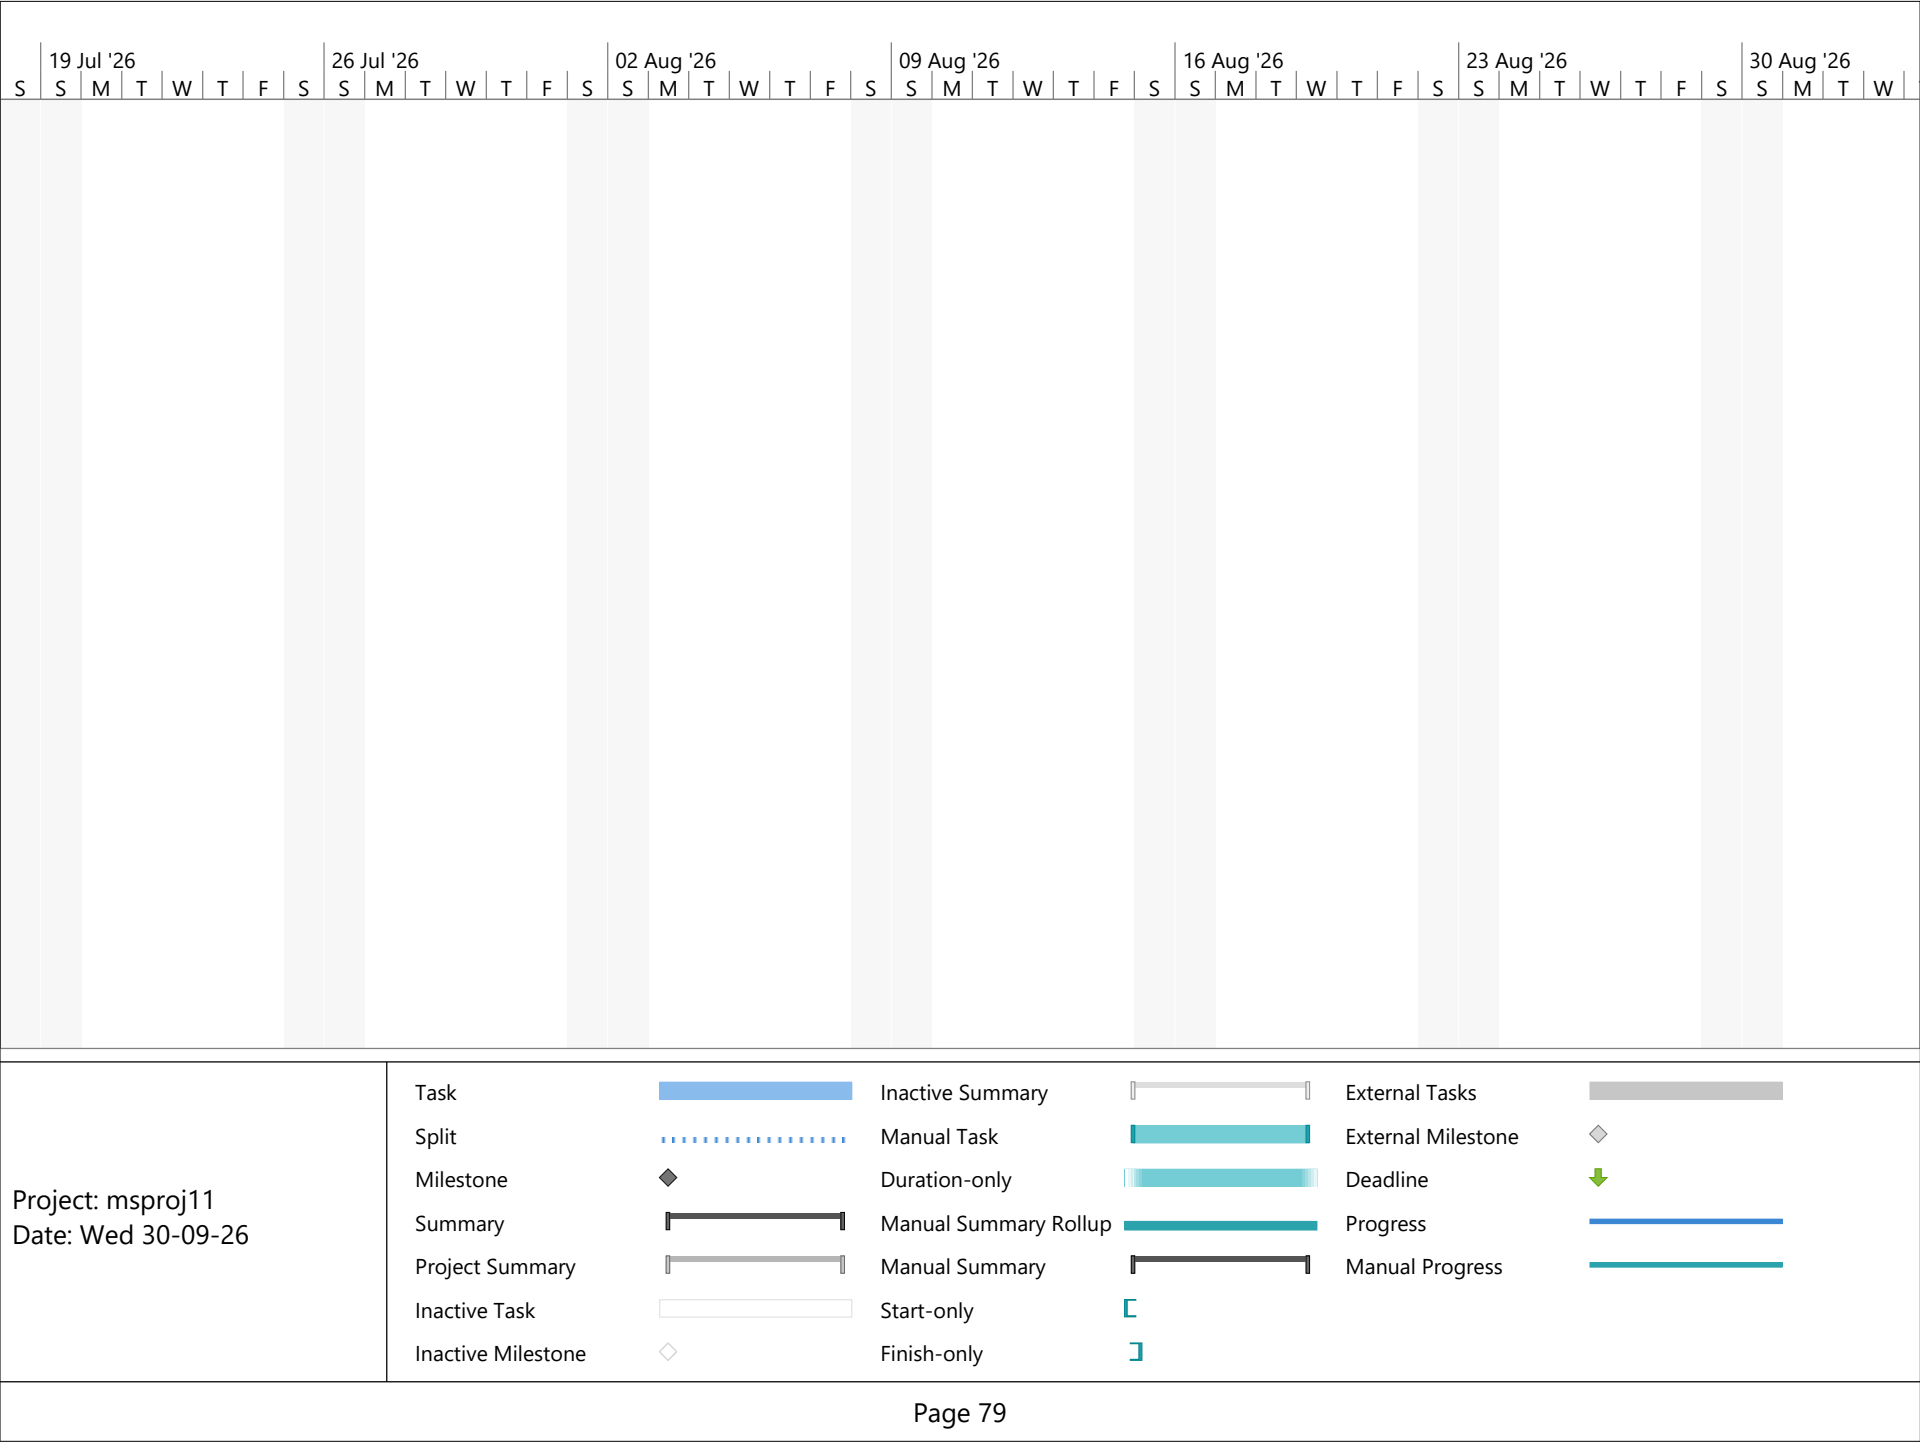

S

S

M

T

W

T

F

S

23 Aug '26

S

S

M

T

W

T

F

S

30 Aug '26

Project: msproj11

Date: Wed 30-09-26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline


Progress

Manual Progress


Page 79

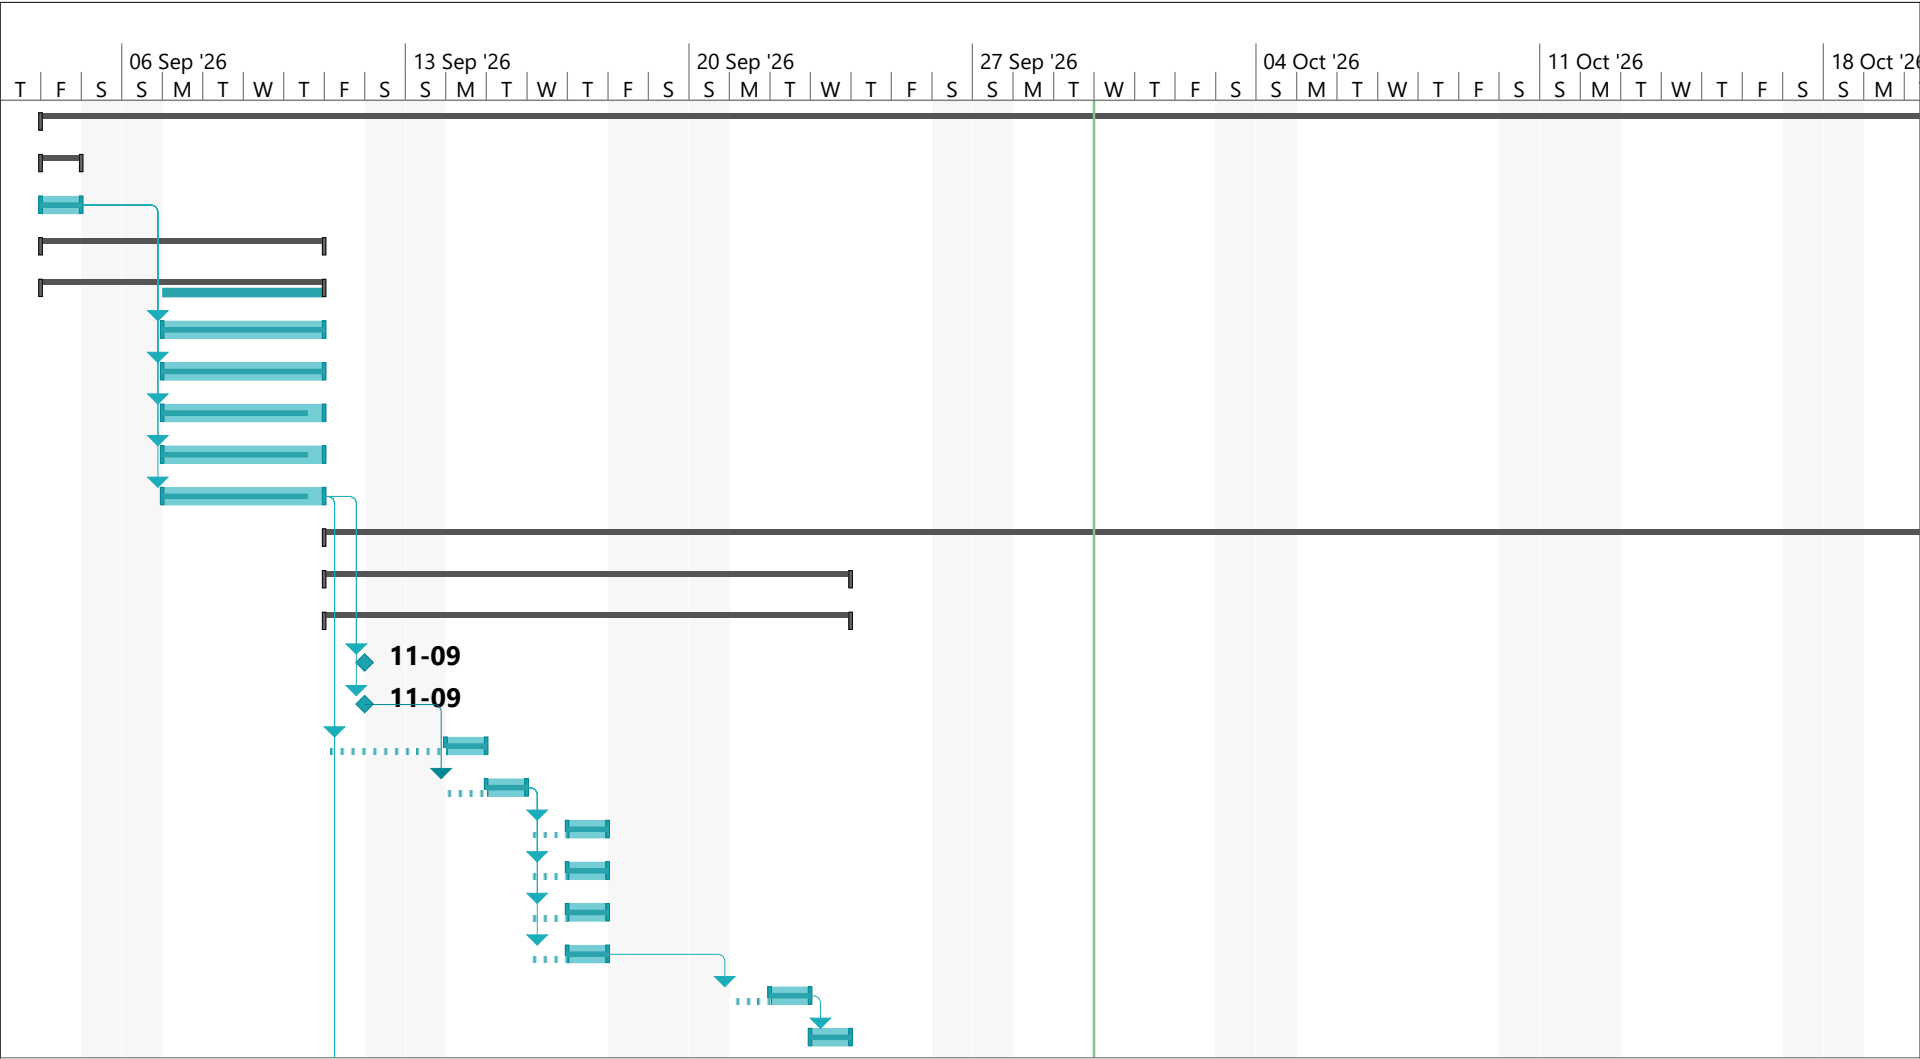


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

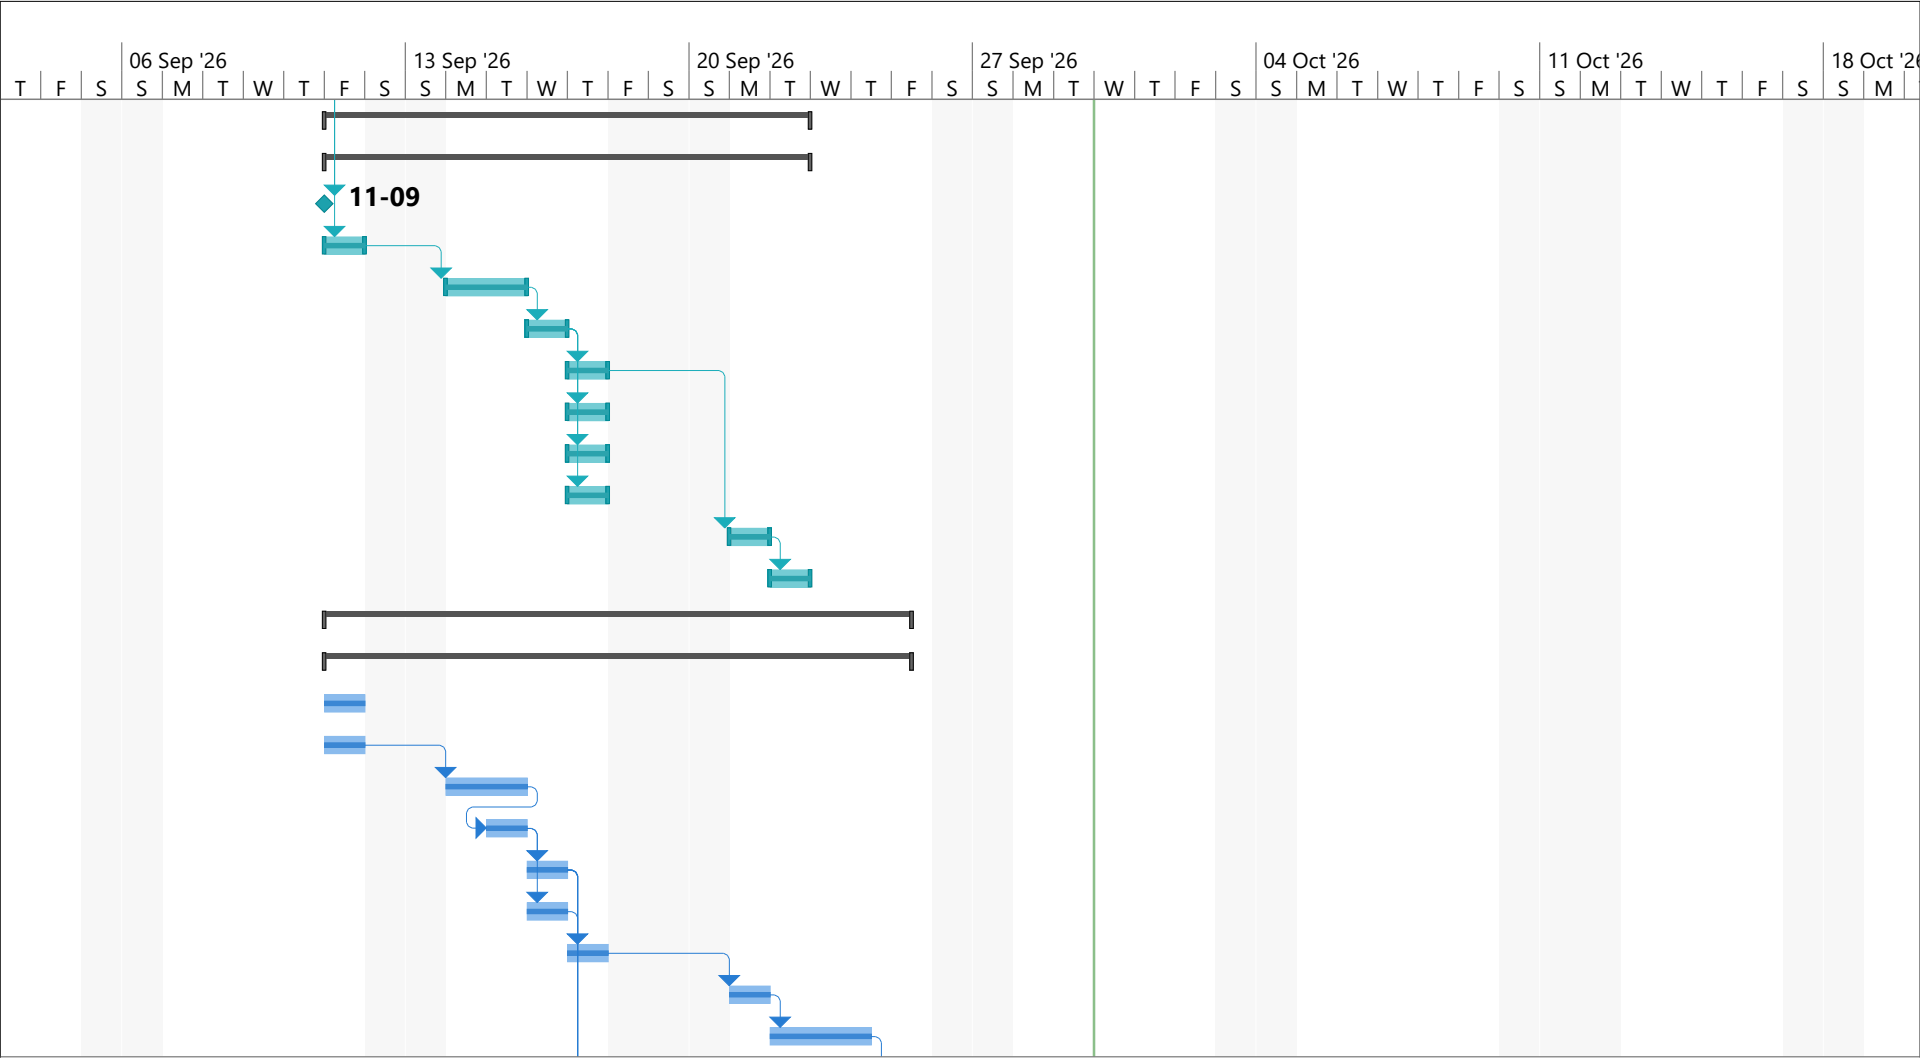


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

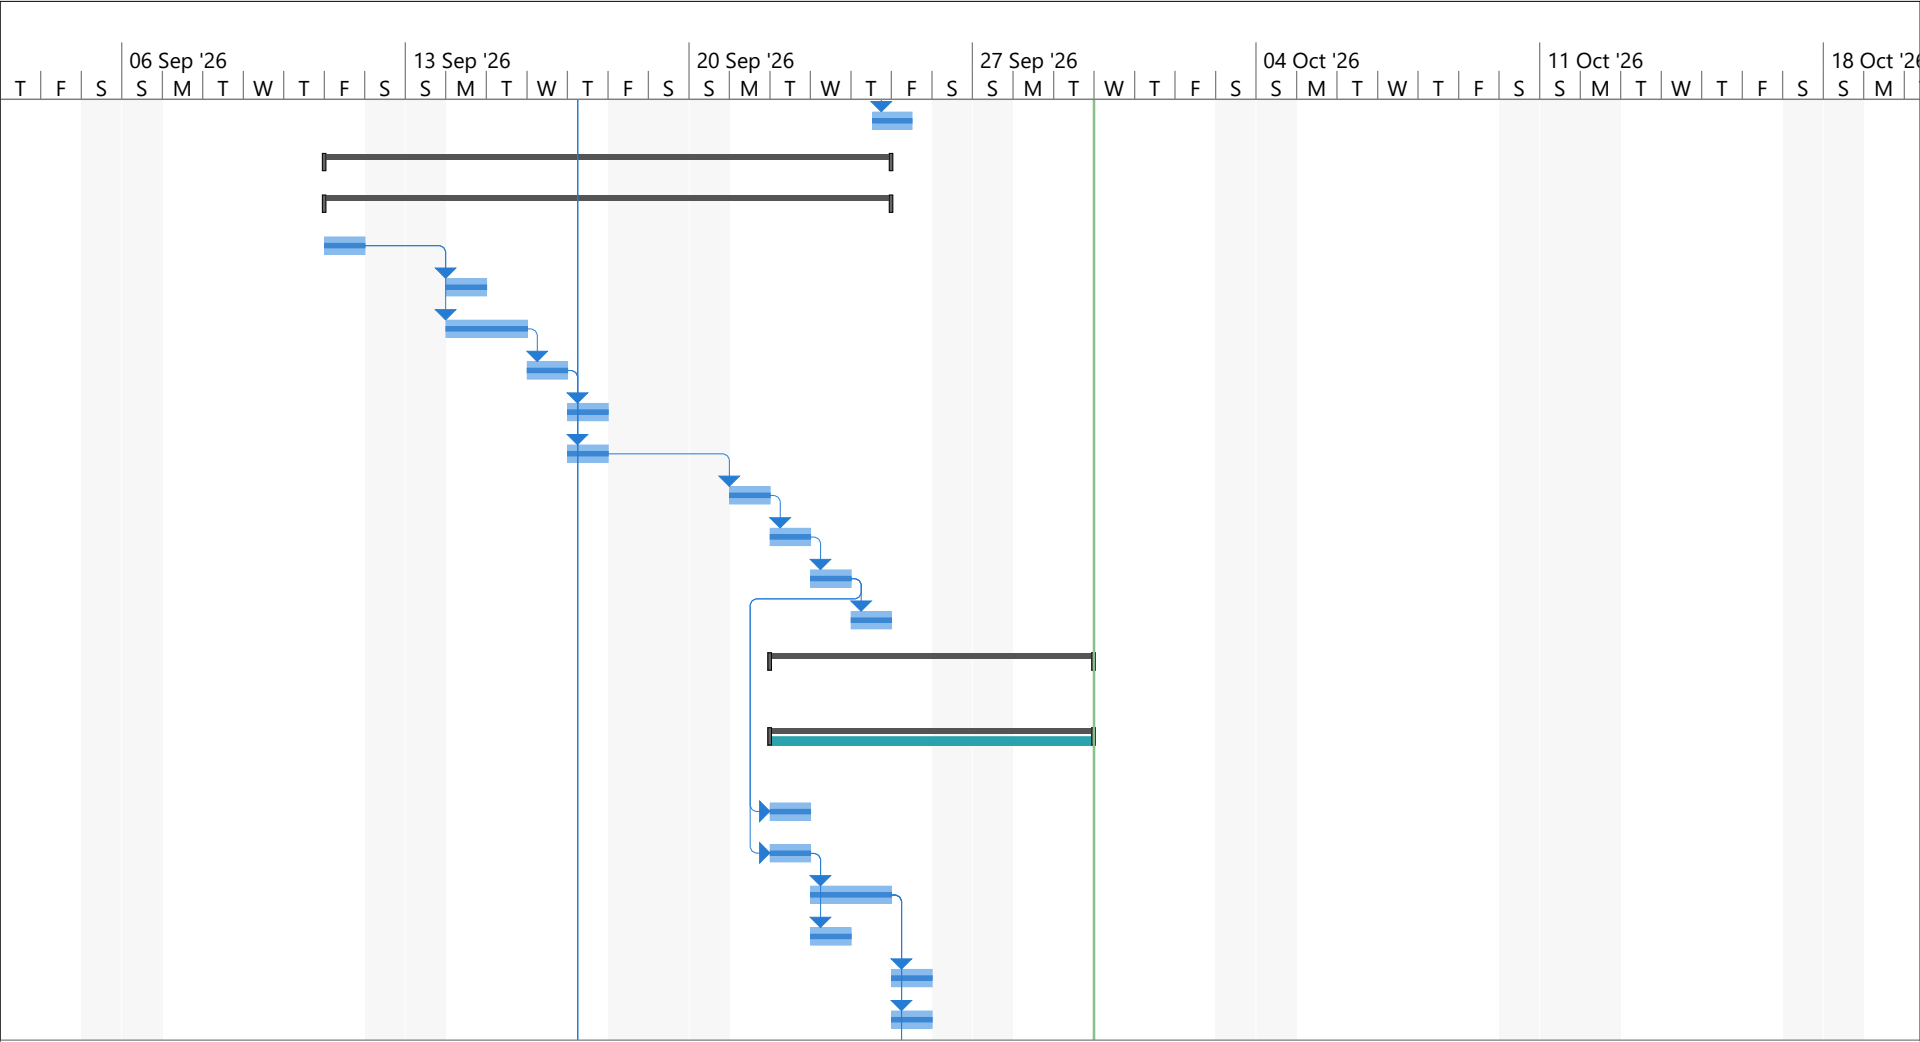


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

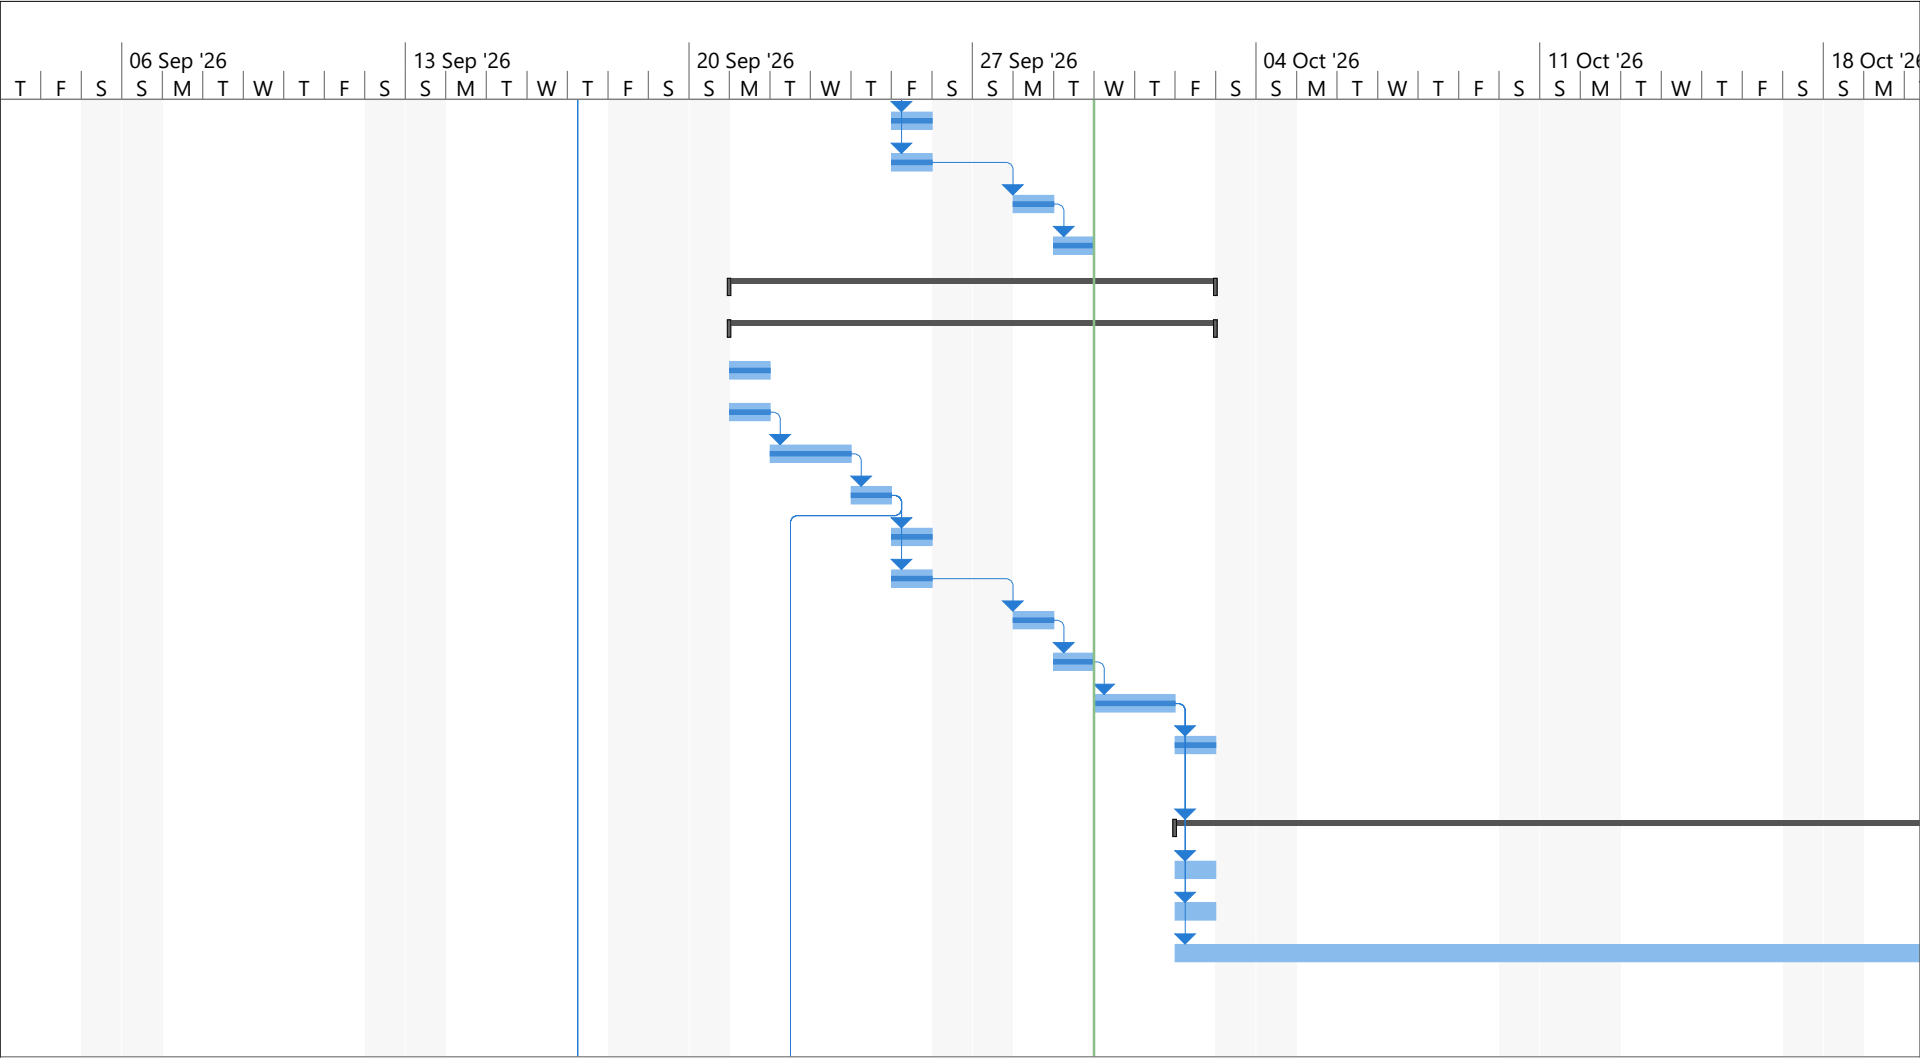


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

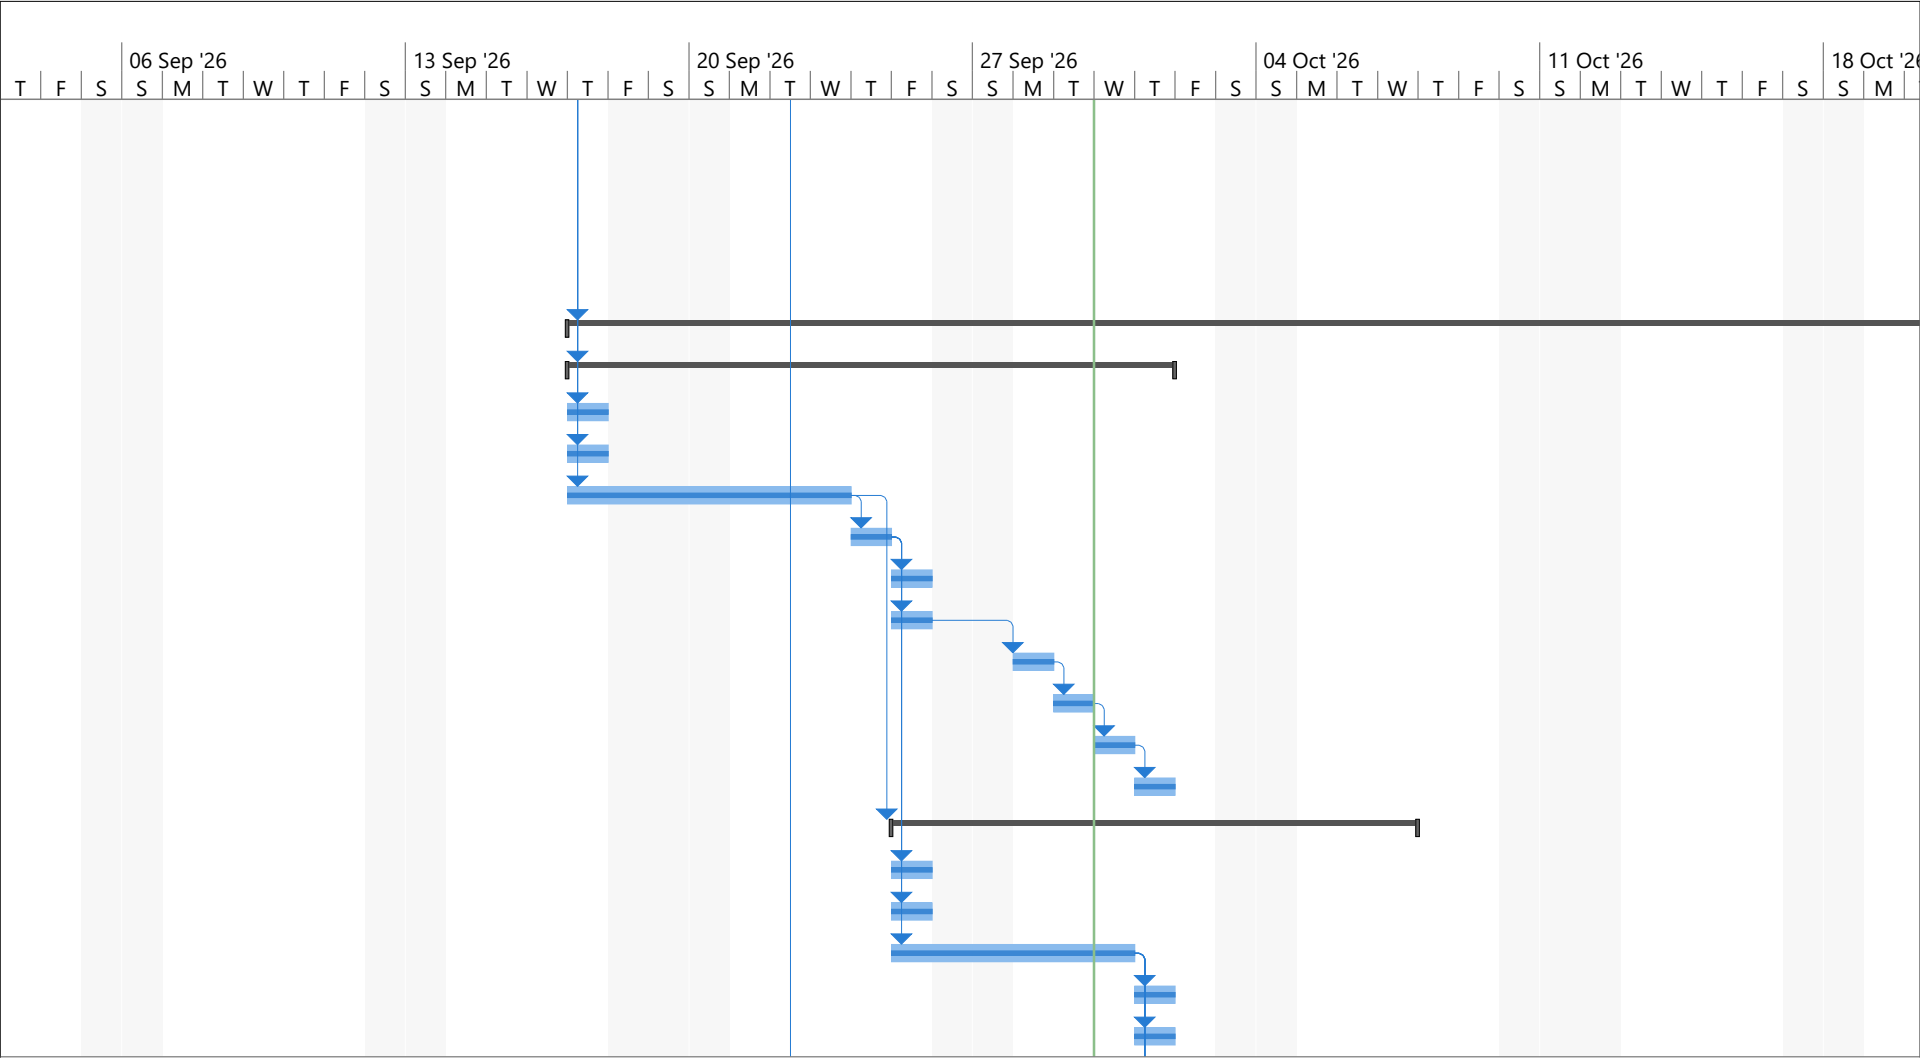


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

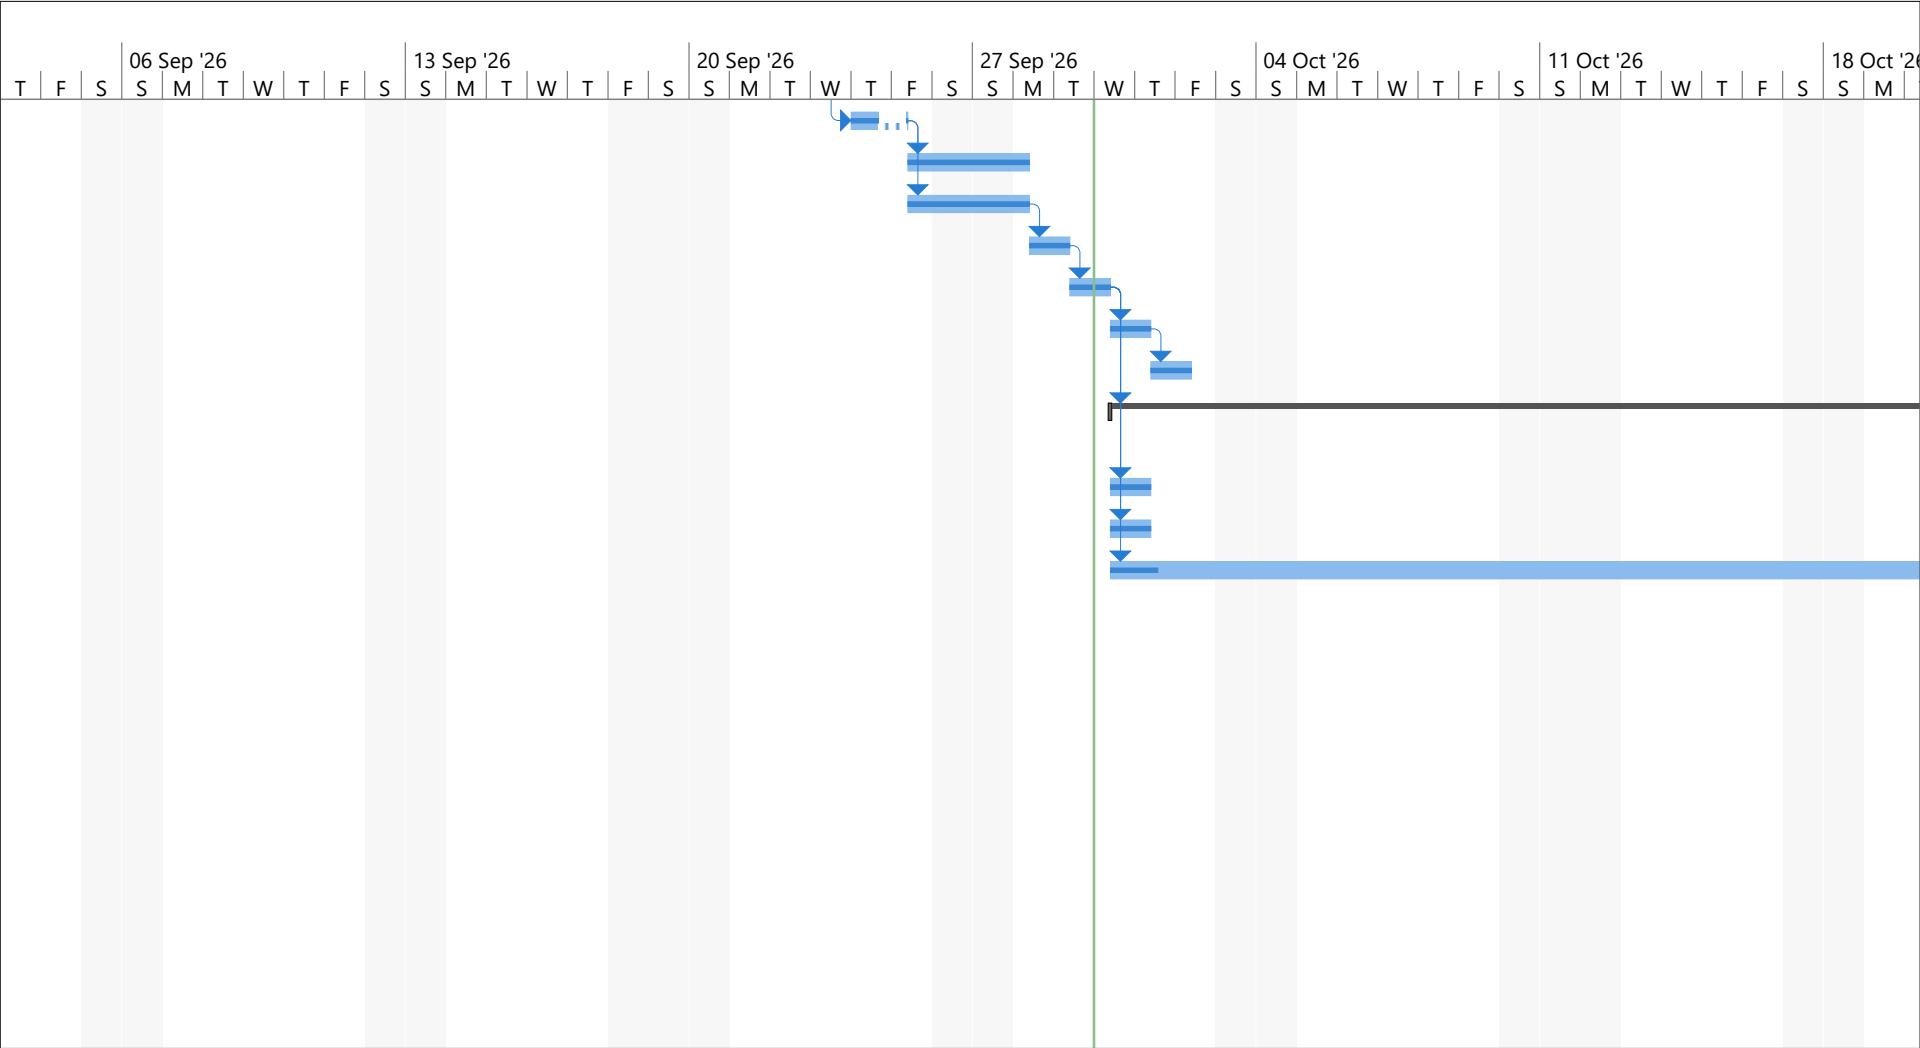


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

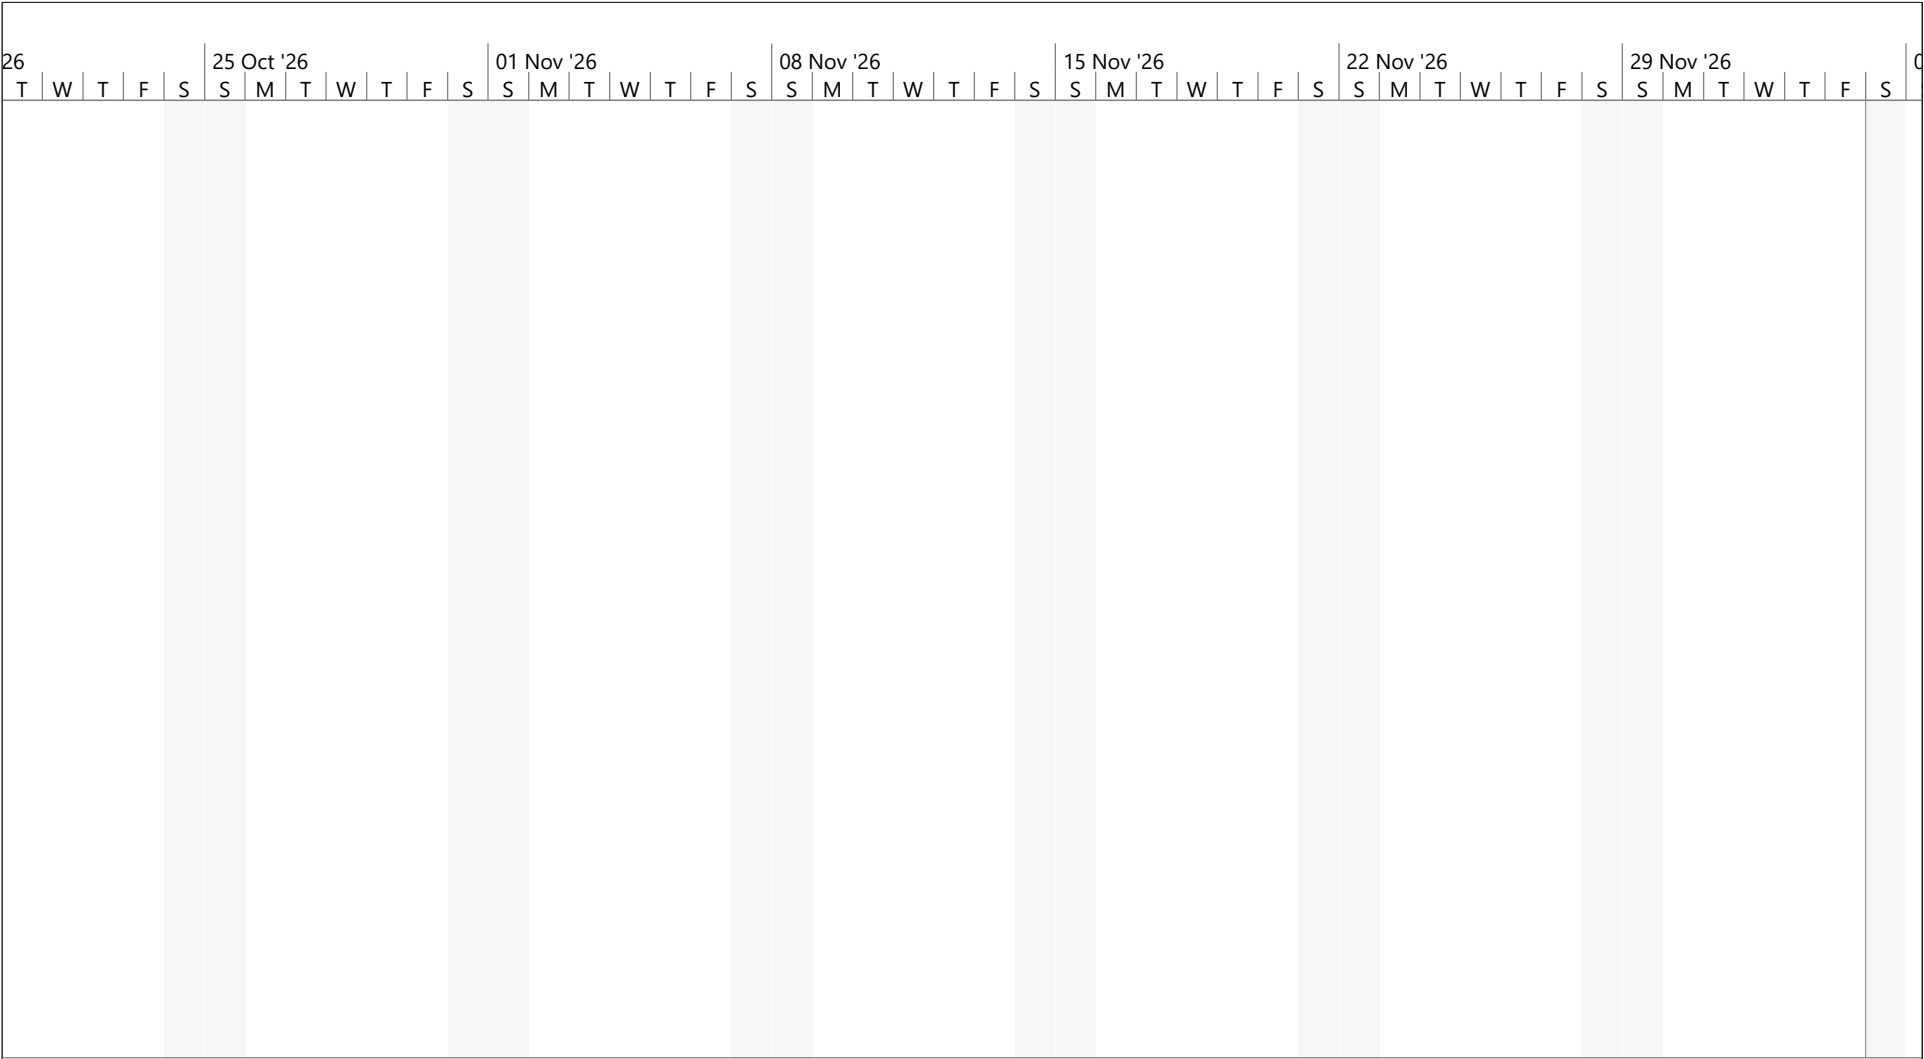


Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

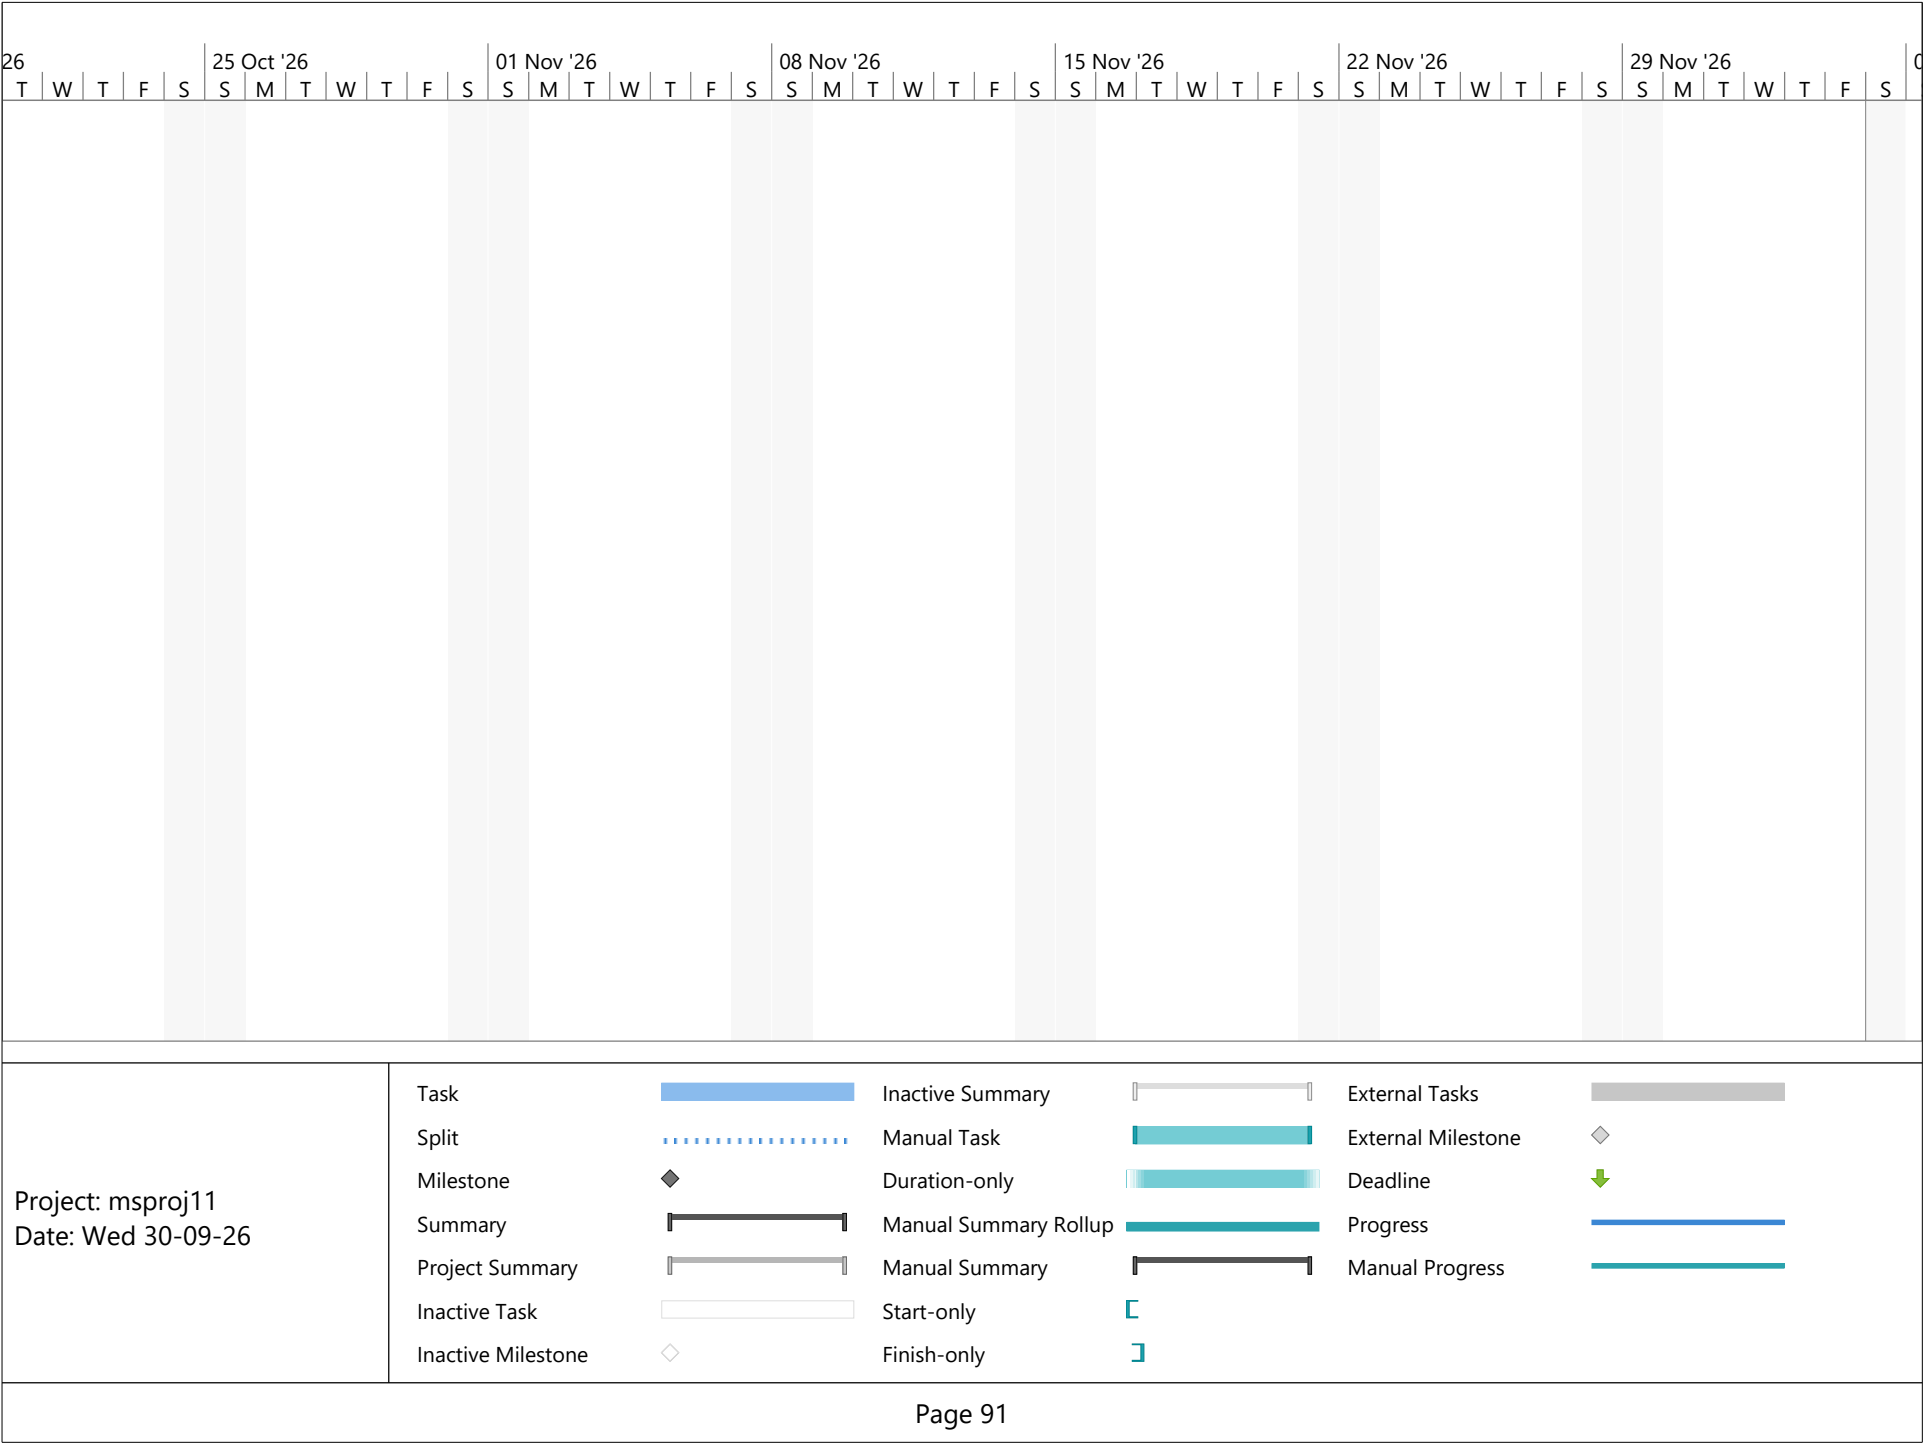

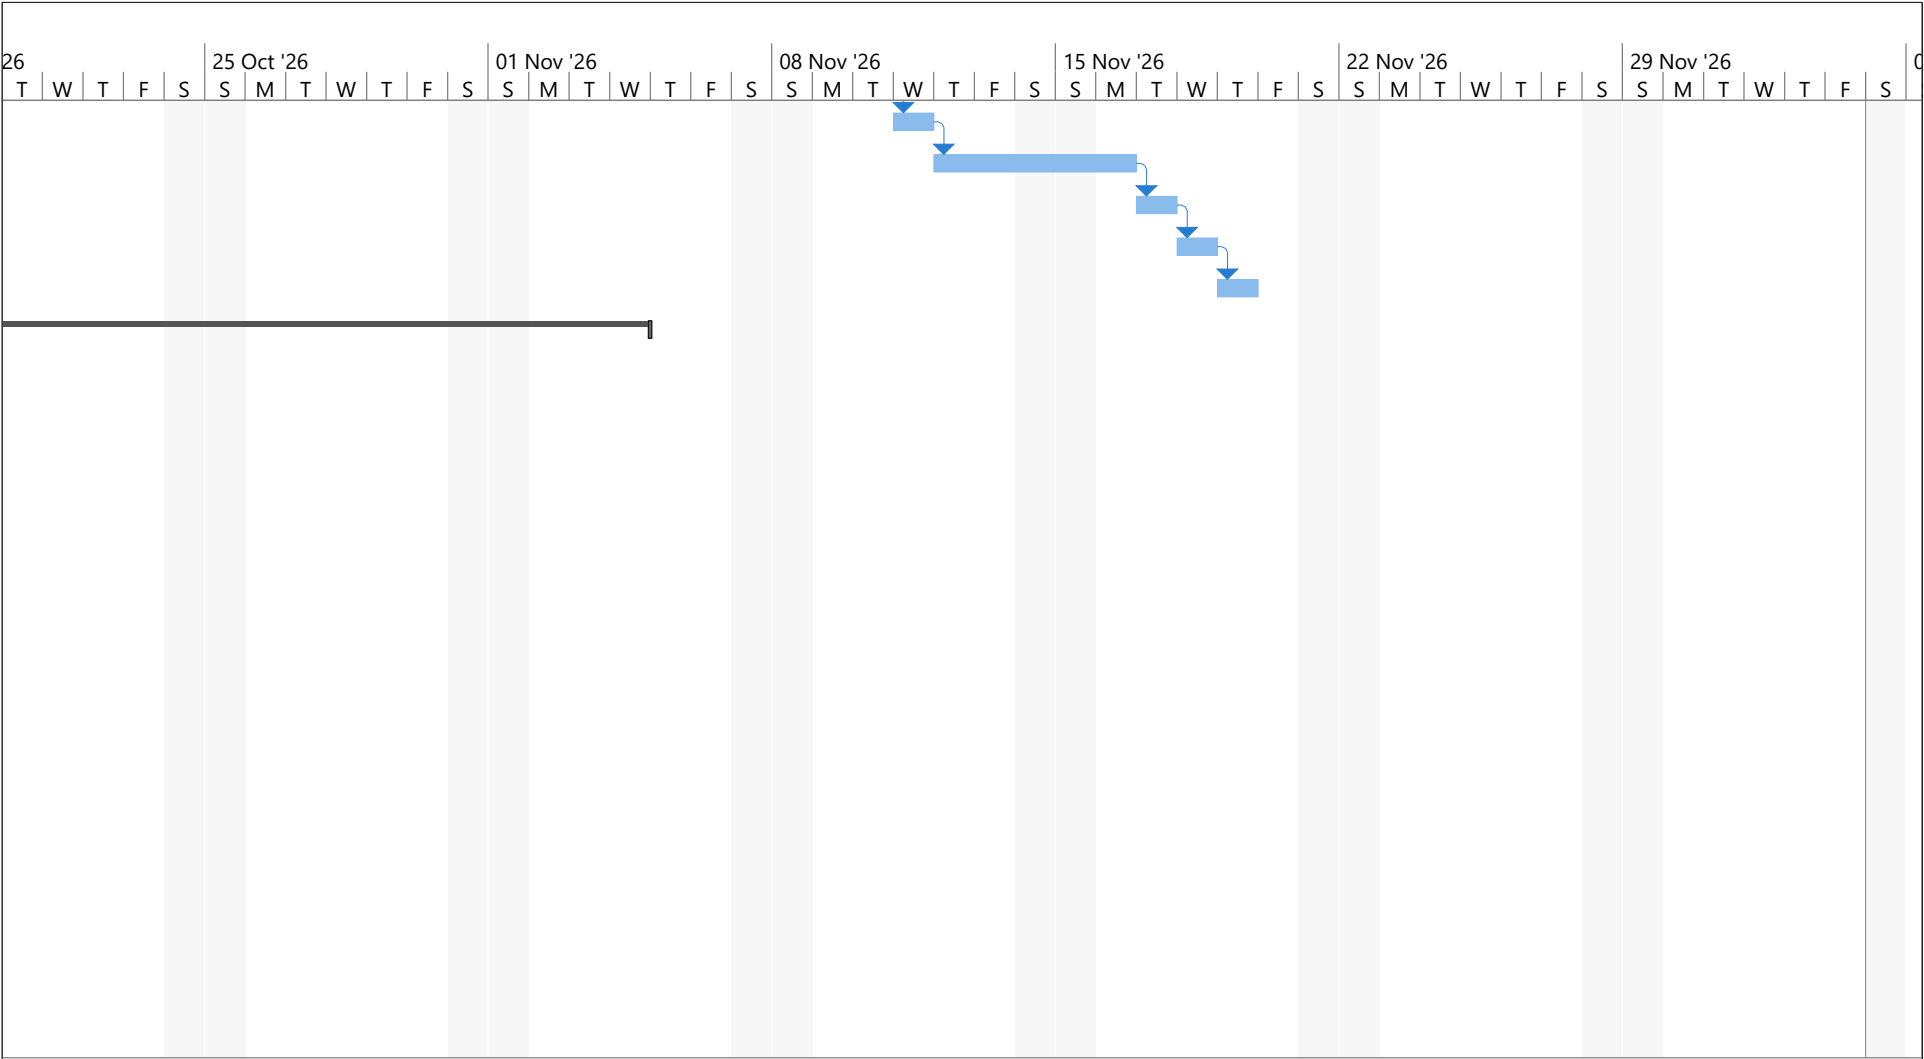

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

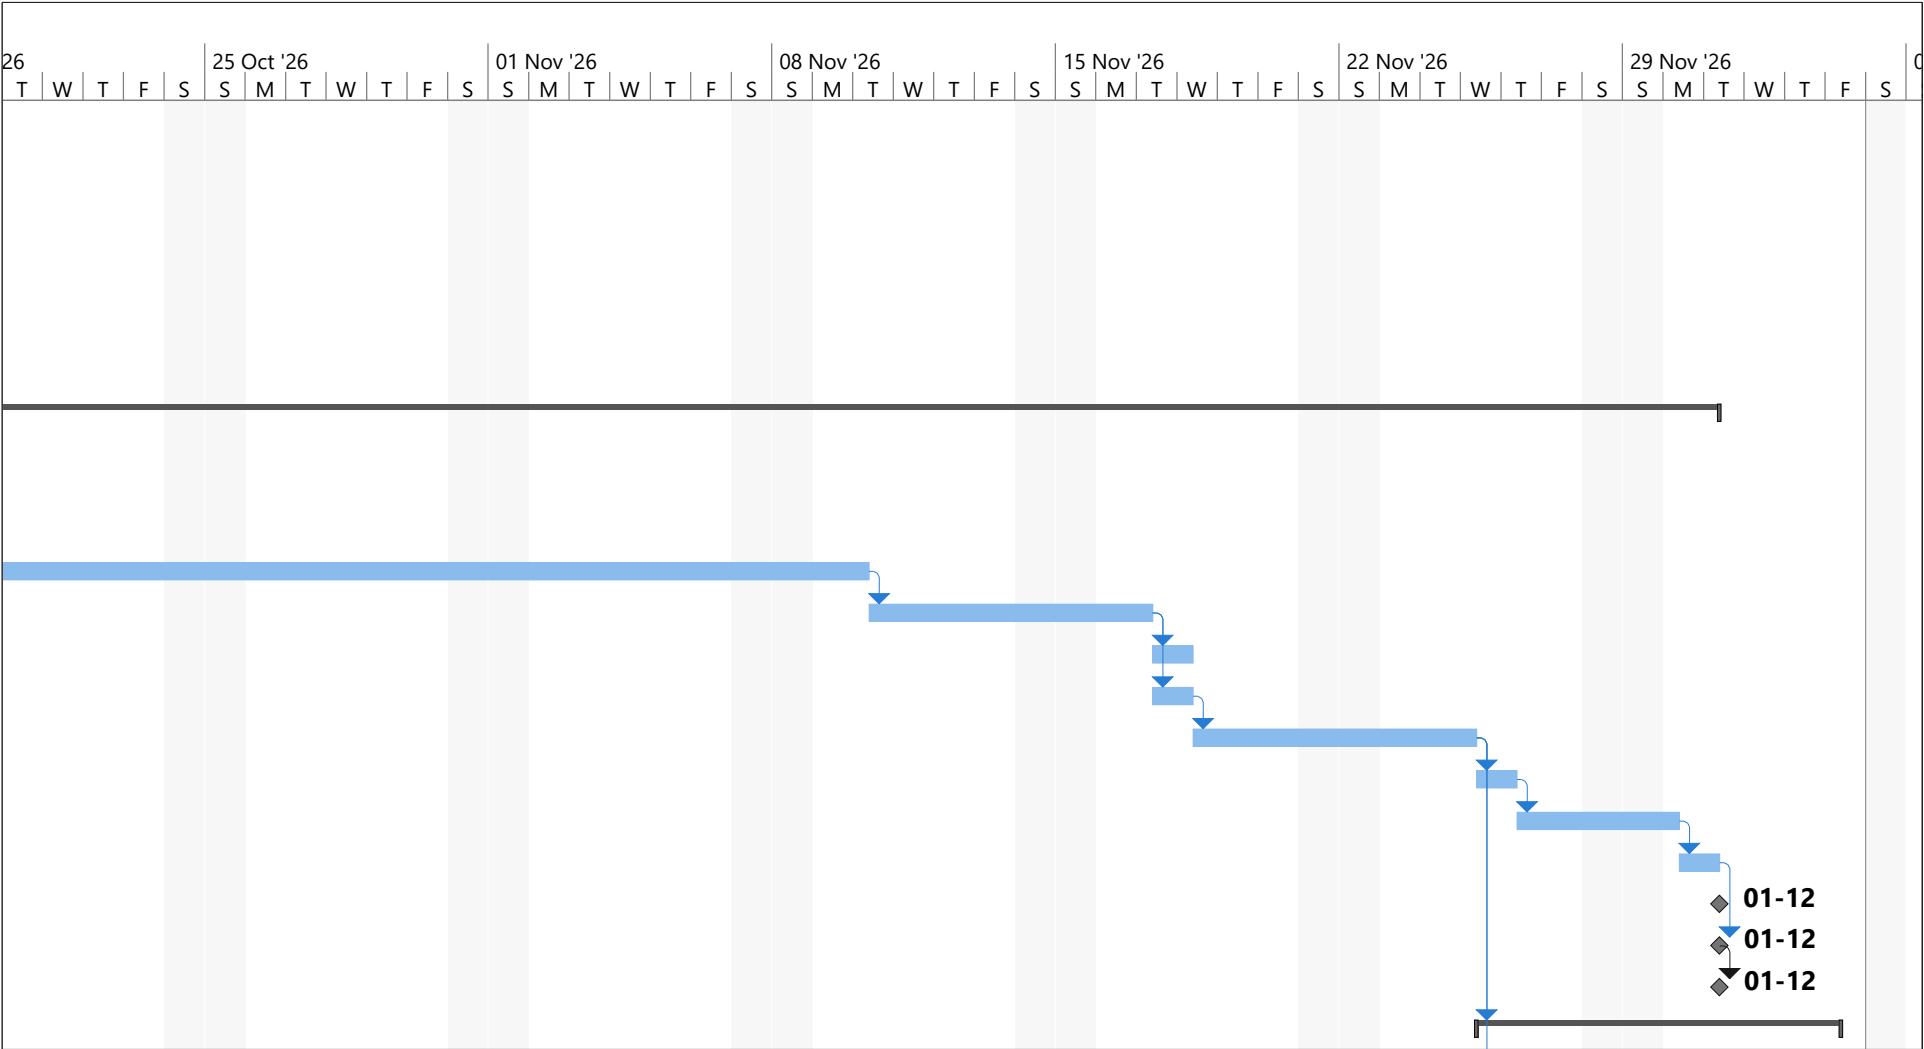

Project: msproj11 Date: Wed 30-09-26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

